
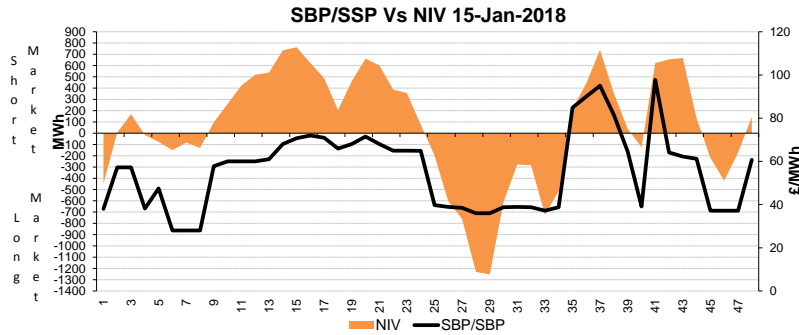
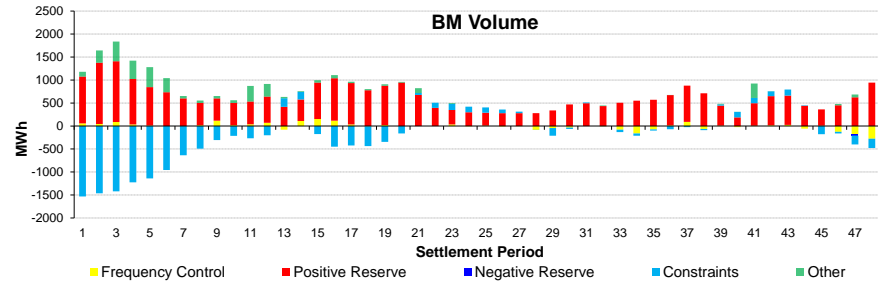
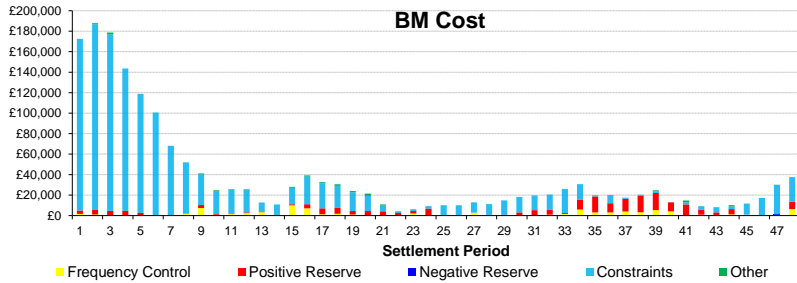



# Daily Balancing Costs

Date:

15/01/2018

**BSUoS Charge Estimate: £2.21/MWh**  
**Total Outturn: £3.38m**



## Commentary

771 MW of Stor was run in the early morning. There were many machines held for regulating reserve (margin) for the darkness peak for high demand that did not materialise, we therefore suspect there was about 2000MW of customer demand management.

The interconnectors were brought down for ROCOF in the early hours and actions taken in the Humber area. Voltage control plant was bought on in the Midlands, South Wales and Lincoln area. Many wind farms were bid off in Scotland to reduce overloading the Scotland/England borders.
