

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar				
							September	October	November	D	
1		EU CODES IMPLEMENTATION PLAN									
2		REQUIREMENTS FOR GENERATORS									
3		CODE DEVELOPMENT	285 days	Mon 01/12/14	Mon 04/01/16						
4		Comitology Process	86 days	Mon 01/12/14	Mon 30/03/15						
5		Entry Into Force	0 days	Mon 04/01/16	Mon 04/01/16						
6		CODE IMPLEMENTATION	261 days	Tue 03/01/17	Wed 03/01/18						
7		GB Alignment	0 days	Wed 04/01/17	Wed 04/01/17	5FS+263 c					
8		Contracts let captured by new requirements	0 days	Wed 03/01/18	Wed 03/01/18	5FS+523 c					
9		Compliance required (1 year window)	0 days	Tue 03/01/17	Tue 03/01/17	5FS+262 c					
10		GB CODE MODIFICATION PROCESS	397 days	Fri 10/10/14	Mon 18/04/16						
11		Code Mapping	7 days	Mon 20/07/15	Tue 28/07/15						
12		Code Mapping Workshop	2 days	Mon 20/07/15	Tue 21/07/15						
13		Code Mapping Outputs captured	5 days	Wed 22/07/15	Tue 28/07/15	12					
14		Definitions	73 days	Fri 20/03/15	Tue 30/06/15						
15		Definitions mapping exercise completed between RfG, Grid Code and Distribution Code	11 days	Fri 20/03/15	Fri 03/04/15						
16		Proposal on how to align Definitions drafted	7 days	Mon 06/04/15	Tue 14/04/15	15					
17		Proposal for Alignment of Definitions discussed by RfG Workgroup	1 day	Tue 21/04/15	Tue 21/04/15						
18		Proposal redrafted	39 days	Wed 22/04/15	Mon 15/06/15	17					
19		Alignment of Definitions agreed by RfG Workgroup	1 day	Tue 16/06/15	Tue 16/06/15						
20		Proposal for Alignment of Definitions discussed by ENC Implementation Steering Group	1 day	Mon 29/06/15	Mon 29/06/15						

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Month			
							September	October	November	D
21		Alignment of Definitions agreed	1 day	Tue 30/06/15	Tue 30/06/15	20				
22		Modification Timeline One: Mod 1 Banding and Structural and Mod 2 Compliance Processes	345 days	Mon 15/12/14	Fri 08/04/16					
23		Mod 1 : Banding Threshold Workgroup Consultation	262 days	Thu 19/02/15	Fri 19/02/16					
24		Workgroup Consultation	153 days	Thu 19/02/15	Mon 21/09/15					
25		Cost Benefit Analysis completed for System Operator Costs	93 days	Thu 19/02/15	Mon 29/06/15					
26		Cost Benefit Analysis completed for Generator Costs	93 days	Thu 19/02/15	Mon 29/06/15					
27		Conclusions and Recommendations finalised	9 days	Tue 30/06/15	Fri 10/07/15					
28		Draft Workgroup Report circulated to RfG Workgroup members	1 day	Mon 13/07/15	Mon 13/07/15	27				
29		Draft Workgroup Report discussed at RfG Workgroup	1 day	Mon 20/07/15	Mon 20/07/15	28FS+4 days				
30		Workgroup Report finalised	5 days	Tue 21/07/15	Mon 27/07/15	29				
31		Workgroup Report circulated to GCRP members	1 day	Wed 09/09/15	Wed 09/09/15					
32		Workgroup Report discussed at GCRP and Industry Consultation recommended	1 day	Wed 16/09/15	Wed 16/09/15					
33		Workgroup Report revised based on GCRP feedback	3 days	Thu 17/09/15	Mon 21/09/15	32				
34		Governance Approval	7 days	Mon 21/09/15	Tue 29/09/15					
35		Consultation discussed at JESG	1 day	Tue 29/09/15	Tue 29/09/15					

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
36		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 21/09/15	Mon 21/09/15					
37		Industry Consultation	43 days	Mon 21/09/15	Thu 19/11/15					
38		Industry Consultation Document published externally	0 days	Mon 21/09/15	Mon 21/09/15	33				
39		Consultation period (20 business days)	20 days	Tue 22/09/15	Mon 19/10/15	38				
40		Consultation redrafted with industry comments	17 days	Tue 20/10/15	Wed 11/11/15	39				
41		Revised Consultation circulated to RfG Workgroup	1 day	Thu 12/11/15	Thu 12/11/15					
42		Revised Consultation presented at RfG Workgroup	1 day	Thu 19/11/15	Thu 19/11/15					
43		Report to the Authority (after Entry Into Force)	10 days	Mon 04/01/16	Fri 15/01/16					
44		Compilation of Report to Authority (10 business days)	10 days	Mon 04/01/16	Fri 15/01/16	5				
45		Report to Authority published externally	0 days	Fri 15/01/16	Fri 15/01/16	44				
46		Report to Authority submitted to Ofgem	0 days	Fri 15/01/16	Fri 15/01/16	44				
47		Modification Approval	25 days	Mon 18/01/16	Fri 19/02/16					
48		Ofgem Consideration (25 business days)	25 days	Mon 18/01/16	Fri 19/02/16	46				
49		Potential Ofgem decision	0 days	Fri 19/02/16	Fri 19/02/16	48				
50		Mod 2 : Compliance	345 days	Mon 15/12/14	Fri 08/04/16					
51		Comparison between GB Code and RfG draft	45 days	Wed 29/07/15	Tue 29/09/15	13				
52		Proposed adjustments to GB Code identified	20 days	Wed 30/09/15	Tue 27/10/15	51				
53		Workgroup Report drafted	6 days	Wed 28/10/15	Wed 04/11/15	52,21				
54		Workgroup Report discussed at RfG Workgroup	1 day	Thu 12/11/15	Thu 12/11/15	53FS+5 da				
55		Workgroup Report discussed at GCRP	1 day	Wed 18/11/15	Wed 18/11/15					
56		GCRP recommend Industry Consultation	0 days	Wed 18/11/15	Wed 18/11/15	55				

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
57		Distribution Code - Stage 1	120 days	Mon 15/12/14	Fri 29/05/15					
68		Distribution Code - Stage 2	153 days	Mon 02/03/15	Wed 30/09/15					
78		Governance Approval	9 days	Wed 02/12/15	Mon 14/12/15					
79		Consultation discussed at JESG	1 day	Wed 02/12/15	Wed 02/12/15					
80		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 14/12/15	Mon 14/12/15					
81		Industry Consultation	38 days	Tue 15/12/15	Thu 04/02/16					
82		Industry Consultation drafted	18 days	Tue 15/12/15	Thu 07/01/16	80				
83		Industry Consultation Document published externally	0 days	Thu 07/01/16	Thu 07/01/16	82				
84		Consultation period (20 business days)	20 days	Fri 08/01/16	Thu 04/02/16	83				
85		Report to the Authority	10 days	Mon 22/02/16	Fri 04/03/16					
86		Compilation of Report to Authority (10 business days)	10 days	Mon 22/02/16	Fri 04/03/16	48				
87		Report to Authority published externally	0 days	Fri 04/03/16	Fri 04/03/16	86				
88		Report to Authority submitted to Ofgem	0 days	Fri 04/03/16	Fri 04/03/16	86				
89		Modification Approval	25 days	Mon 07/03/16	Fri 08/04/16					
90		Ofgem Consideration (25 business days)	25 days	Mon 07/03/16	Fri 08/04/16	88				
91		Potential Ofgem decision	0 days	Fri 08/04/16	Fri 08/04/16	90				
92		Modification Time Line Two : Mod 3 General, Mod 4 Fault Ride Through, Mod 5 Voltage and Reactive Power and Mod 6 Frequency	220 days	Fri 10/10/14	Thu 13/08/15					
93		Mod 3 : General	220 days	Tue 16/06/15	Mon 18/04/16					
94		Grid Code	98 days	Thu 02/07/15	Mon 16/11/15					

Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
95		Workgroup Report drafted	69 days	Thu 02/07/15	Tue 06/10/15					
96		Workgroup Report discussed at RfG Workgroup	0 days	Tue 13/10/15	Tue 13/10/15					
97		Workgroup Report revised	15 days	Tue 13/10/15	Mon 02/11/15	96				
98		Workgroup Report agreed by Workgroup members	0 days	Tue 10/11/15	Tue 10/11/15					
99		Workgroup Report discussed at GCRP	1 day	Mon 16/11/15	Mon 16/11/15					
100		GCRP recommend Industry Consultation	0 days	Mon 16/11/15	Mon 16/11/15					
101		Distribution Code - Stage 3	119 days	Tue 16/06/15	Fri 27/11/15					
111		Governance Approval	9 days	Wed 02/12/15	Mon 14/12/15					
112		Consultation discussed at JESG	1 day	Wed 02/12/15	Wed 02/12/15					
113		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 14/12/15	Mon 14/12/15					
114		Industry Consultation	55 days	Tue 15/12/15	Mon 29/02/16	94,101				
115		Industry Consultation drafted	10 days	Tue 15/12/15	Mon 28/12/15	113				
116		Industry Consultation Document published externally (after Christmas break)	0 days	Tue 05/01/16	Tue 05/01/16					
117		Consultation Period	30 days	Tue 05/01/16	Mon 15/02/16	116				
118		Consultation responses considered	10 days	Tue 16/02/16	Mon 29/02/16	117				
119		Report to the Authority	10 days	Tue 01/03/16	Mon 14/03/16	114				
120		Compilation of Report to Authority (10 business days)	10 days	Tue 01/03/16	Mon 14/03/16	118				
121		Report to Authority published externally	0 days	Mon 14/03/16	Mon 14/03/16	120				
122		Report to Authority submitted to Ofgem	0 days	Mon 14/03/16	Mon 14/03/16	120				
123		Modification Approval	25 days	Tue 15/03/16	Mon 18/04/16	119				
124		Ofgem Consideration (25 business days)	25 days	Tue 15/03/16	Mon 18/04/16	122				

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar			
							September	October	November	D
125		Potential Ofgem decision	0 days	Mon 18/04/16	Mon 18/04/16	124				
126		Mod 4 : Fault Ride Through	220 days	Tue 16/06/15	Mon 18/04/16					
127		Grid Code	98 days	Thu 02/07/15	Mon 16/11/15					
128		Workgroup Report drafted	69 days	Thu 02/07/15	Tue 06/10/15					
129		Workgroup Report discussed at RfG Workgroup	0 days	Tue 13/10/15	Tue 13/10/15					
130		Workgroup Report revised	15 days	Tue 13/10/15	Mon 02/11/15	129				
131		Workgroup Report agreed by Workgroup members	0 days	Tue 10/11/15	Tue 10/11/15					
132		Workgroup Report discussed at GCRP	1 day	Mon 16/11/15	Mon 16/11/15					
133		GCRP recommend Industry Consultation	0 days	Mon 16/11/15	Mon 16/11/15					
134		Distribution Code - Stage 3	119 days	Tue 16/06/15	Fri 27/11/15					
144		Governance Approval	9 days	Wed 02/12/15	Mon 14/12/15					
145		Consultation discussed at JESG	1 day	Wed 02/12/15	Wed 02/12/15					
146		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 14/12/15	Mon 14/12/15					
147		Industry Consultation	55 days	Tue 15/12/15	Mon 29/02/16	127,134				
148		Industry Consultation drafted	10 days	Tue 15/12/15	Mon 28/12/15	146				
149		Industry Consultation Document published externally (after Christmas break)	0 days	Tue 05/01/16	Tue 05/01/16					
150		Consultation Period	30 days	Tue 05/01/16	Mon 15/02/16	149				
151		Consultation responses considered	10 days	Tue 16/02/16	Mon 29/02/16	150				
152		Report to the Authority	10 days	Tue 01/03/16	Mon 14/03/16	147				
153		Compilation of Report to Authority (10 business days)	10 days	Tue 01/03/16	Mon 14/03/16	151				
154		Report to Authority published externally	0 days	Mon 14/03/16	Mon 14/03/16	153				

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
155		Report to Authority submitted to Ofgem	0 days	Mon 14/03/16	Mon 14/03/16	153				
156		Modification Approval	25 days	Tue 15/03/16	Mon 18/04/16	152				
157		Ofgem Consideration (25 business days)	25 days	Tue 15/03/16	Mon 18/04/16	155				
158		Potential Ofgem decision	0 days	Mon 18/04/16	Mon 18/04/16	157				
159		Mod 5 : Voltage	220 days	Tue 16/06/15	Mon 18/04/16					
160		Grid Code	98 days	Thu 02/07/15	Mon 16/11/15					
161		Workgroup Report drafted	69 days	Thu 02/07/15	Tue 06/10/15					
162		Workgroup Report discussed at RfG Workgroup	0 days	Tue 13/10/15	Tue 13/10/15					
163		Workgroup Report revised	15 days	Tue 13/10/15	Mon 02/11/15	162				
164		Workgroup Report agreed by Workgroup members	0 days	Tue 10/11/15	Tue 10/11/15					
165		Workgroup Report discussed at GCRP	1 day	Mon 16/11/15	Mon 16/11/15					
166		GCRP recommend Industry Consultation	0 days	Mon 16/11/15	Mon 16/11/15					
167		Distribution Code - Stage 3	119 days	Tue 16/06/15	Fri 27/11/15					
177		Governance Approval	9 days	Wed 02/12/15	Mon 14/12/15					
178		Consultation discussed at JESG	1 day	Wed 02/12/15	Wed 02/12/15					
179		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 14/12/15	Mon 14/12/15					
180		Industry Consultation	55 days	Tue 15/12/15	Mon 29/02/16	160,167				
181		Industry Consultation drafted	10 days	Tue 15/12/15	Mon 28/12/15	179				
182		Industry Consultation Document published externally (after Christmas break)	0 days	Tue 05/01/16	Tue 05/01/16					
183		Consultation Period	30 days	Tue 05/01/16	Mon 15/02/16	182				
184		Consultation responses considered	10 days	Tue 16/02/16	Mon 29/02/16	183				
185		Report to the Authority	10 days	Tue 01/03/16	Mon 14/03/16	180				

Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor				
							September	October	November	D
186		Compilation of Report to Authority (10 business days)	10 days	Tue 01/03/16	Mon 14/03/16	184				
187		Report to Authority published externally	0 days	Mon 14/03/16	Mon 14/03/16	186				
188		Report to Authority submitted to Ofgem	0 days	Mon 14/03/16	Mon 14/03/16	186				
189		Modification Approval	25 days	Tue 15/03/16	Mon 18/04/16	185				
190		Ofgem Consideration (25 business days)	25 days	Tue 15/03/16	Mon 18/04/16	188				
191		Potential Ofgem decision	0 days	Mon 18/04/16	Mon 18/04/16	190				
192		Mod 6 : Frequency	220 days	Tue 16/06/15	Mon 18/04/16					
193		Grid Code	98 days	Thu 02/07/15	Mon 16/11/15					
194		Workgroup Report drafted	69 days	Thu 02/07/15	Tue 06/10/15					
195		Workgroup Report discussed at RfG Workgroup	0 days	Tue 13/10/15	Tue 13/10/15					
196		Workgroup Report revised	15 days	Tue 13/10/15	Mon 02/11/15	195				
197		Workgroup Report agreed by Workgroup members	0 days	Tue 10/11/15	Tue 10/11/15					
198		Workgroup Report discussed at GCRP	1 day	Mon 16/11/15	Mon 16/11/15					
199		GCRP recommend Industry Consultation	0 days	Mon 16/11/15	Mon 16/11/15					
200		Distribution Code - Stage 3	119 days	Tue 16/06/15	Fri 27/11/15					
210		Governance Approval	9 days	Wed 02/12/15	Mon 14/12/15					
211		Consultation discussed at JESG	1 day	Wed 02/12/15	Wed 02/12/15					
212		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 14/12/15	Mon 14/12/15					
213		Industry Consultation	55 days	Tue 15/12/15	Mon 29/02/16	193,200				
214		Industry Consultation drafted	10 days	Tue 15/12/15	Mon 28/12/15	212				
215		Industry Consultation Document published externally (after Christmas break)	0 days	Tue 05/01/16	Tue 05/01/16					

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
216		Consultation Period	30 days	Tue 05/01/16	Mon 15/02/16	215				
217		Consultation responses considered	10 days	Tue 16/02/16	Mon 29/02/16	216				
218		Report to the Authority	10 days	Tue 01/03/16	Mon 14/03/16	213				
219		Compilation of Report to Authority (10 business days)	10 days	Tue 01/03/16	Mon 14/03/16	217				
220		Report to Authority published externally	0 days	Mon 14/03/16	Mon 14/03/16	219				
221		Report to Authority submitted to Ofgem	0 days	Mon 14/03/16	Mon 14/03/16	219				
222		Modification Approval	25 days	Tue 15/03/16	Mon 18/04/16	218				
223		Ofgem Consideration (25 business days)	25 days	Tue 15/03/16	Mon 18/04/16	221				
224		Potential Ofgem decision	0 days	Mon 18/04/16	Mon 18/04/16	223				
225		Consideration of impact on Demand Connection and HVDC Codes	133 days	Tue 30/06/15	Thu 31/12/15					
226		Licence and Legislative changes	130 days	Mon 04/01/16	Fri 01/07/16	5				
227		Post Implementation	0 days	Fri 01/12/17	Fri 01/12/17					
229		GB Engagement	120 days	Thu 18/06/15	Wed 02/12/15					
237		DEMAND CONNECTION CODE	374 days?	Mon 02/11/15	Thu 06/04/17					
238		Entry Into Force	0 days	Tue 01/12/15	Tue 01/12/15					
239		Grid Code	182 days?	Mon 02/11/15	Tue 12/07/16					
240		Mod : 1	182 days?	Mon 02/11/15	Tue 12/07/16					
241		Workgroup Report drafted	86.25 days	Mon 02/11/15	Tue 01/03/16					
242		Workgroup Report discussed at RfG Workgroup	0 days	Tue 08/03/16	Tue 08/03/16	241FS+5 c				
243		Workgroup Report revised	15 days	Tue 08/03/16	Tue 29/03/16	242				
244		Workgroup Report discussed by Workgroup members	0 days	Tue 05/04/16	Tue 05/04/16	243FS+5 c				
245		Workgroup Report discussed at GCRP	1 day	Wed 20/01/16	Wed 20/01/16					

Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor				
							September	October	November	D
246		Workgroup Report agreed by Workgroup members	1 day	Wed 17/02/16	Wed 17/02/16					
247		Workgroup Report discussed at GCRP	1 day	Wed 16/03/16	Wed 16/03/16					
248		GCRP recommend Industry Consultation	0 days	Thu 17/03/16	Thu 17/03/16	247				
249		Distribution Code								
250		Governance Approval	9 days	Mon 21/03/16	Thu 31/03/16					
251		Consultation discussed at JESG	1 day	Mon 28/03/16	Mon 28/03/16					
252		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 28/03/16	Mon 28/03/16					
253		Industry Consultation	41 days	Thu 17/03/16	Thu 12/05/16					
254		Industry Consultation drafted	10 days	Thu 17/03/16	Wed 30/03/16	248				
255		Industry Consultation Document published external	0 days	Thu 31/03/16	Thu 31/03/16	254				
256		Consultation period (20 business days)	20 days	Fri 01/04/16	Thu 28/04/16	255				
257		Consultation responses considered	10 days	Fri 29/04/16	Thu 12/05/16	256				
258		Report to the Authority	10 days	Wed 25/05/16	Tue 07/06/16					
259		Compilation of Report to Authority (5 business days)	10 days	Wed 25/05/16	Tue 07/06/16	257				
260		Report to Authority published externally	0 days	Tue 07/06/16	Tue 07/06/16	259				
261		Report to Authority submitted to Ofgem	0 days	Tue 07/06/16	Tue 07/06/16	259				
262		Modification Approval	25 days	Wed 08/06/16	Tue 12/07/16					
263		Ofgem Consideration (25 business days)	25 days	Wed 08/06/16	Tue 12/07/16	261				
264		Potential Ofgem decision	0 days	Tue 12/07/16	Tue 12/07/16	263				
265		Mod : 2	182 days?	Mon 02/11/15	Tue 12/07/16					
266		Workgroup Report drafted	86.25 days	Mon 02/11/15	Tue 01/03/16					
267		Workgroup Report discussed at RfG Workgroup	0 days	Tue 08/03/16	Tue 08/03/16	266FS+5 c				

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor				
							September	October	November	D
268		Workgroup Report revised	15 days	Tue 08/03/16	Tue 29/03/16	267				
269		Workgroup Report discussed by Workgroup members	0 days	Tue 05/04/16	Tue 05/04/16	268FS+5 c				
270		Workgroup Report discussed at GCRP	1 day	Wed 20/01/16	Wed 20/01/16					
271		Workgroup Report agreed by Workgroup members	1 day	Wed 17/02/16	Wed 17/02/16					
272		Workgroup Report discussed at GCRP	1 day	Wed 16/03/16	Wed 16/03/16					
273		GCRP recommend Industry Consultation	0 days	Thu 17/03/16	Thu 17/03/16	272				
274		Distribution Code								
275		Governance Approval	9 days	Mon 21/03/16	Thu 31/03/16					
276		Consultation discussed at JESG	1 day	Mon 28/03/16	Mon 28/03/16					
277		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 28/03/16	Mon 28/03/16					
278		Industry Consultation	41 days	Thu 17/03/16	Thu 12/05/16					
279		Industry Consultation drafted	10 days	Thu 17/03/16	Wed 30/03/16	273				
280		Industry Consultation Document published external	0 days	Thu 31/03/16	Thu 31/03/16	279				
281		Consultation period (20 business days)	20 days	Fri 01/04/16	Thu 28/04/16	280				
282		Consultation responses considered	10 days	Fri 29/04/16	Thu 12/05/16	281				
283		Report to the Authority	10 days	Wed 25/05/16	Tue 07/06/16					
284		Compilation of Report to Authority (5 business days)	10 days	Wed 25/05/16	Tue 07/06/16	282				
285		Report to Authority published externally	0 days	Tue 07/06/16	Tue 07/06/16	284				
286		Report to Authority submitted to Ofgem	0 days	Tue 07/06/16	Tue 07/06/16	284				
287		Modification Approval	25 days	Wed 08/06/16	Tue 12/07/16					
288		Ofgem Consideration (25 business days)	25 days	Wed 08/06/16	Tue 12/07/16	286				
289		Potential Ofgem decision	0 days	Tue 12/07/16	Tue 12/07/16	288				

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
290		Mod : 3	182 days?	Mon 02/11/15	Tue 12/07/16					
291		Workgroup Report drafted	86.25 days	Mon 02/11/15	Tue 01/03/16					
292		Workgroup Report discussed at RfG Workgroup	0 days	Tue 08/03/16	Tue 08/03/16	291	FS+5 c			
293		Workgroup Report revised	15 days	Tue 08/03/16	Tue 29/03/16	292				
294		Workgroup Report discussed by Workgroup members	0 days	Tue 05/04/16	Tue 05/04/16	293	FS+5 c			
295		Workgroup Report discussed at GCRP	1 day	Wed 20/01/16	Wed 20/01/16					
296		Workgroup Report agreed by Workgroup members	1 day	Wed 17/02/16	Wed 17/02/16					
297		Workgroup Report discussed at GCRP	1 day	Wed 16/03/16	Wed 16/03/16					
298		GCRP recommend Industry Consultation	0 days	Thu 17/03/16	Thu 17/03/16	297				
299		Distribution Code								
300		Governance Approval	9 days	Mon 21/03/16	Thu 31/03/16					
301		Consultation discussed at JESG	1 day	Mon 28/03/16	Mon 28/03/16					
302		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 28/03/16	Mon 28/03/16					
303		Industry Consultation	41 days	Thu 17/03/16	Thu 12/05/16					
304		Industry Consultation drafted	10 days	Thu 17/03/16	Wed 30/03/16	298				
305		Industry Consultation Document published external	0 days	Thu 31/03/16	Thu 31/03/16	304				
306		Consultation period (20 business days)	20 days	Fri 01/04/16	Thu 28/04/16	305				
307		Consultation responses considered	10 days	Fri 29/04/16	Thu 12/05/16	306				
308		Report to the Authority	10 days	Wed 25/05/16	Tue 07/06/16					
309		Compilation of Report to Authority (5 business days)	10 days	Wed 25/05/16	Tue 07/06/16	307				
310		Report to Authority published externally	0 days	Tue 07/06/16	Tue 07/06/16	309				
311		Report to Authority submitted to Ofgem	0 days	Tue 07/06/16	Tue 07/06/16	309				

Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
312		Modification Approval	25 days	Wed 08/06/16	Tue 12/07/16					
313		Ofgem Consideration (25 business days)	25 days	Wed 08/06/16	Tue 12/07/16	311				
314		Potential Ofgem decision	0 days	Tue 12/07/16	Tue 12/07/16	313				
315		HVDC	0 days	Wed 01/06/16	Wed 01/06/16					
317		Mod : 1	182 days	Mon 02/05/16	Wed 11/01/17					
318		Grid Code	116.25 days	Mon 02/05/16	Tue 11/10/16					
319		Workgroup report drafted	86.25 days	Mon 02/05/16	Tue 30/08/16					
320		Workgroup Report discussed at RfG Workgroup	1 day	Tue 06/09/16	Wed 07/09/16	319FS+5 c				
321		Workgroup Report revised	18 days	Wed 07/09/16	Mon 03/10/16	320				
322		Workgroup Report agreed by Workgroup members	1 day	Mon 10/10/16	Tue 11/10/16	321FS+5 c				
323		Workgroup Report discussed at GCRP	1 day	Wed 21/09/16	Wed 21/09/16					
324		GCRP recommend Industry Consultation	0 days	Thu 22/09/16	Thu 22/09/16	323				
325		Governance Approval	1 day	Mon 03/10/16	Mon 03/10/16					
326		Consultation discussed at JESG	1 day	Mon 03/10/16	Mon 03/10/16					
327		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 03/10/16	Mon 03/10/16					
328		Distribution Code								
329		Industry Consultation	49 days	Thu 22/09/16	Tue 29/11/16					
330		Industry Consultation drafted	10 days	Thu 22/09/16	Wed 05/10/16	324				
331		Industry Consultation Document published externally	1 day	Thu 06/10/16	Thu 06/10/16	330				
332		Consultation period (20 business days)	20 days	Fri 07/10/16	Thu 03/11/16	331				
333		Consultation responses considered	18 days	Fri 04/11/16	Tue 29/11/16	332				
334		Report to the Authority	5 days	Wed 30/11/16	Wed 07/12/16					

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
335		Compilation of Report to Authority (5 business days)	5 days	Wed 30/11/16	Tue 06/12/16	333				
336		Report to Authority published externally	0 days	Wed 07/12/16	Wed 07/12/16	335				
337		Report to Authority submitted to Ofgem	0 days	Wed 07/12/16	Wed 07/12/16	335				
338		Modification Approval	25 days	Wed 07/12/16	Wed 11/01/17					
339		Ofgem Consideration (25 business days)	25 days	Wed 07/12/16	Tue 10/01/17	337				
340		Potential Ofgem decision	0 days	Wed 11/01/17	Wed 11/01/17	339				
341		Mod : 2	182 days	Mon 02/05/16	Wed 11/01/17					
342		Entry Into Force	0 days	Wed 01/06/16	Wed 01/06/16					
343		Grid Code	116.25 days	Mon 02/05/16	Tue 11/10/16					
344		Workgroup report drafted	86.25 days	Mon 02/05/16	Tue 30/08/16					
345		Workgroup Report discussed at RfG Workgroup	1 day	Tue 06/09/16	Wed 07/09/16	344FS+5 c				
346		Workgroup Report revised	18 days	Wed 07/09/16	Mon 03/10/16	345				
347		Workgroup Report agreed by Workgroup members	1 day	Mon 10/10/16	Tue 11/10/16	346FS+5 c				
348		Workgroup Report discussed at GCRP	1 day	Wed 21/09/16	Wed 21/09/16					
349		GCRP recommend Industry Consultation	0 days	Thu 22/09/16	Thu 22/09/16	348				
350		Governance Approval	1 day	Mon 03/10/16	Mon 03/10/16					
351		Consultation discussed at JESG	1 day	Mon 03/10/16	Mon 03/10/16					
352		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 03/10/16	Mon 03/10/16					
353		Distribution Code								
354		Industry Consultation	49 days	Thu 22/09/16	Tue 29/11/16					
355		Industry Consultation drafted	10 days	Thu 22/09/16	Wed 05/10/16	349				
356		Industry Consultation Document published externally	1 day	Thu 06/10/16	Thu 06/10/16	355				

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Calendar			
							September	October	November	D
357		Consultation period (20 business days)	20 days	Fri 07/10/16	Thu 03/11/16	356				
358		Consultation responses considered	18 days	Fri 04/11/16	Tue 29/11/16	357				
359		Report to the Authority	5 days	Wed 30/11/16	Wed 07/12/16					
360		Compilation of Report to Authority (5 business days)	5 days	Wed 30/11/16	Tue 06/12/16	358				
361		Report to Authority published externally	0 days	Wed 07/12/16	Wed 07/12/16	360				
362		Report to Authority submitted to Ofgem	0 days	Wed 07/12/16	Wed 07/12/16	360				
363		Modification Approval	25 days	Wed 07/12/16	Wed 11/01/17					
364		Ofgem Consideration (25 business days)	25 days	Wed 07/12/16	Tue 10/01/17	362				
365		Potential Ofgem decision	0 days	Wed 11/01/17	Wed 11/01/17	364				
366		Mod : 3	182 days	Mon 02/05/16	Wed 11/01/17					
367		Entry Into Force	0 days	Wed 01/06/16	Wed 01/06/16					
368		Grid Code	116.25 days	Mon 02/05/16	Tue 11/10/16					
369		Workgroup report drafted	86.25 days	Mon 02/05/16	Tue 30/08/16					
370		Workgroup Report discussed at RfG Workgroup	1 day	Tue 06/09/16	Wed 07/09/16	369FS+5 c				
371		Workgroup Report revised	18 days	Wed 07/09/16	Mon 03/10/16	370				
372		Workgroup Report agreed by Workgroup members	1 day	Mon 10/10/16	Tue 11/10/16	371FS+5 c				
373		Workgroup Report discussed at GCRP	1 day	Wed 21/09/16	Wed 21/09/16					
374		GCRP recommend Industry Consultation	0 days	Thu 22/09/16	Thu 22/09/16	373				
375		Governance Approval	1 day	Mon 03/10/16	Mon 03/10/16					
376		Consultation discussed at JESG	1 day	Mon 03/10/16	Mon 03/10/16					
377		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 03/10/16	Mon 03/10/16					
378		Distribution Code								

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor				
							September	October	November	D
379		Industry Consultation	49 days	Thu 22/09/16	Tue 29/11/16					
380		Industry Consultation drafted	10 days	Thu 22/09/16	Wed 05/10/16	374				
381		Industry Consultation Document published externally	1 day	Thu 06/10/16	Thu 06/10/16	380				
382		Consultation period (20 business days)	20 days	Fri 07/10/16	Thu 03/11/16	381				
383		Consultation responses considered	18 days	Fri 04/11/16	Tue 29/11/16	382				
384		Report to the Authority	5 days	Wed 30/11/16	Wed 07/12/16					
385		Compilation of Report to Authority (5 business days)	5 days	Wed 30/11/16	Tue 06/12/16	383				
386		Report to Authority published externally	0 days	Wed 07/12/16	Wed 07/12/16	385				
387		Report to Authority submitted to Ofgem	0 days	Wed 07/12/16	Wed 07/12/16	385				
388		Modification Approval	25 days	Wed 07/12/16	Wed 11/01/17					
389		Ofgem Consideration (25 business days)	25 days	Wed 07/12/16	Tue 10/01/17	387				
390		Potential Ofgem decision	0 days	Wed 11/01/17	Wed 11/01/17	389				
391		Mod : 4	182 days	Mon 02/05/16	Wed 11/01/17					
392		Entry Into Force	0 days	Wed 01/06/16	Wed 01/06/16					
393		Grid Code	116.25 days	Mon 02/05/16	Tue 11/10/16					
394		Workgroup report drafted	86.25 days	Mon 02/05/16	Tue 30/08/16					
395		Workgroup Report discussed at RfG Workgroup	1 day	Tue 06/09/16	Wed 07/09/16	394FS+5 c				
396		Workgroup Report revised	18 days	Wed 07/09/16	Mon 03/10/16	395				
397		Workgroup Report agreed by Workgroup members	1 day	Mon 10/10/16	Tue 11/10/16	396FS+5 c				
398		Workgroup Report discussed at GCRP	1 day	Wed 21/09/16	Wed 21/09/16					
399		GCRP recommend Industry Consultation	0 days	Thu 22/09/16	Thu 22/09/16	398				
400		Governance Approval	1 day	Mon 03/10/16	Mon 03/10/16					
401		Consultation discussed at JESG	1 day	Mon 03/10/16	Mon 03/10/16					

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar			
							September	October	November	D
402		Consultation signoff by ENC Implementation Steering Group	1 day	Mon 03/10/16	Mon 03/10/16					
403		Distribution Code								
404		Industry Consultation	49 days	Thu 22/09/16	Tue 29/11/16					
405		Industry Consultation drafted	10 days	Thu 22/09/16	Wed 05/10/16	399				
406		Industry Consultation Document published externally	1 day	Thu 06/10/16	Thu 06/10/16	405				
407		Consultation period (20 business days)	20 days	Fri 07/10/16	Thu 03/11/16	406				
408		Consultation responses considered	18 days	Fri 04/11/16	Tue 29/11/16	407				
409		Report to the Authority	5 days	Wed 30/11/16	Wed 07/12/16					
410		Compilation of Report to Authority (5 business days)	5 days	Wed 30/11/16	Tue 06/12/16	408				
411		Report to Authority published externally	0 days	Wed 07/12/16	Wed 07/12/16	410				
412		Report to Authority submitted to Ofgem	0 days	Wed 07/12/16	Wed 07/12/16	410				
413		Modification Approval	25 days	Wed 07/12/16	Wed 11/01/17					
414		Ofgem Consideration (25 business days)	25 days	Wed 07/12/16	Tue 10/01/17	412				
415		Potential Ofgem decision	0 days	Wed 11/01/17	Wed 11/01/17	414				
416		GB ENGAGEMENT	606 days	Wed 19/11/14	Wed 15/03/17					
417		Grid Code Review Panel (GCRP)	605 days	Wed 19/11/14	Wed 15/03/17					
418		Grid Code Review Panel (GCRP) 1	0 days	Wed 19/11/14	Wed 19/11/14					
419		Grid Code Review Panel (GCRP) 2	0 days	Wed 21/01/15	Wed 21/01/15					
420		Grid Code Review Panel (GCRP) 3	0 days	Wed 18/03/15	Wed 18/03/15					
421		Grid Code Review Panel (GCRP) 4	0 days	Wed 20/05/15	Wed 20/05/15					
422		Grid Code Review Panel (GCRP) 5	0 days	Wed 15/07/15	Wed 15/07/15					
423		Grid Code Review Panel (GCRP) 6	0 days	Wed 16/09/15	Wed 16/09/15					

Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors				
							September	October	November	D
424		Grid Code Review Panel (GCRP) 7	0 days	Wed 18/11/15	Wed 18/11/15					
425		Grid Code Review Panel (GCRP) 8	0 days	Wed 20/01/16	Wed 20/01/16					
426		Grid Code Review Panel (GCRP) 9	0 days	Wed 16/03/16	Wed 16/03/16					
427		Grid Code Review Panel (GCRP) 10	0 days	Wed 18/05/16	Wed 18/05/16					
428		Grid Code Review Panel (GCRP) 11	0 days	Wed 20/07/16	Wed 20/07/16					
429		Grid Code Review Panel (GCRP) 12	0 days	Wed 21/09/16	Wed 21/09/16					
430		Grid Code Review Panel (GCRP) 13	0 days	Wed 16/11/16	Wed 16/11/16					
431		Grid Code Review Panel (GCRP) 14	0 days	Wed 18/01/17	Wed 18/01/17					
432		Grid Code Review Panel (GCRP) 15	0 days	Wed 15/03/17	Wed 15/03/17					
433		RfG Workgroup	280 days	Thu 20/11/14	Thu 17/12/15					
434		RfG workgroup	0 days	Thu 20/11/14	Thu 20/11/14					
435		RfG workgroup	0 days	Wed 17/12/14	Wed 17/12/14					
436		RfG workgroup	0 days	Tue 20/01/15	Tue 20/01/15					
437		RfG Workgroup	0 days	Tue 17/02/15	Tue 17/02/15					
438		RfG Workgroup	0 days	Thu 19/03/15	Thu 19/03/15					
439		RfG Workgroup	0 days	Tue 21/04/15	Tue 21/04/15					
440		RfG Workgroup	0 days	Tue 19/05/15	Tue 19/05/15					
441		RfG Workgroup	0 days	Tue 16/06/15	Tue 16/06/15					
442		RfG Workgroup	0 days	Mon 20/07/15	Mon 20/07/15					
443		RfG Workgroup	0 days	Tue 18/08/15	Tue 18/08/15					
444		RfG Workgroup	0 days	Fri 25/09/15	Fri 25/09/15					
445		RfG Workgroup	0 days	Wed 28/10/15	Wed 28/10/15					
446		RfG Workgroup	0 days	Thu 19/11/15	Thu 19/11/15					

Project: RfG
Date: Mon 11/05/15


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors				
							September	October	November	D
447		RfG Workgroup	0 days	Thu 17/12/15	Thu 17/12/15					
448		Provisional Distribution Code Review Panel (DCRP)	195 days	Thu 05/03/15	Thu 03/12/15					
449		DCRP	0 days	Thu 05/03/15	Thu 05/03/15					
450		DCRP	0 days	Fri 05/06/15	Fri 05/06/15					
451		DCRP	0 days	Thu 03/09/15	Thu 03/09/15					
452		DCRP	0 days	Thu 03/12/15	Thu 03/12/15					
453		ENC Implementation Steering Group	176 days	Mon 13/04/15	Mon 14/12/15					
454		ENC Implementation Steering Group	1 day	Mon 13/04/15	Mon 13/04/15					
455		ENC Implementation Steering Group	1 day	Tue 19/05/15	Tue 19/05/15					
456		ENC Implementation Steering Group	1 day	Mon 29/06/15	Mon 29/06/15					
457		ENC Implementation Steering Group	1 day	Mon 10/08/15	Mon 10/08/15					
458		ENC Implementation Steering Group	1 day	Mon 21/09/15	Mon 21/09/15					
459		ENC Implementation Steering Group	1 day	Mon 02/11/15	Mon 02/11/15					
460		ENC Implementation Steering Group	1 day	Mon 14/12/15	Mon 14/12/15					
461		Joint European Stakeholder Group	140 days	Thu 21/05/15	Wed 02/12/15					
462		JESG	1 day	Thu 21/05/15	Thu 21/05/15					
463		JESG	1 day	Thu 18/06/15	Thu 18/06/15					
464		JESG	1 day	Wed 29/07/15	Wed 29/07/15					
465		JESG	1 day	Wed 26/08/15	Wed 26/08/15					
466		JESG	1 day	Tue 29/09/15	Tue 29/09/15					
467		JESG	1 day	Tue 20/10/15	Tue 20/10/15					
468		JESG	1 day	Tue 17/11/15	Tue 17/11/15					
469		JESG	1 day	Wed 02/12/15	Wed 02/12/15					


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

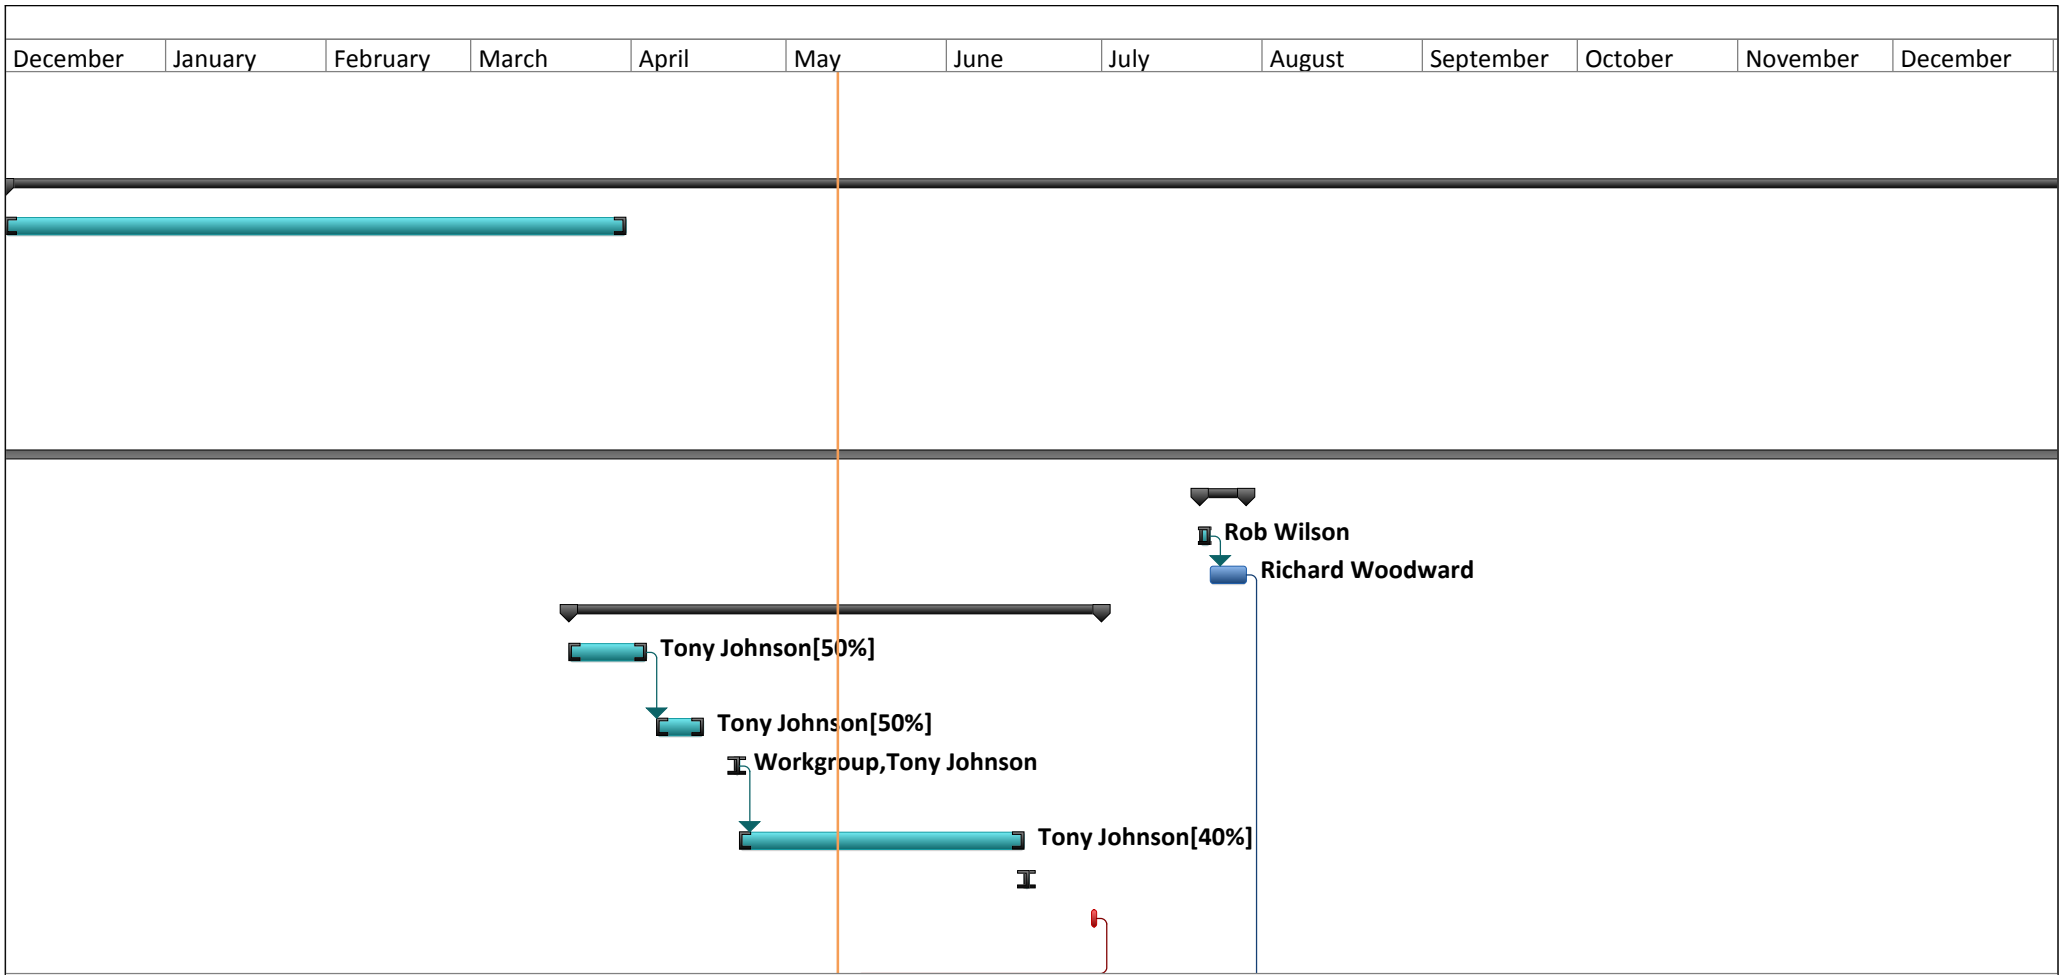


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

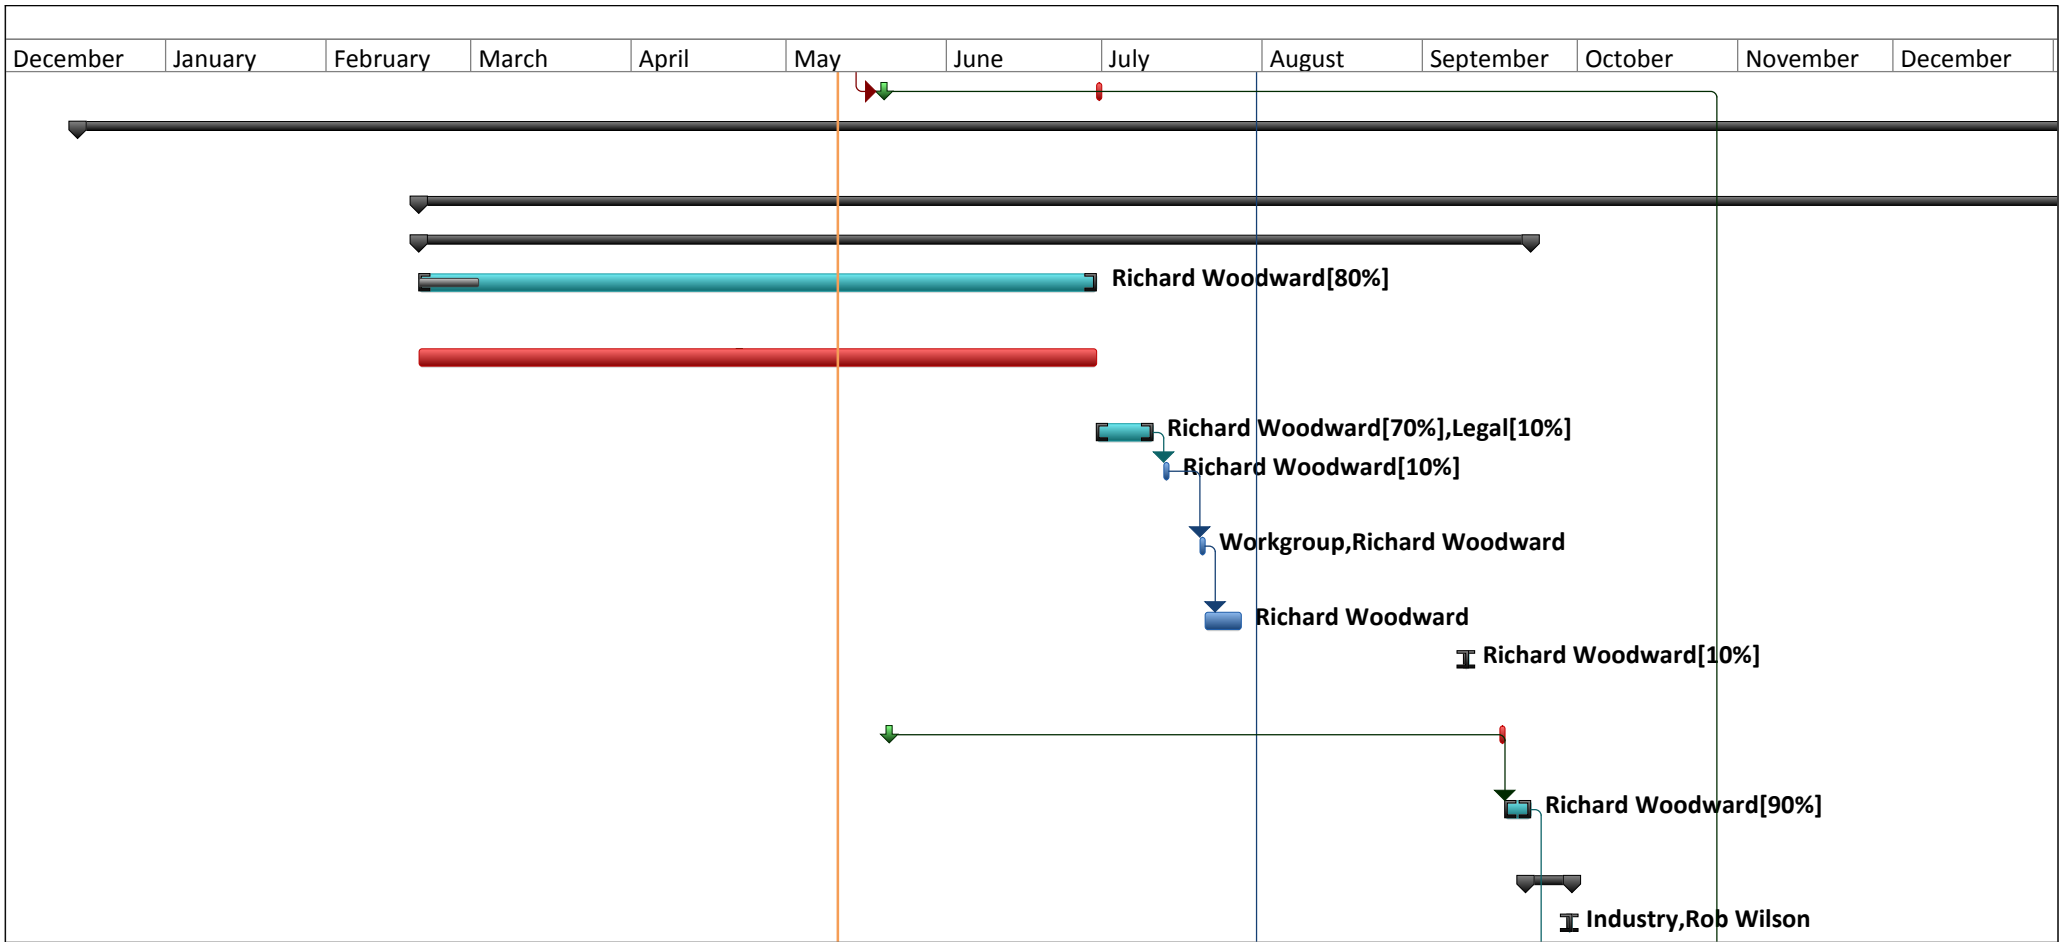

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

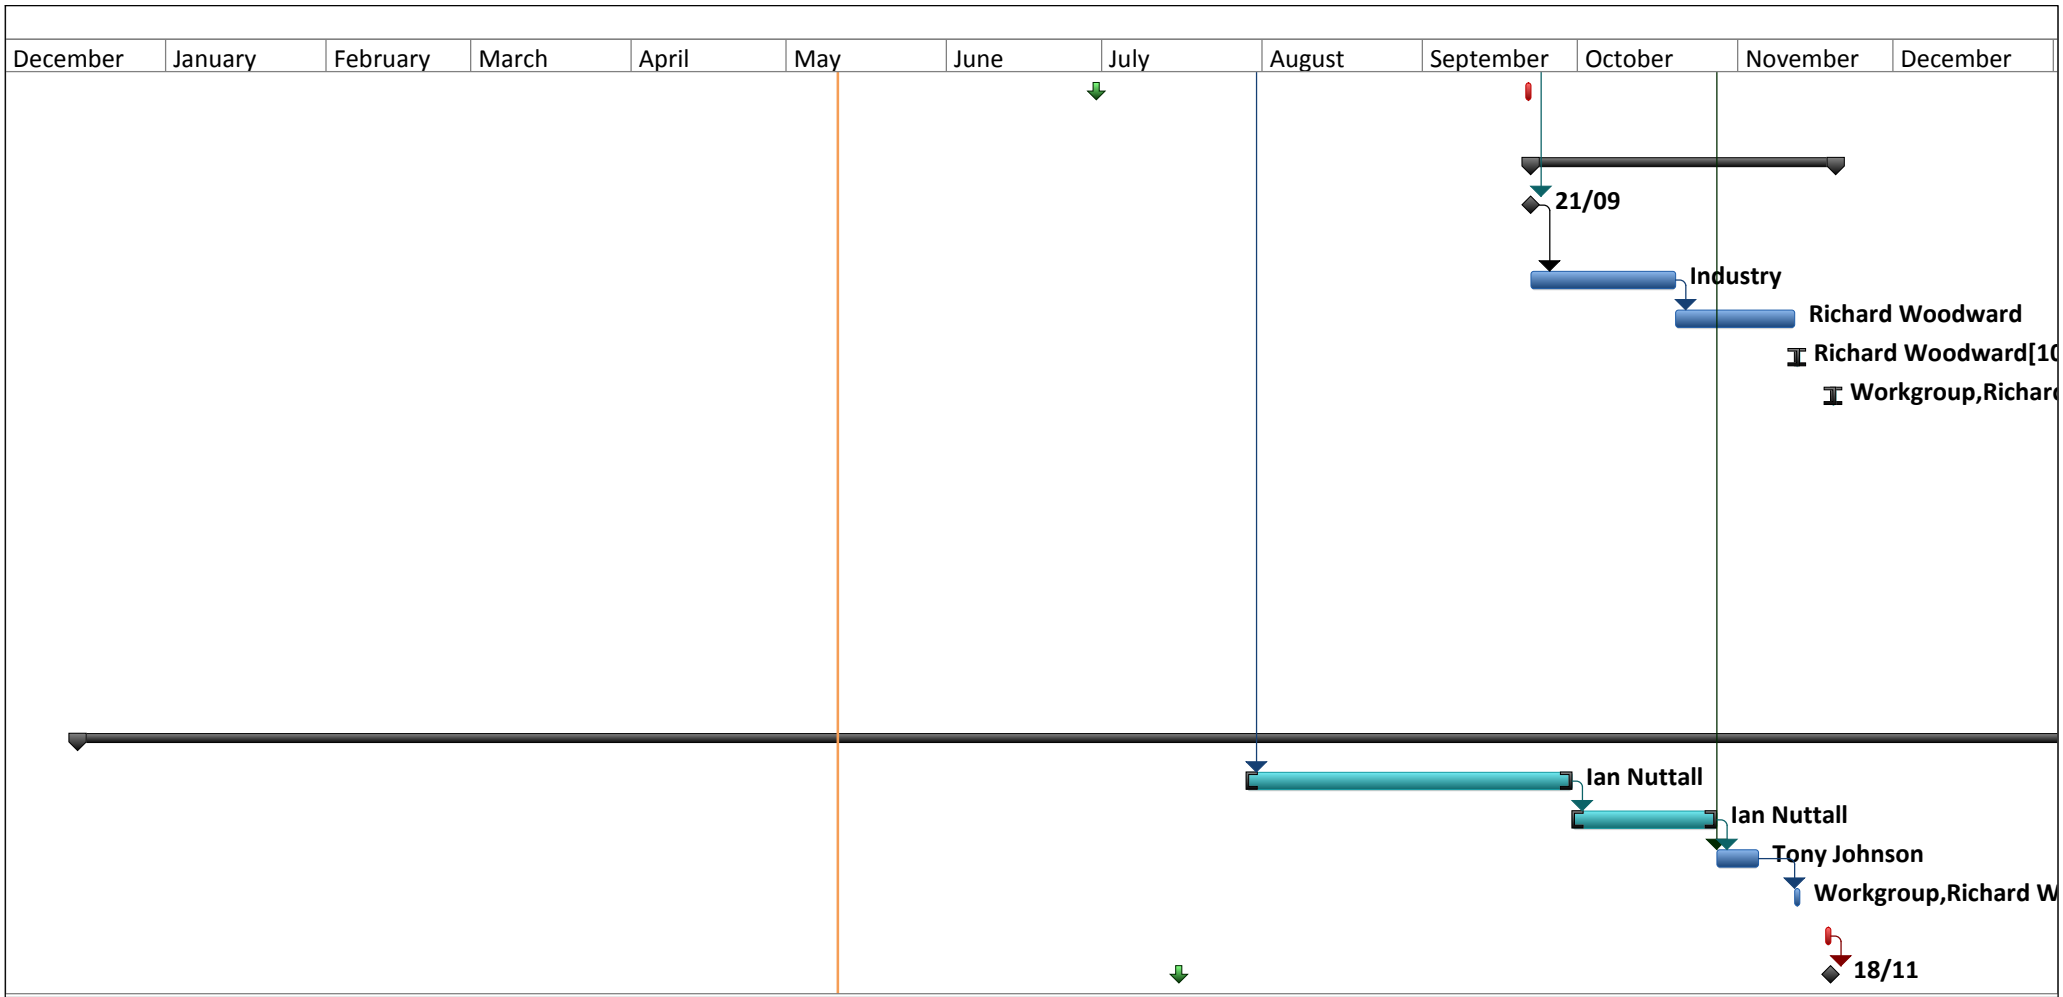


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

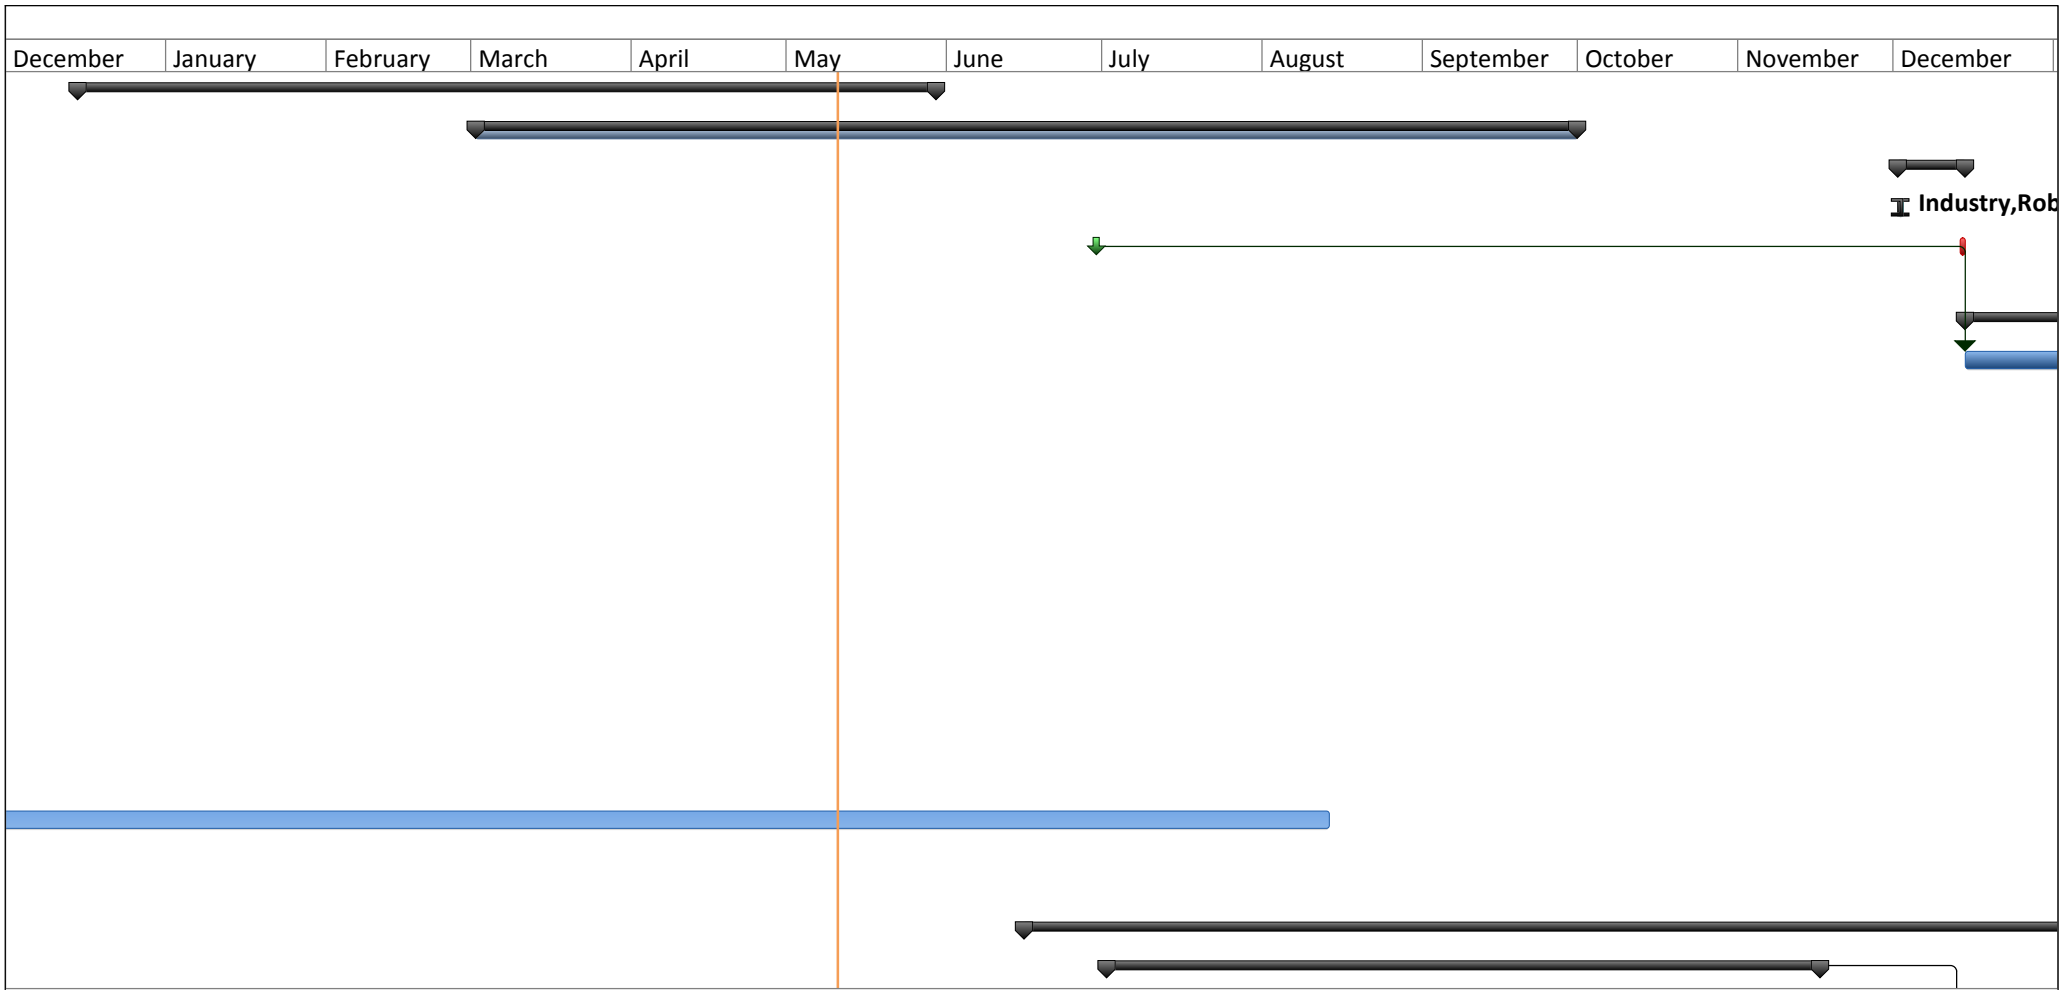


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

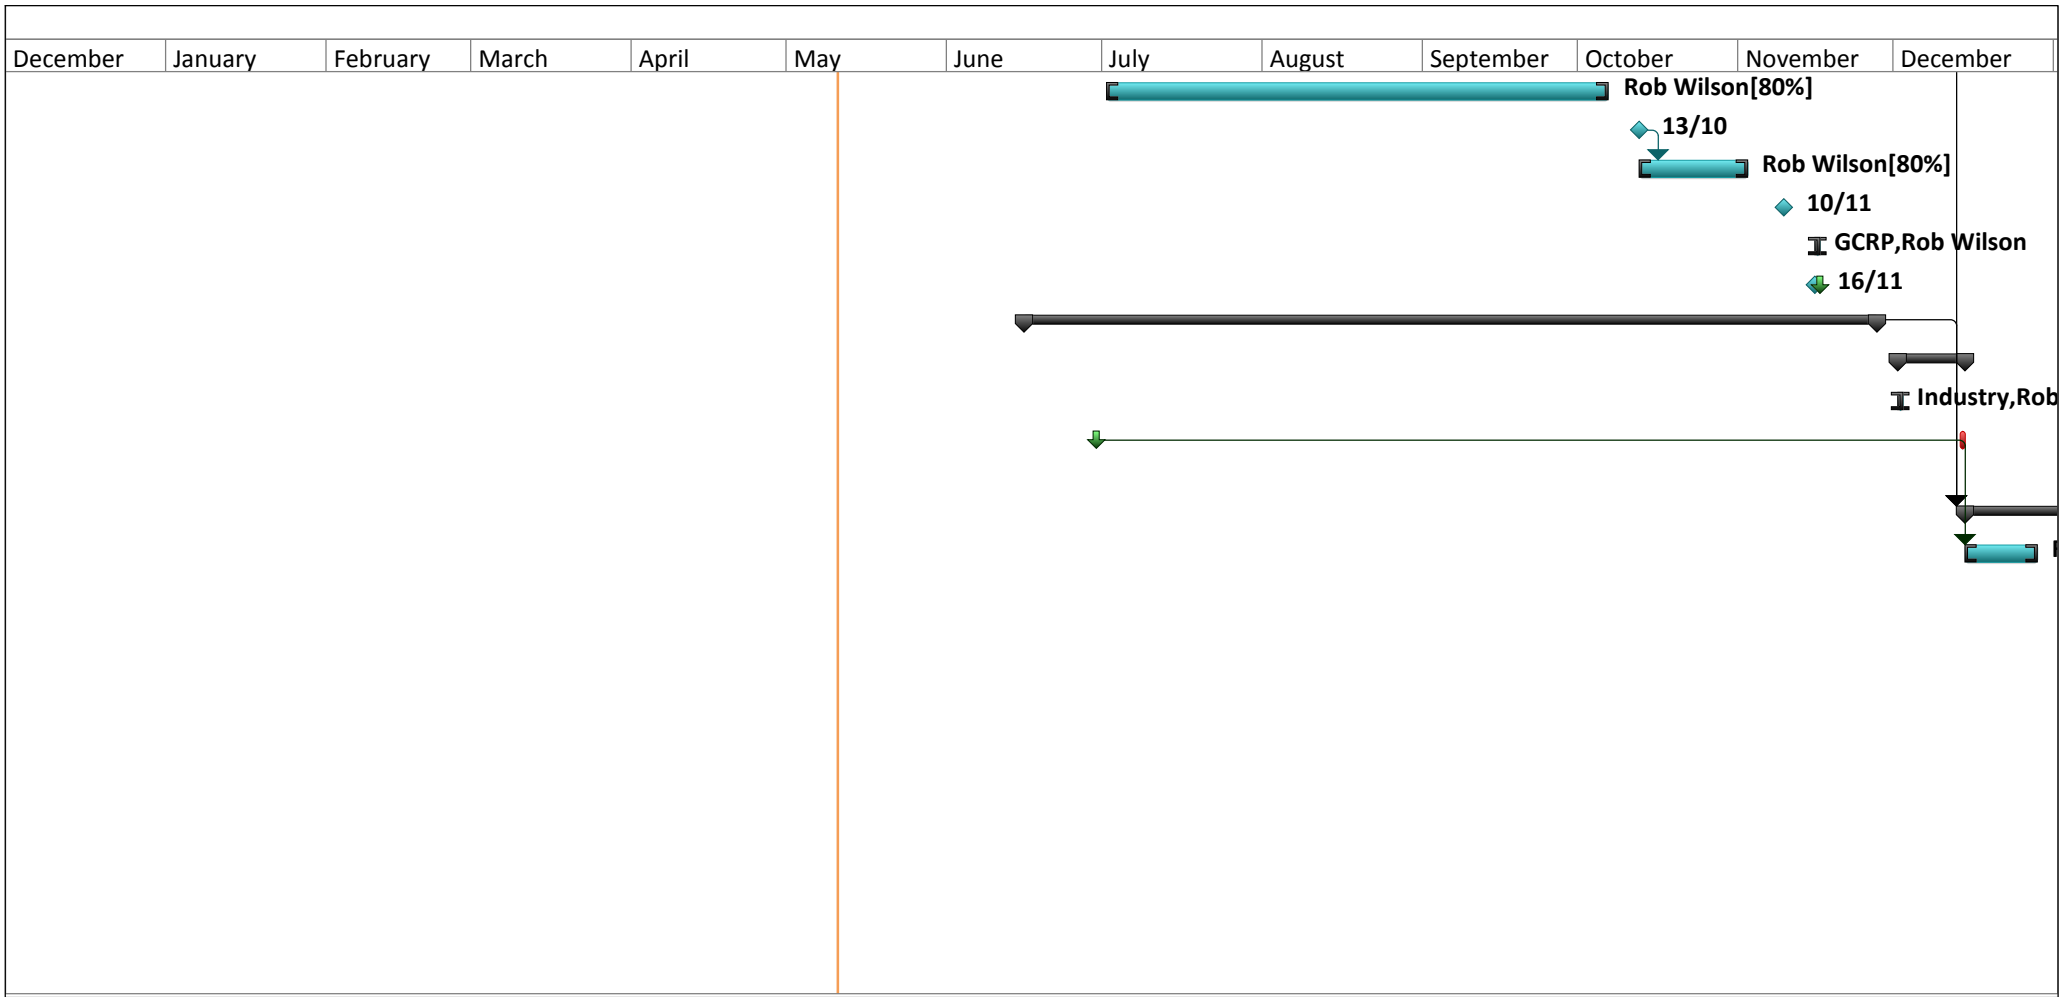


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary				

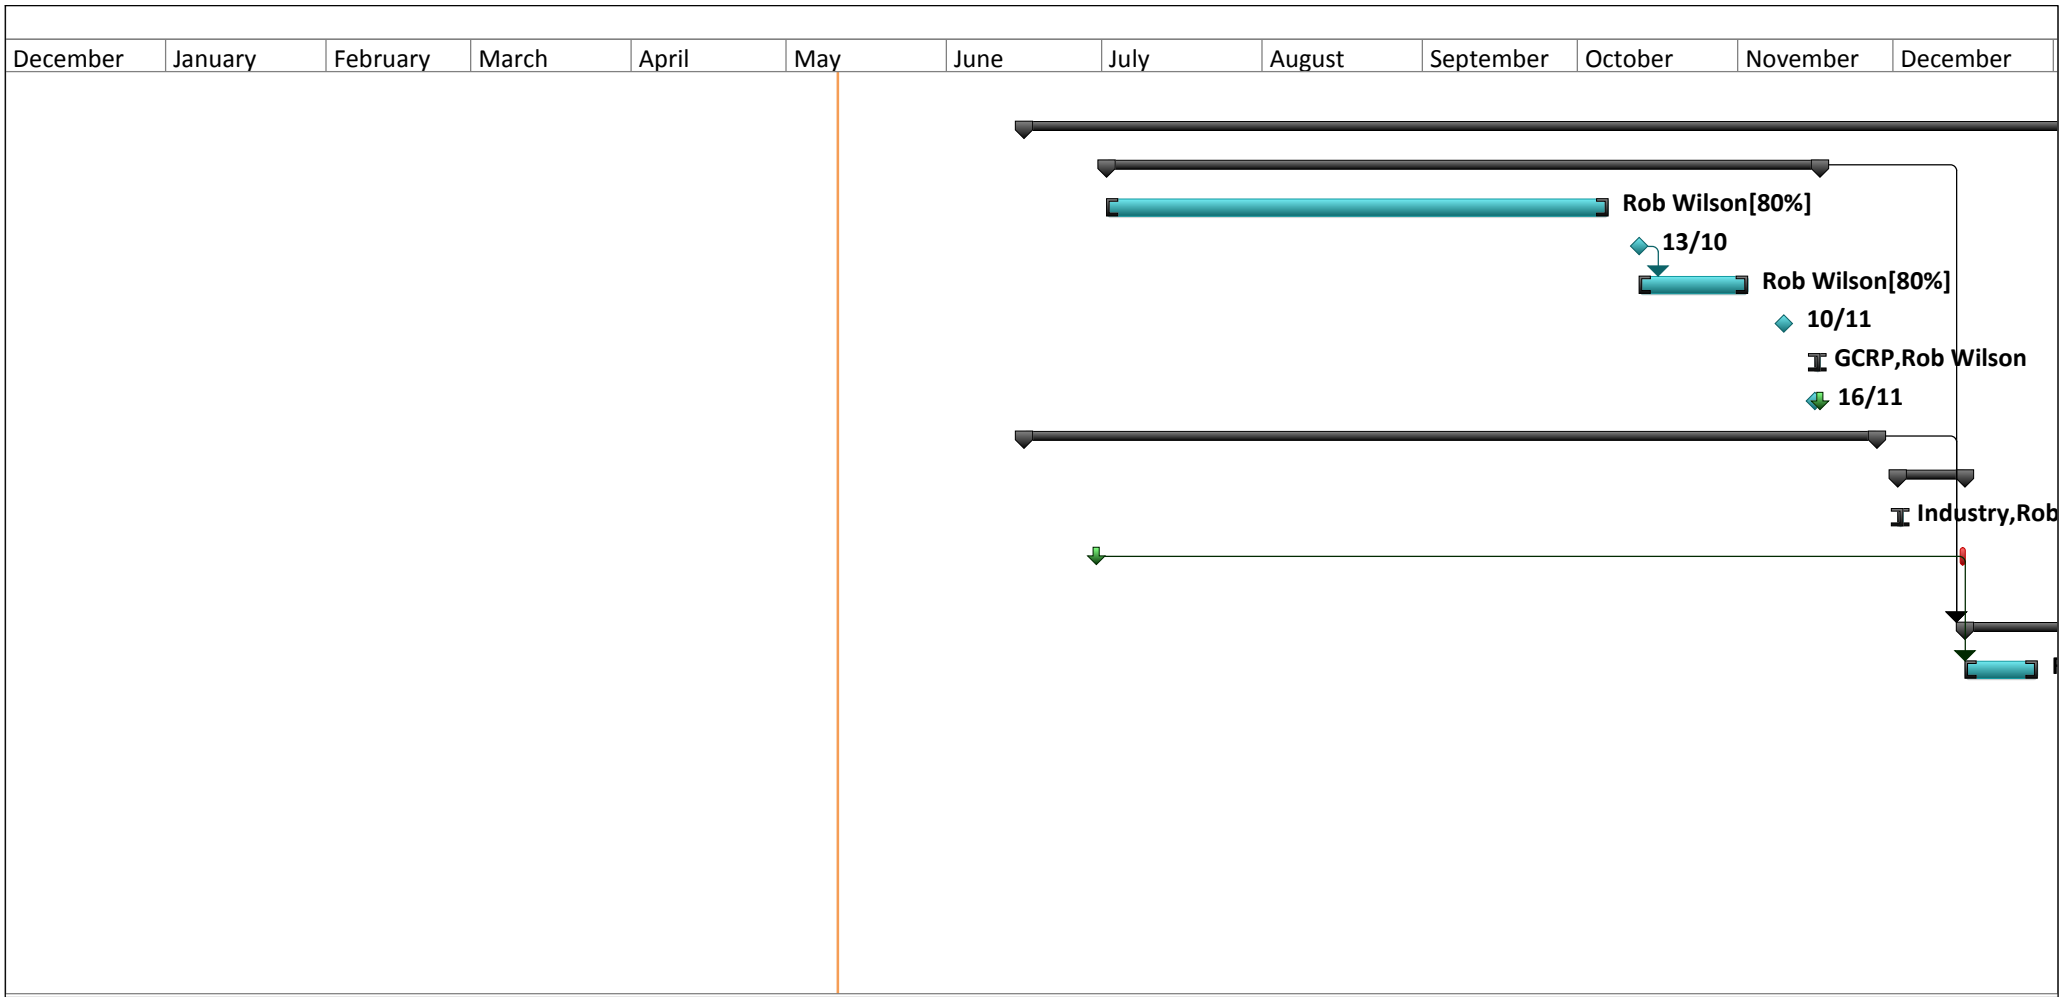


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

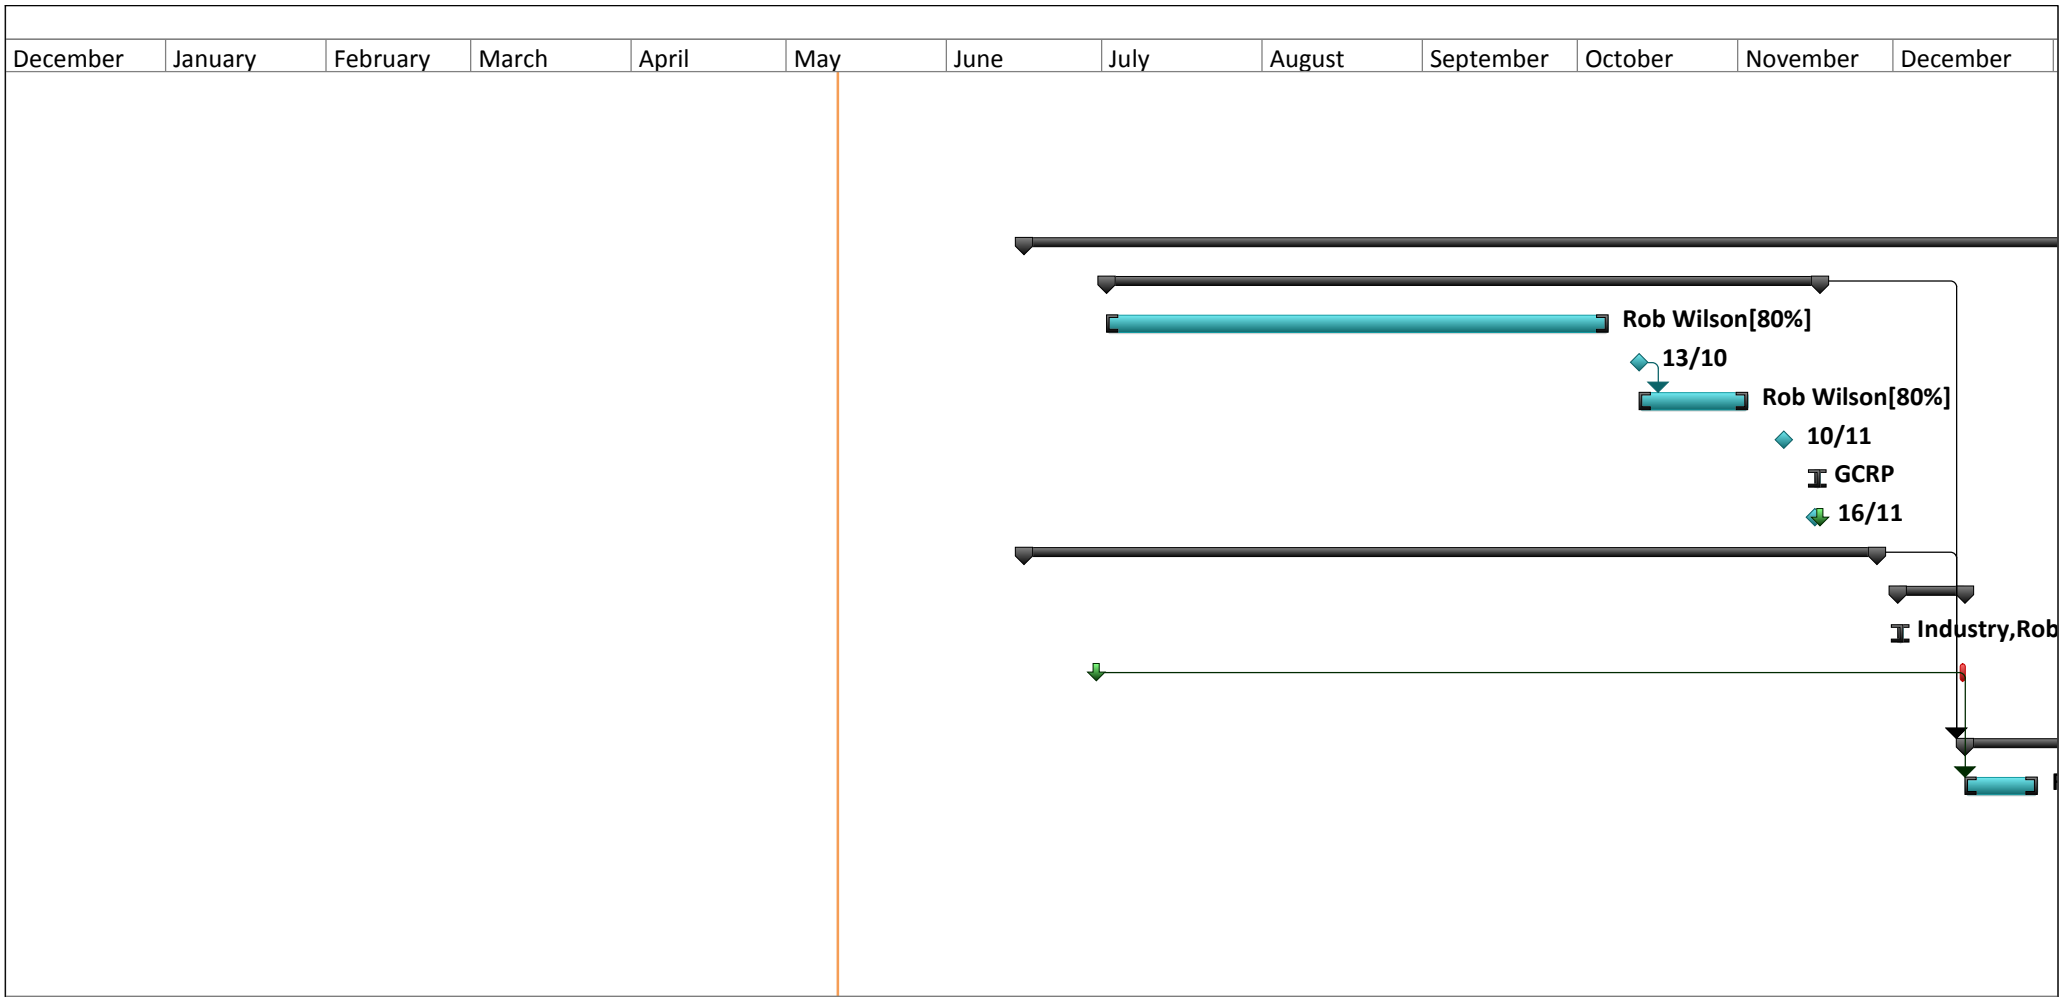


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

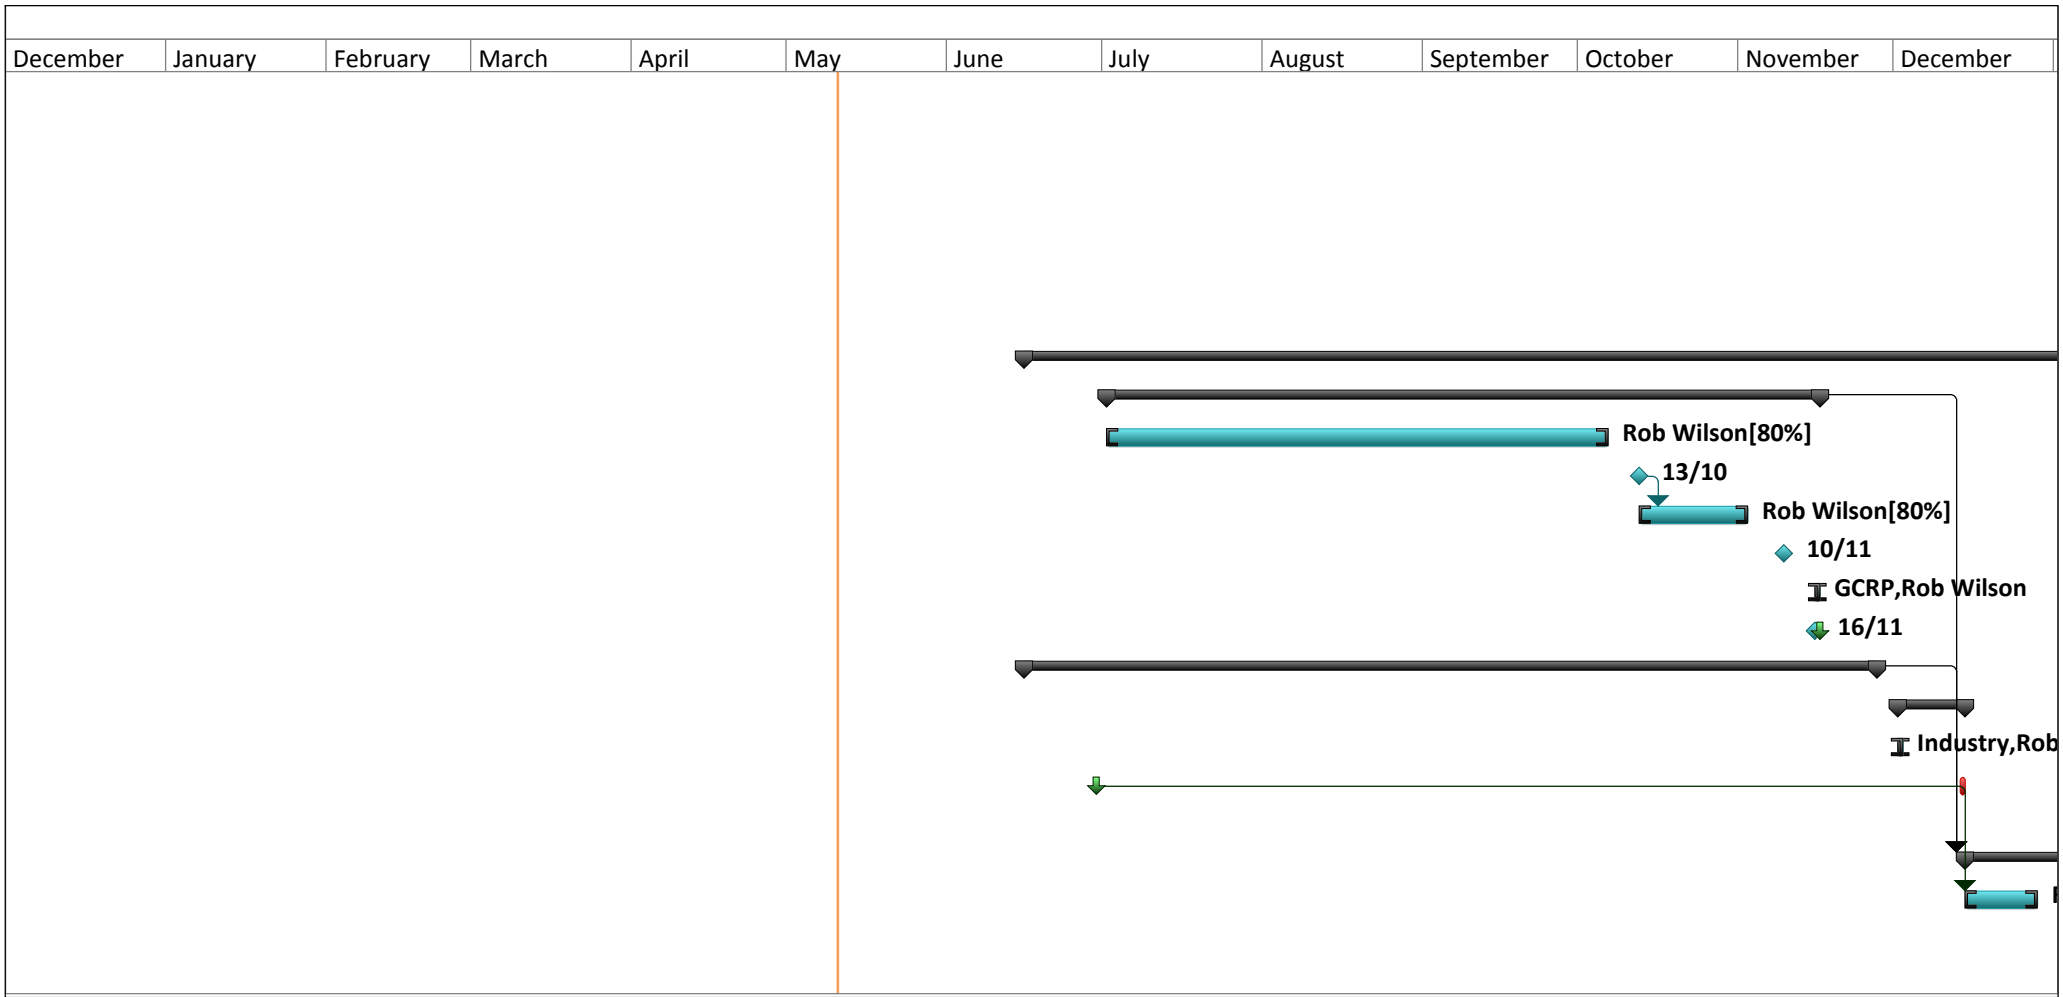


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

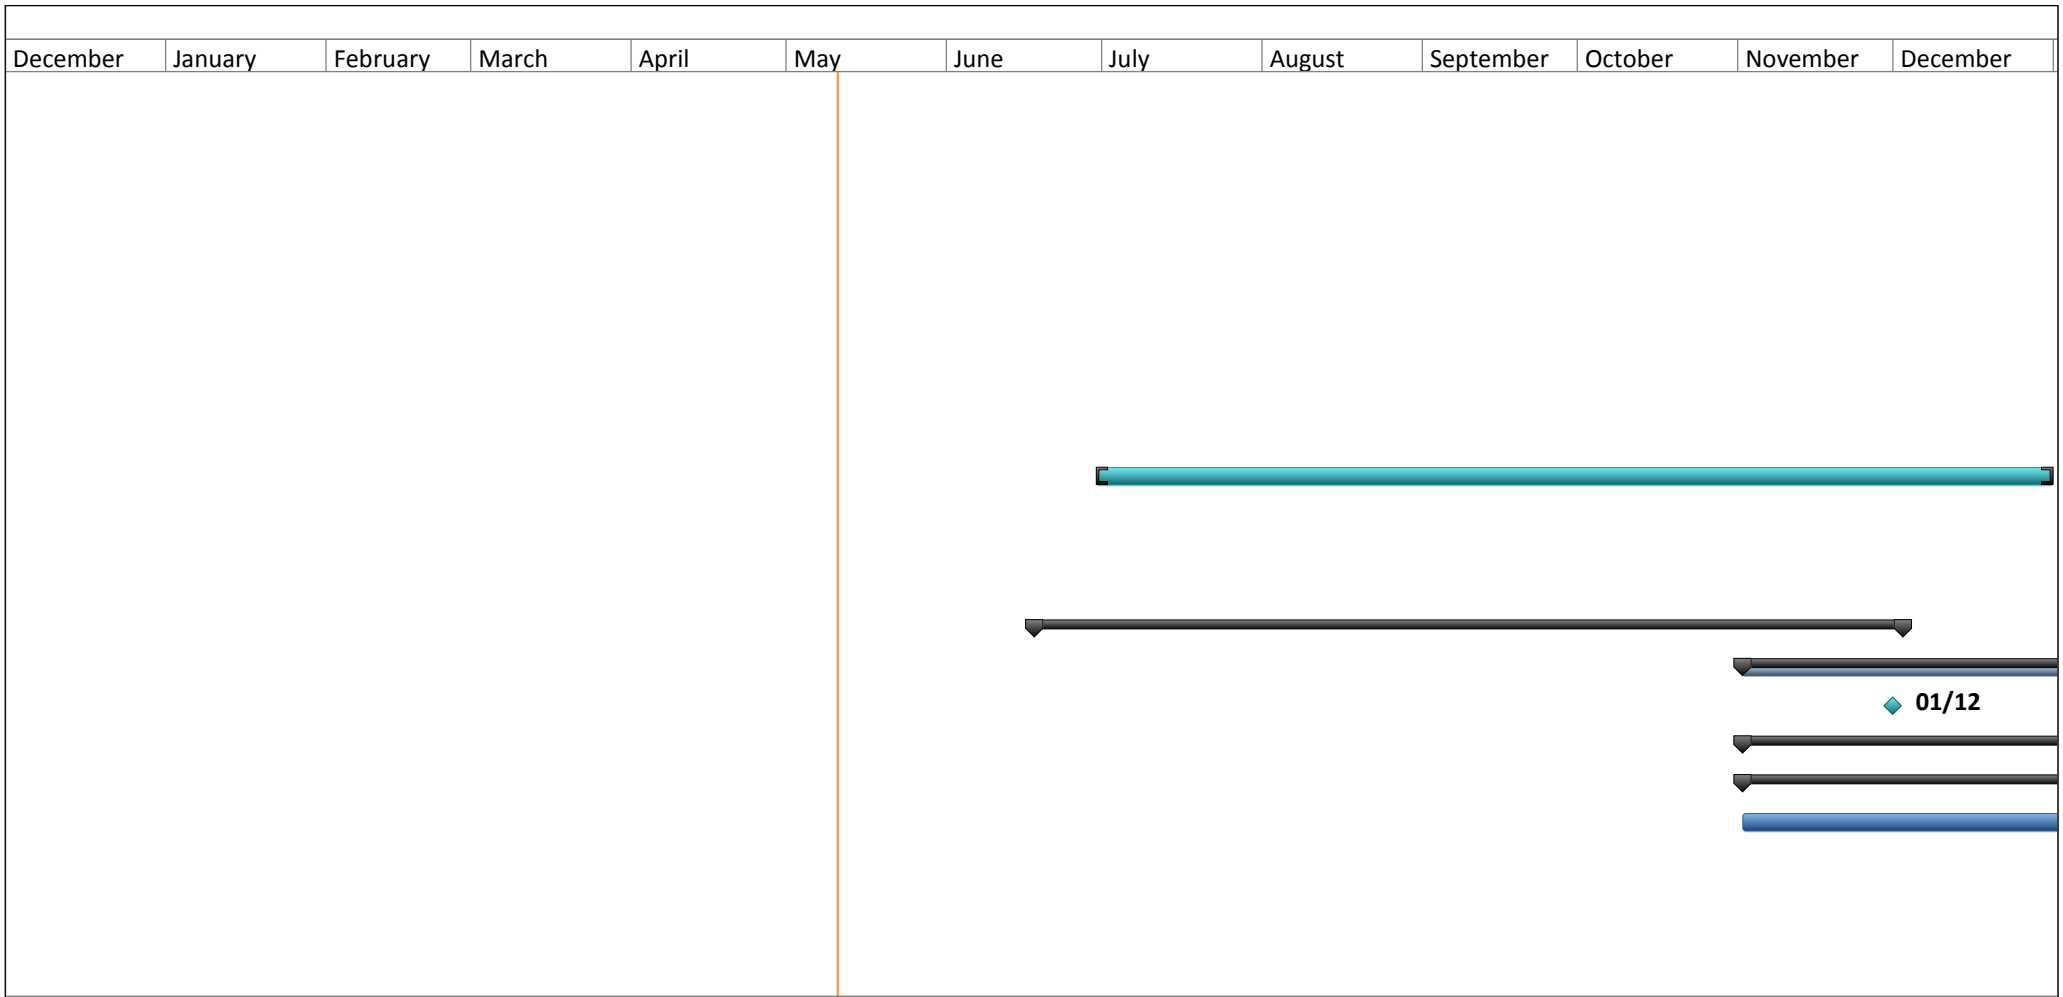


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

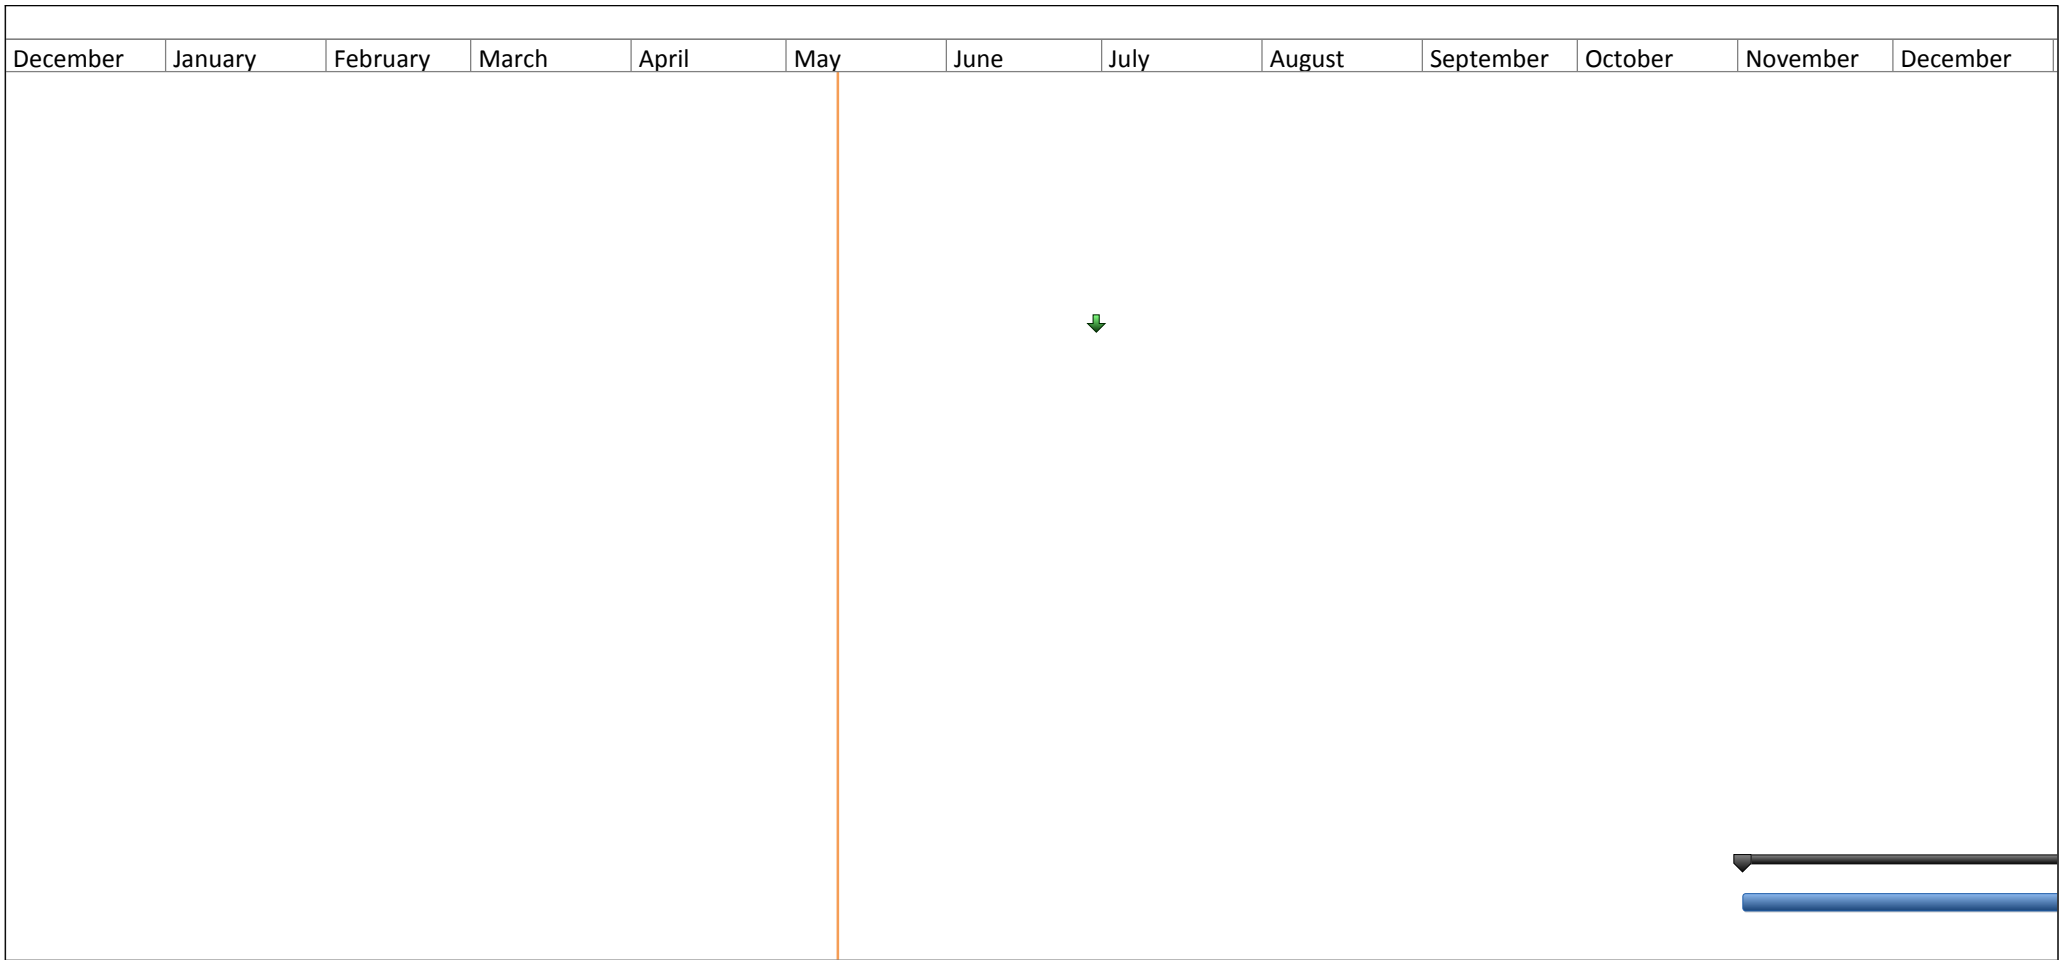


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			




Project: RfG
Date: Mon 11/05/15


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

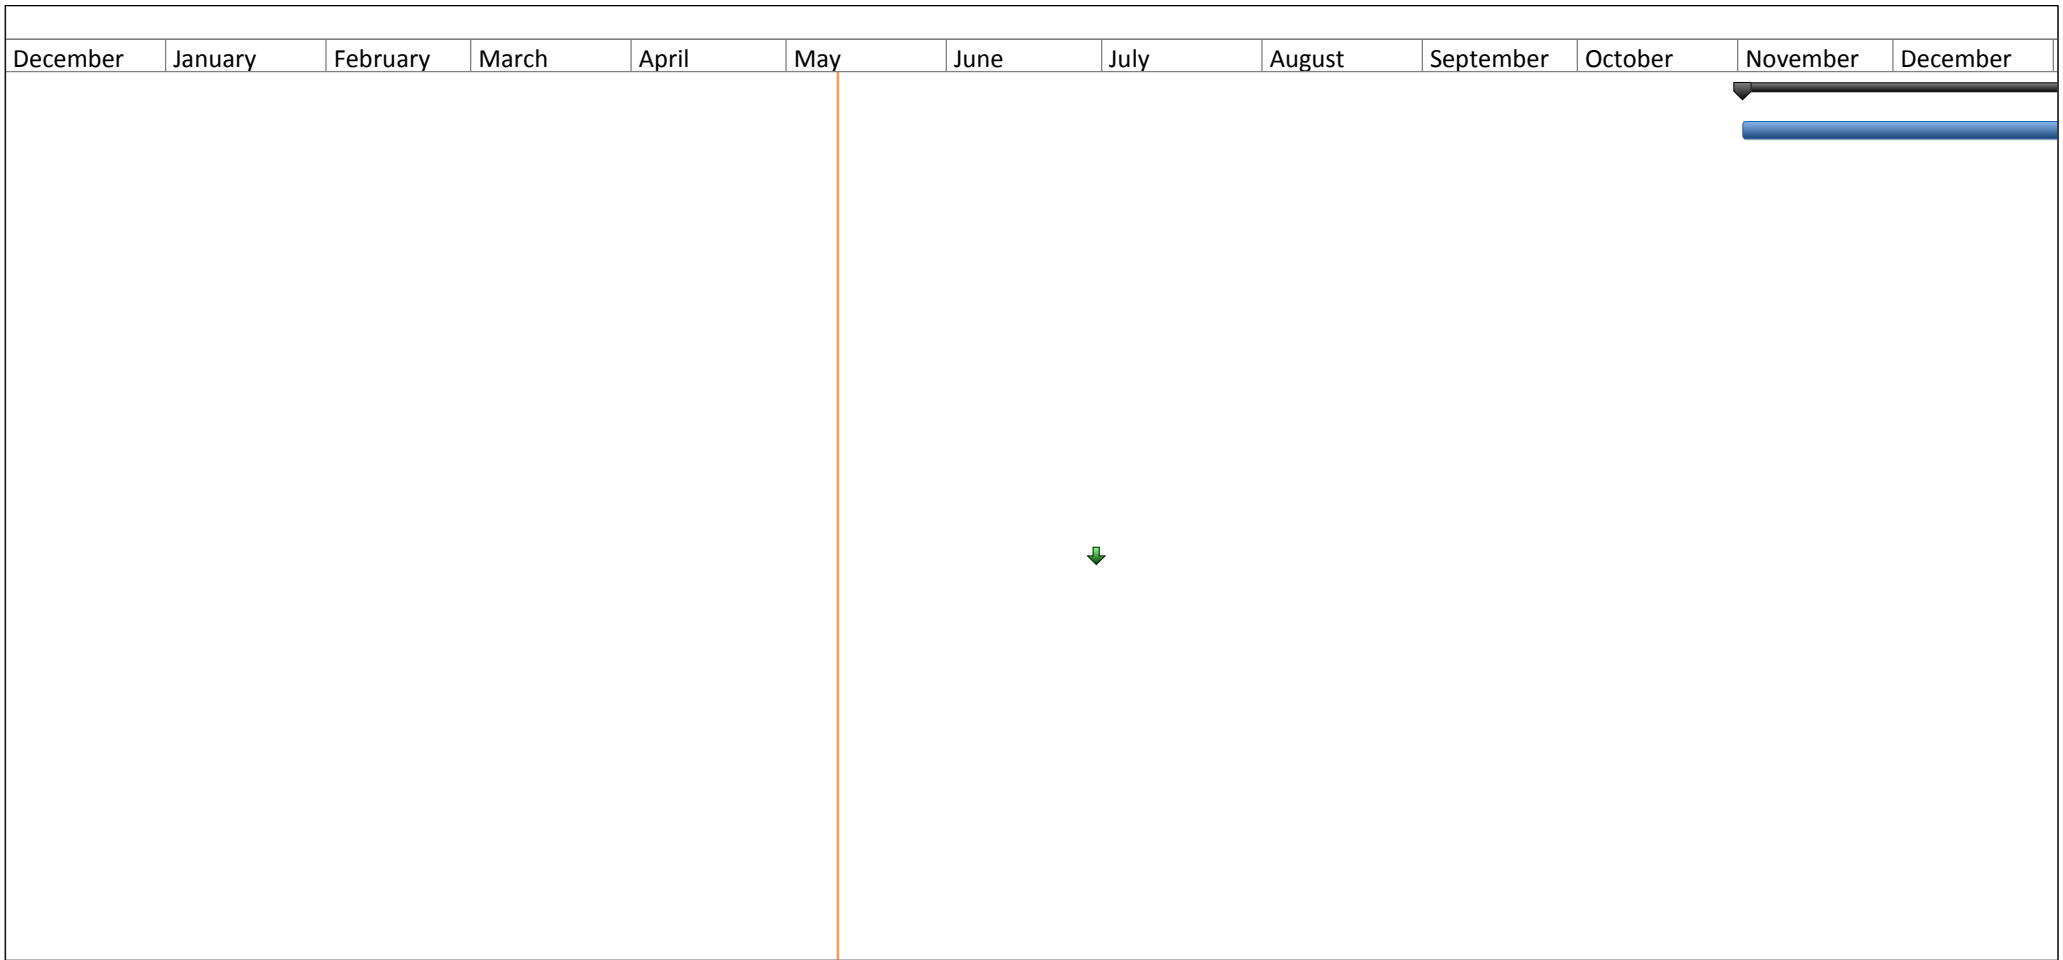

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			




Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



Project: RfG
Date: Mon 11/05/15


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

December	January	February	March	April	May	June	July	August	September	October	November	December
----------	---------	----------	-------	-------	-----	------	------	--------	-----------	---------	----------	----------




Project: RfG
Date: Mon 11/05/15


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			



Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			




Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary				

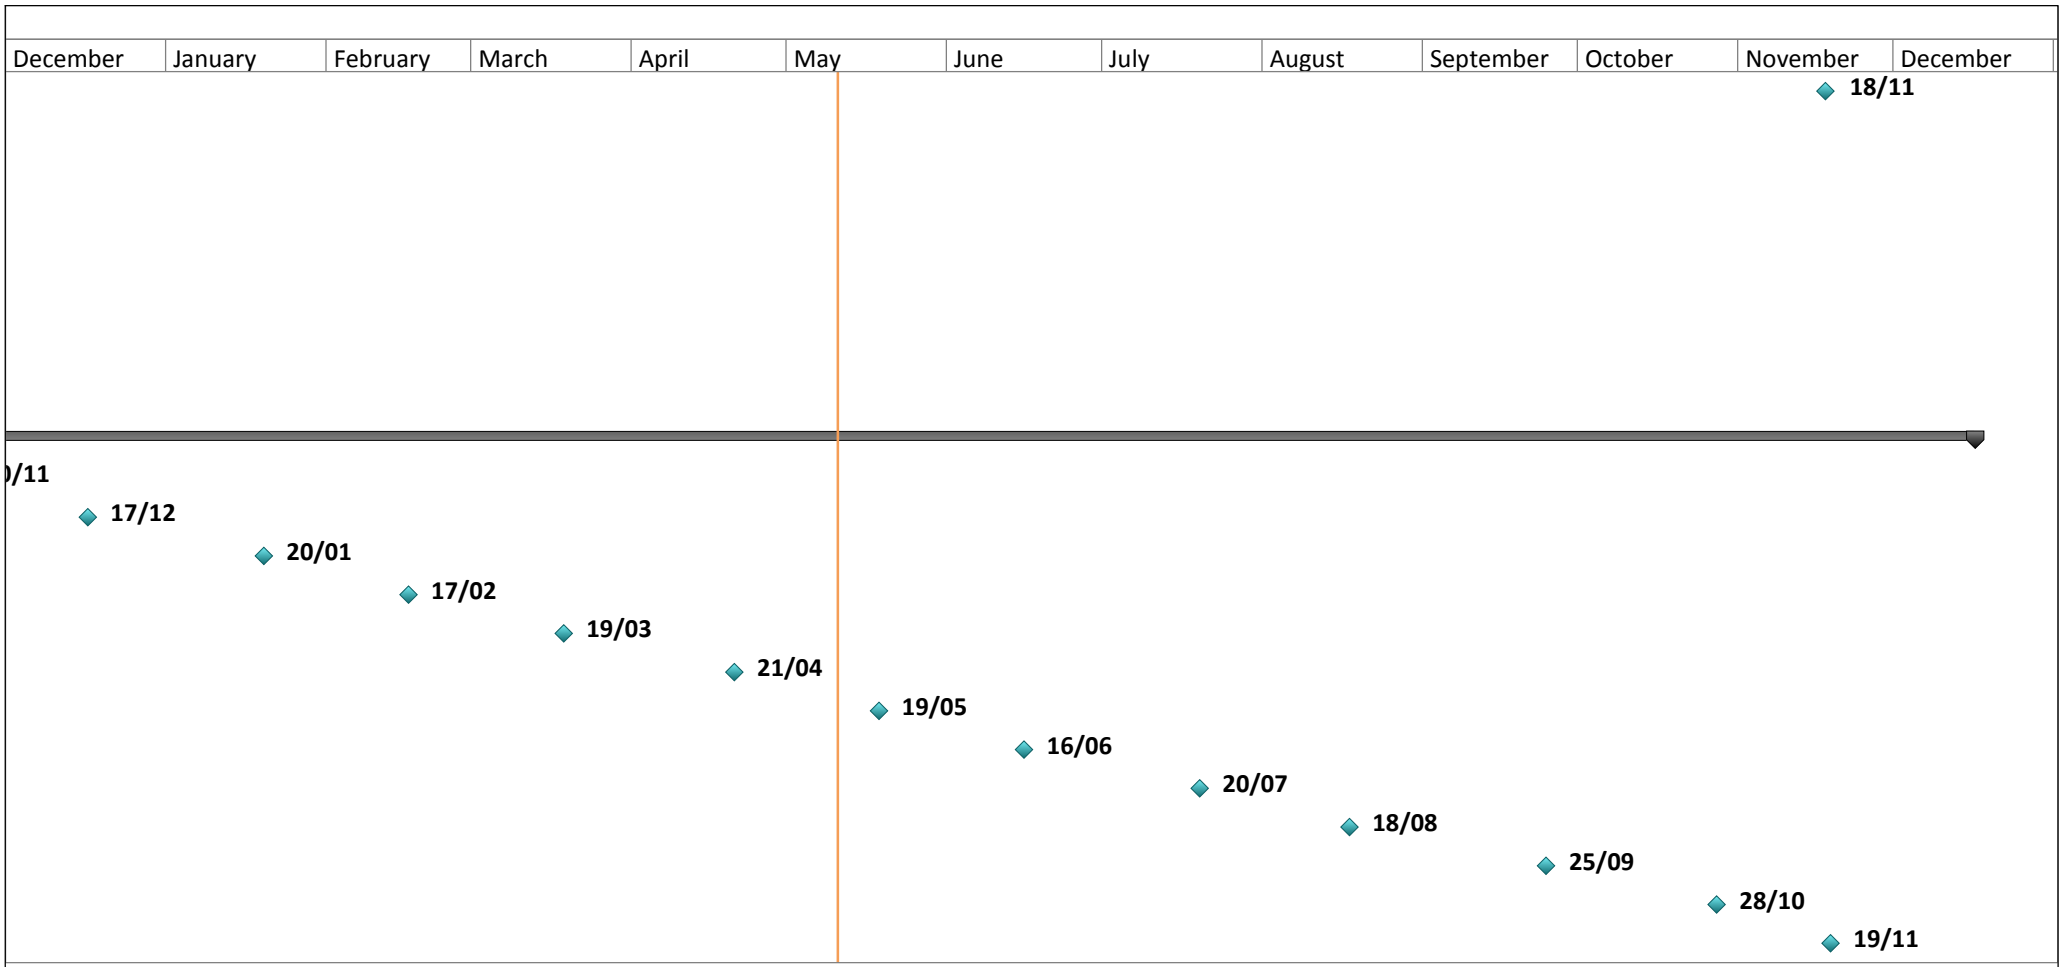


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

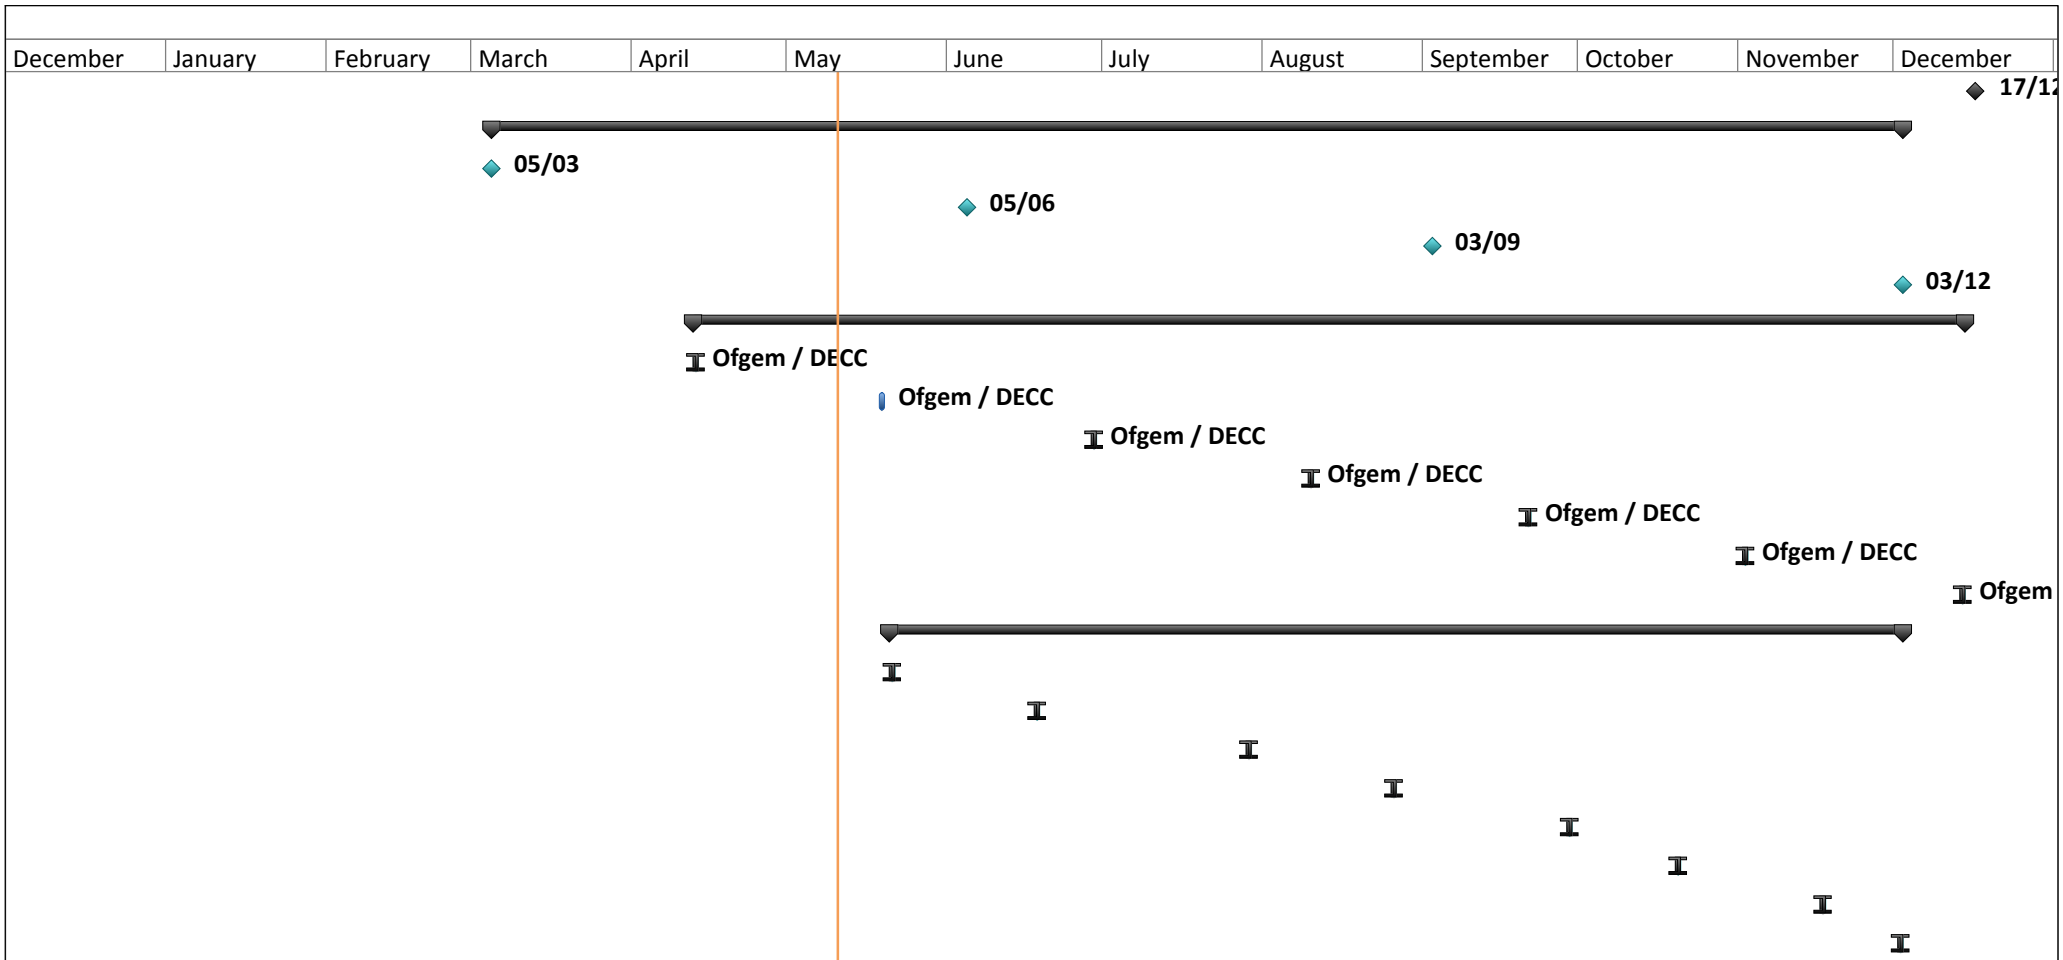


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

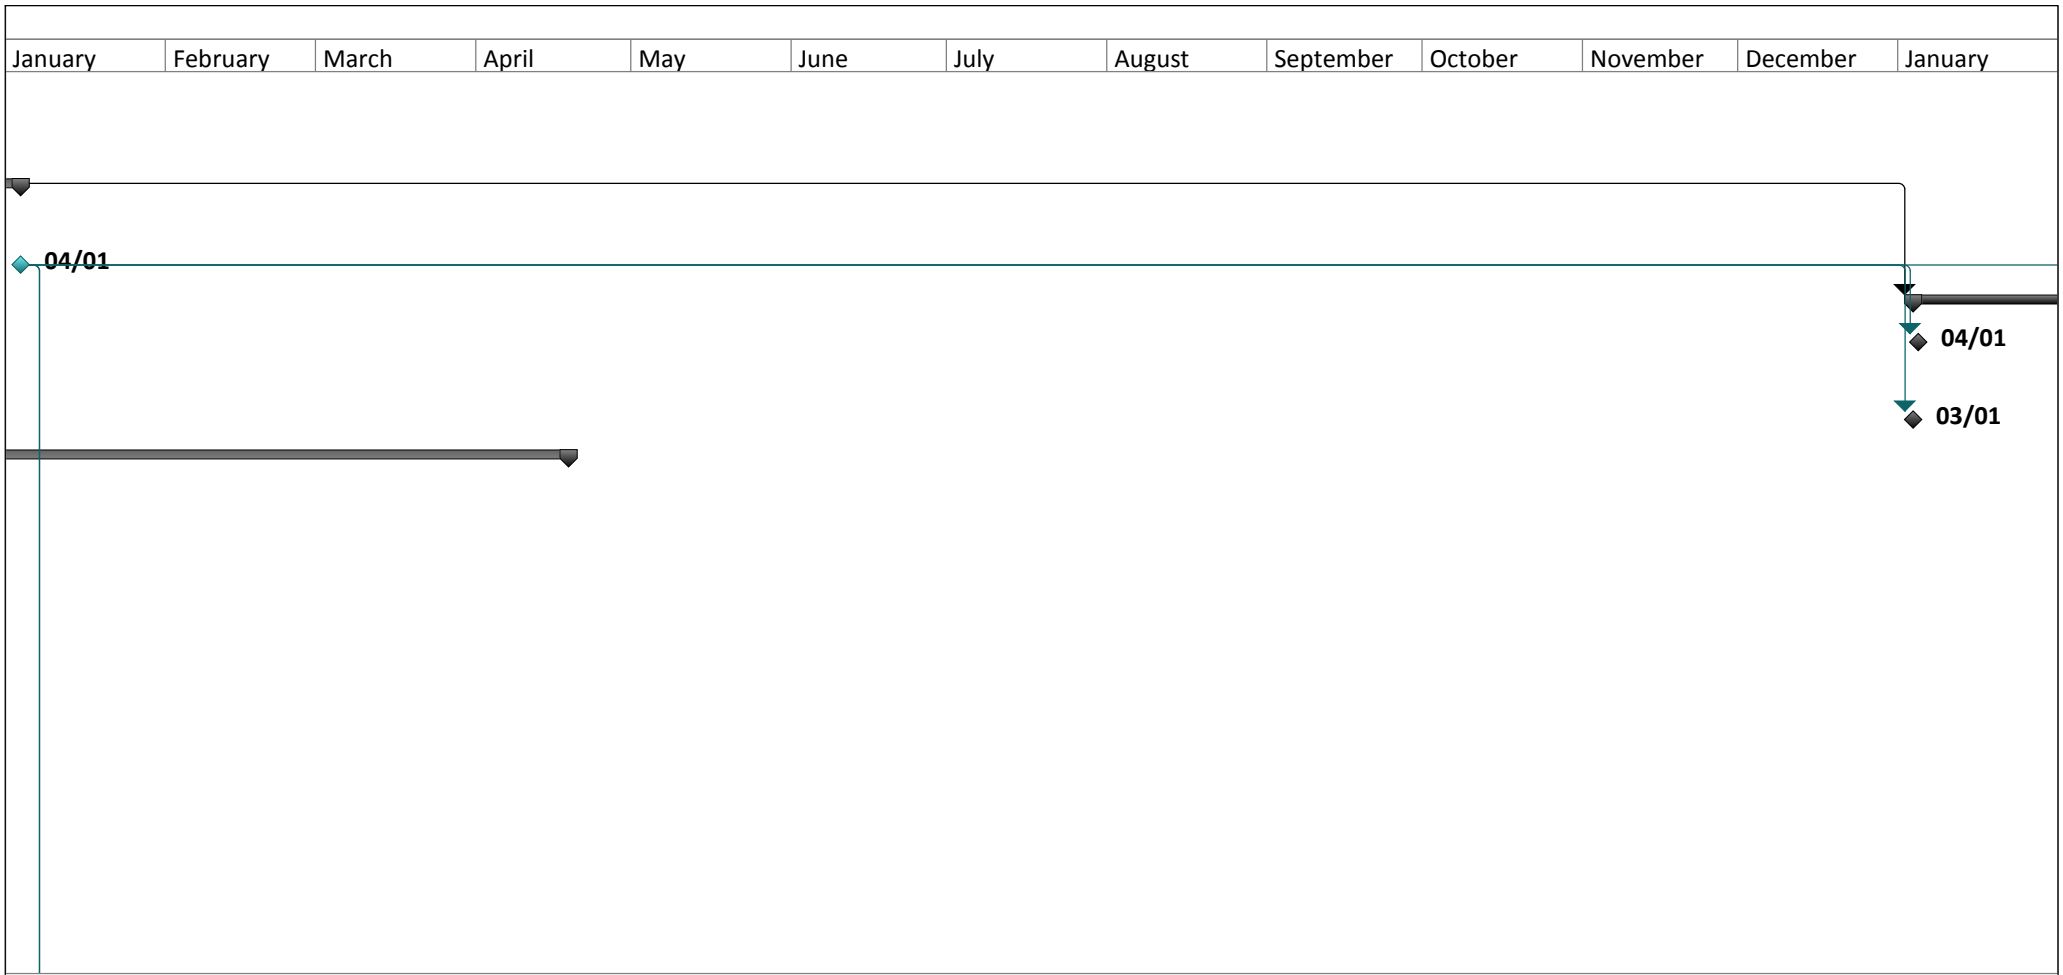


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

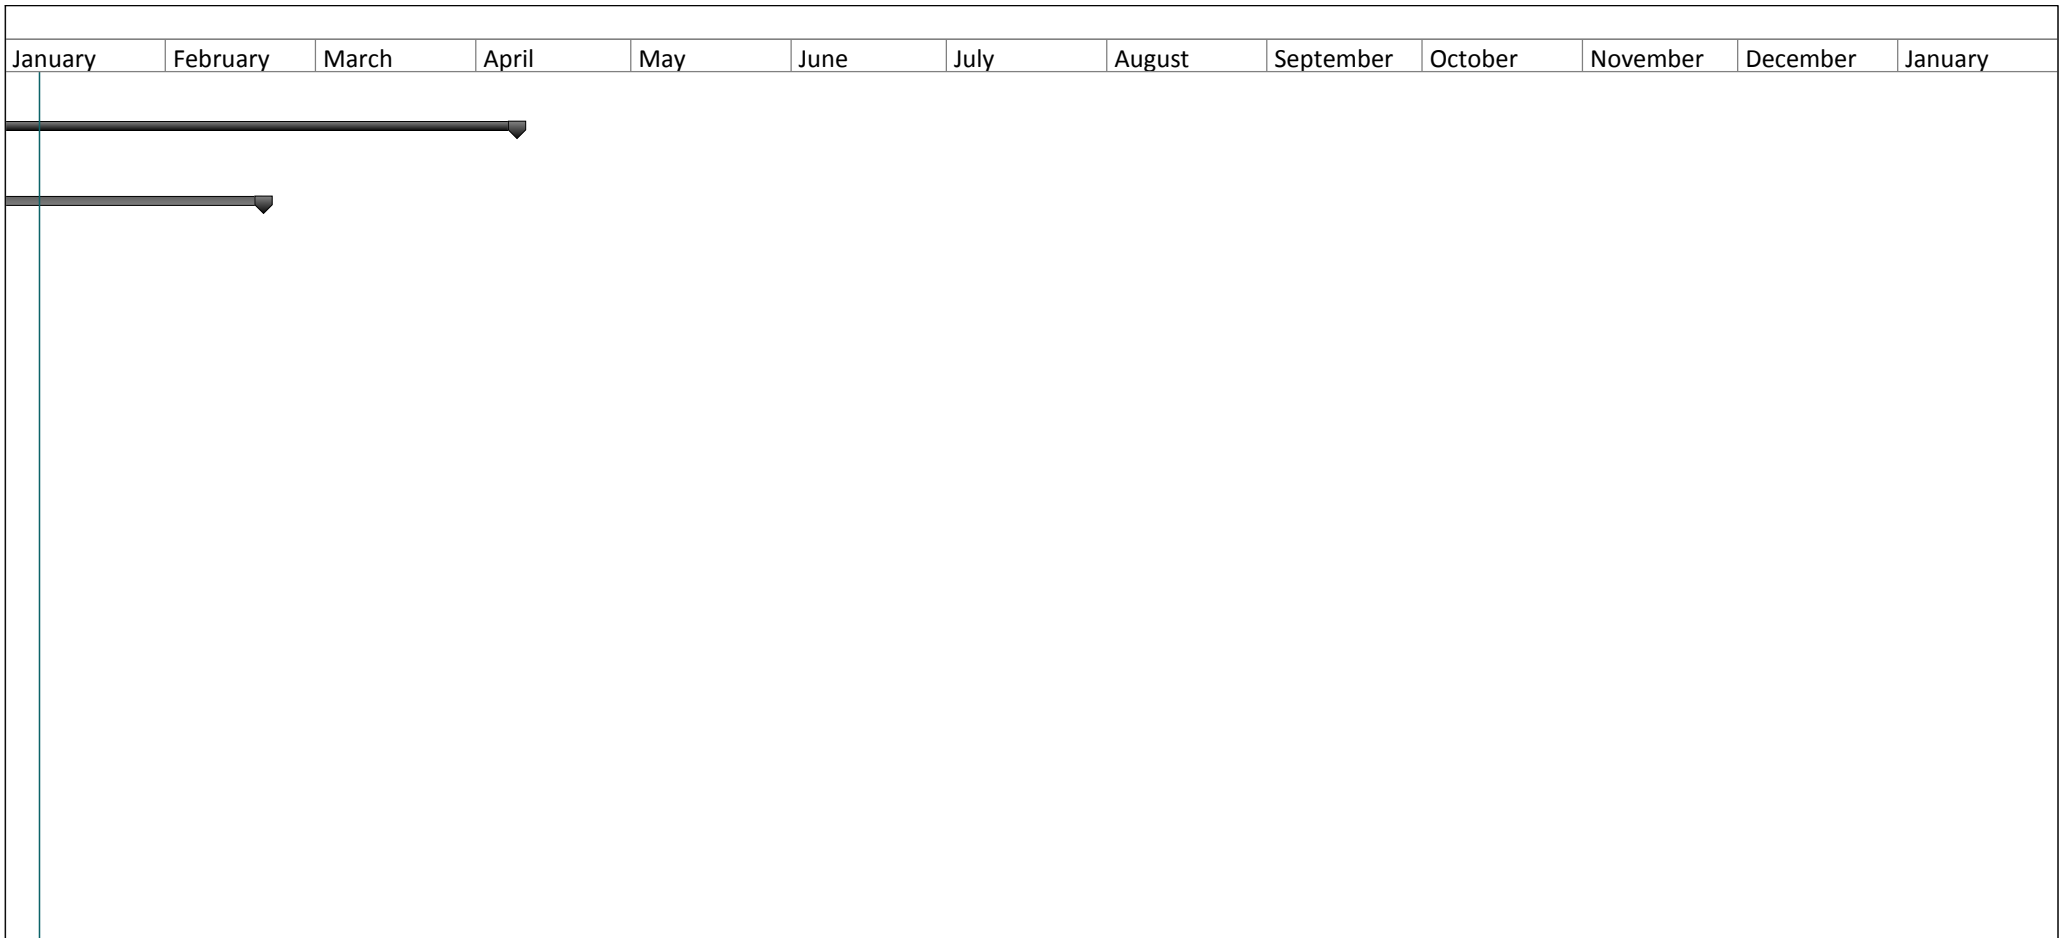


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			




Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

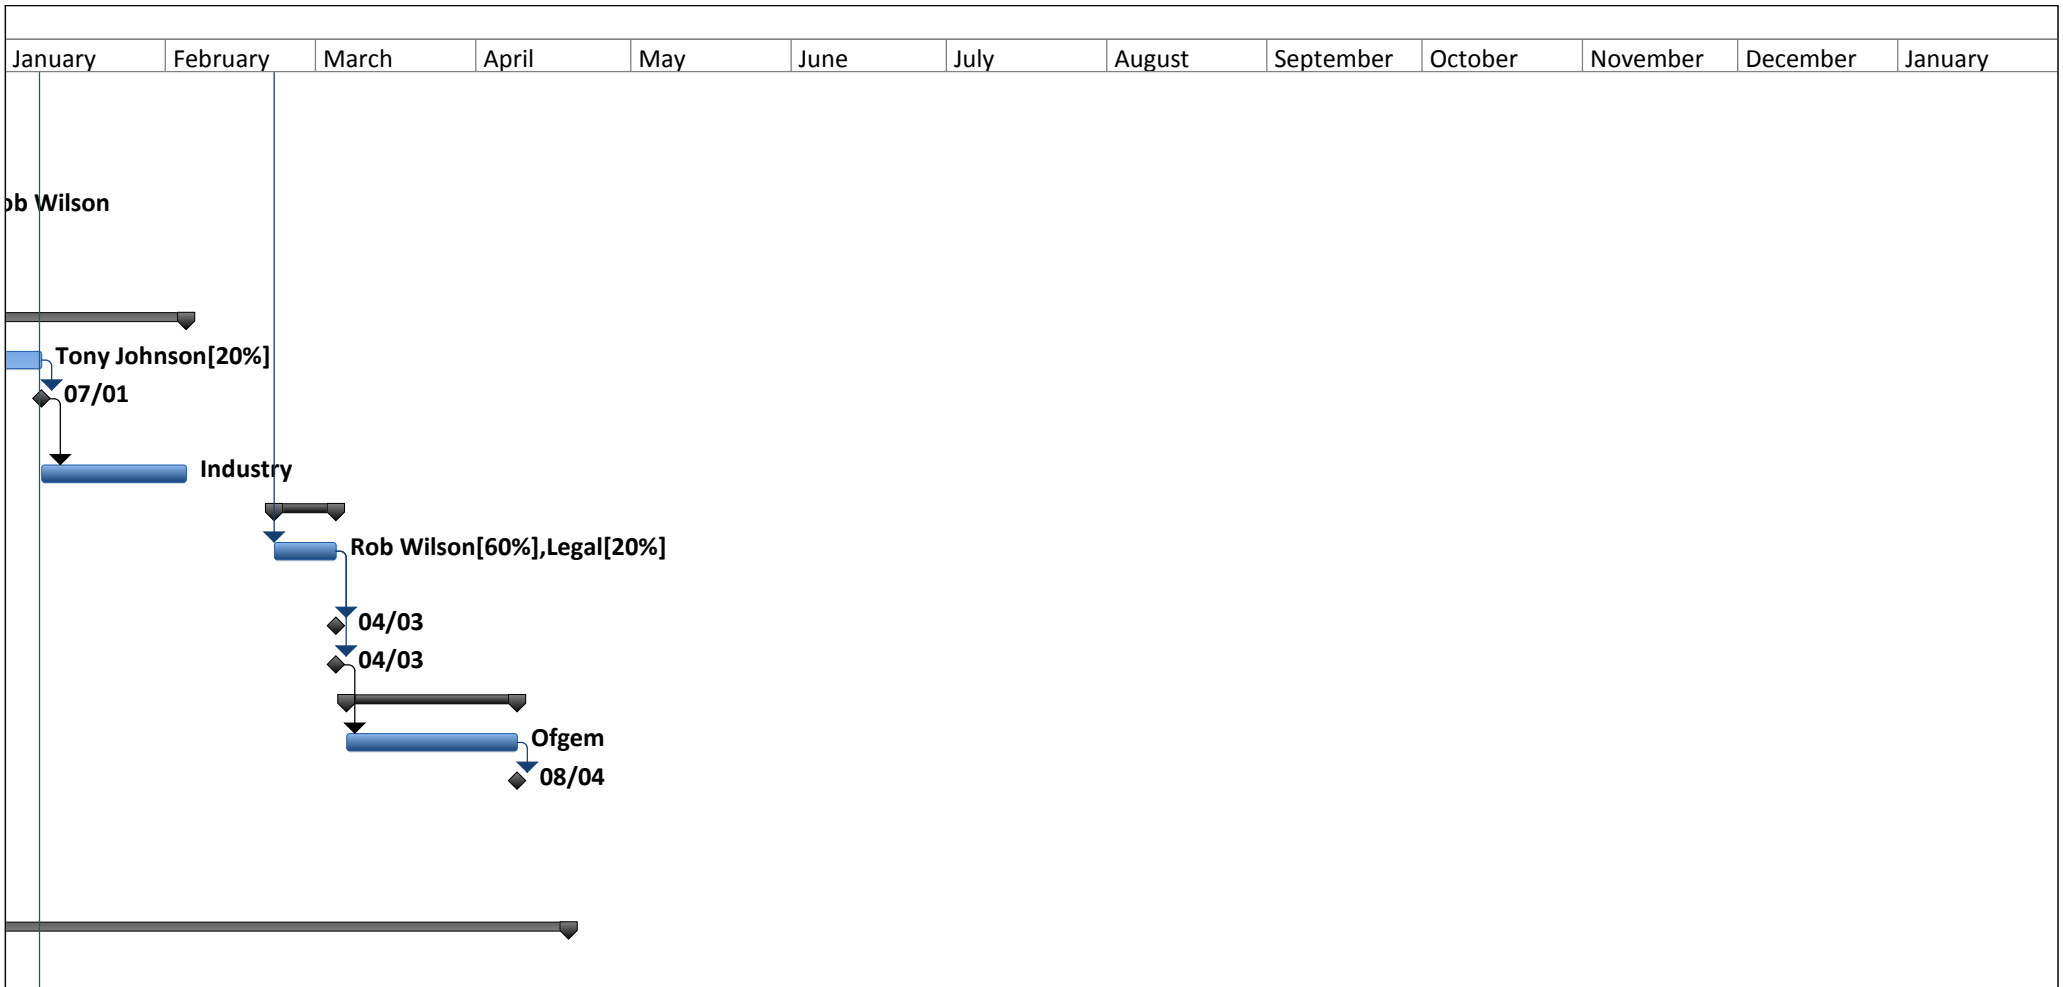


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

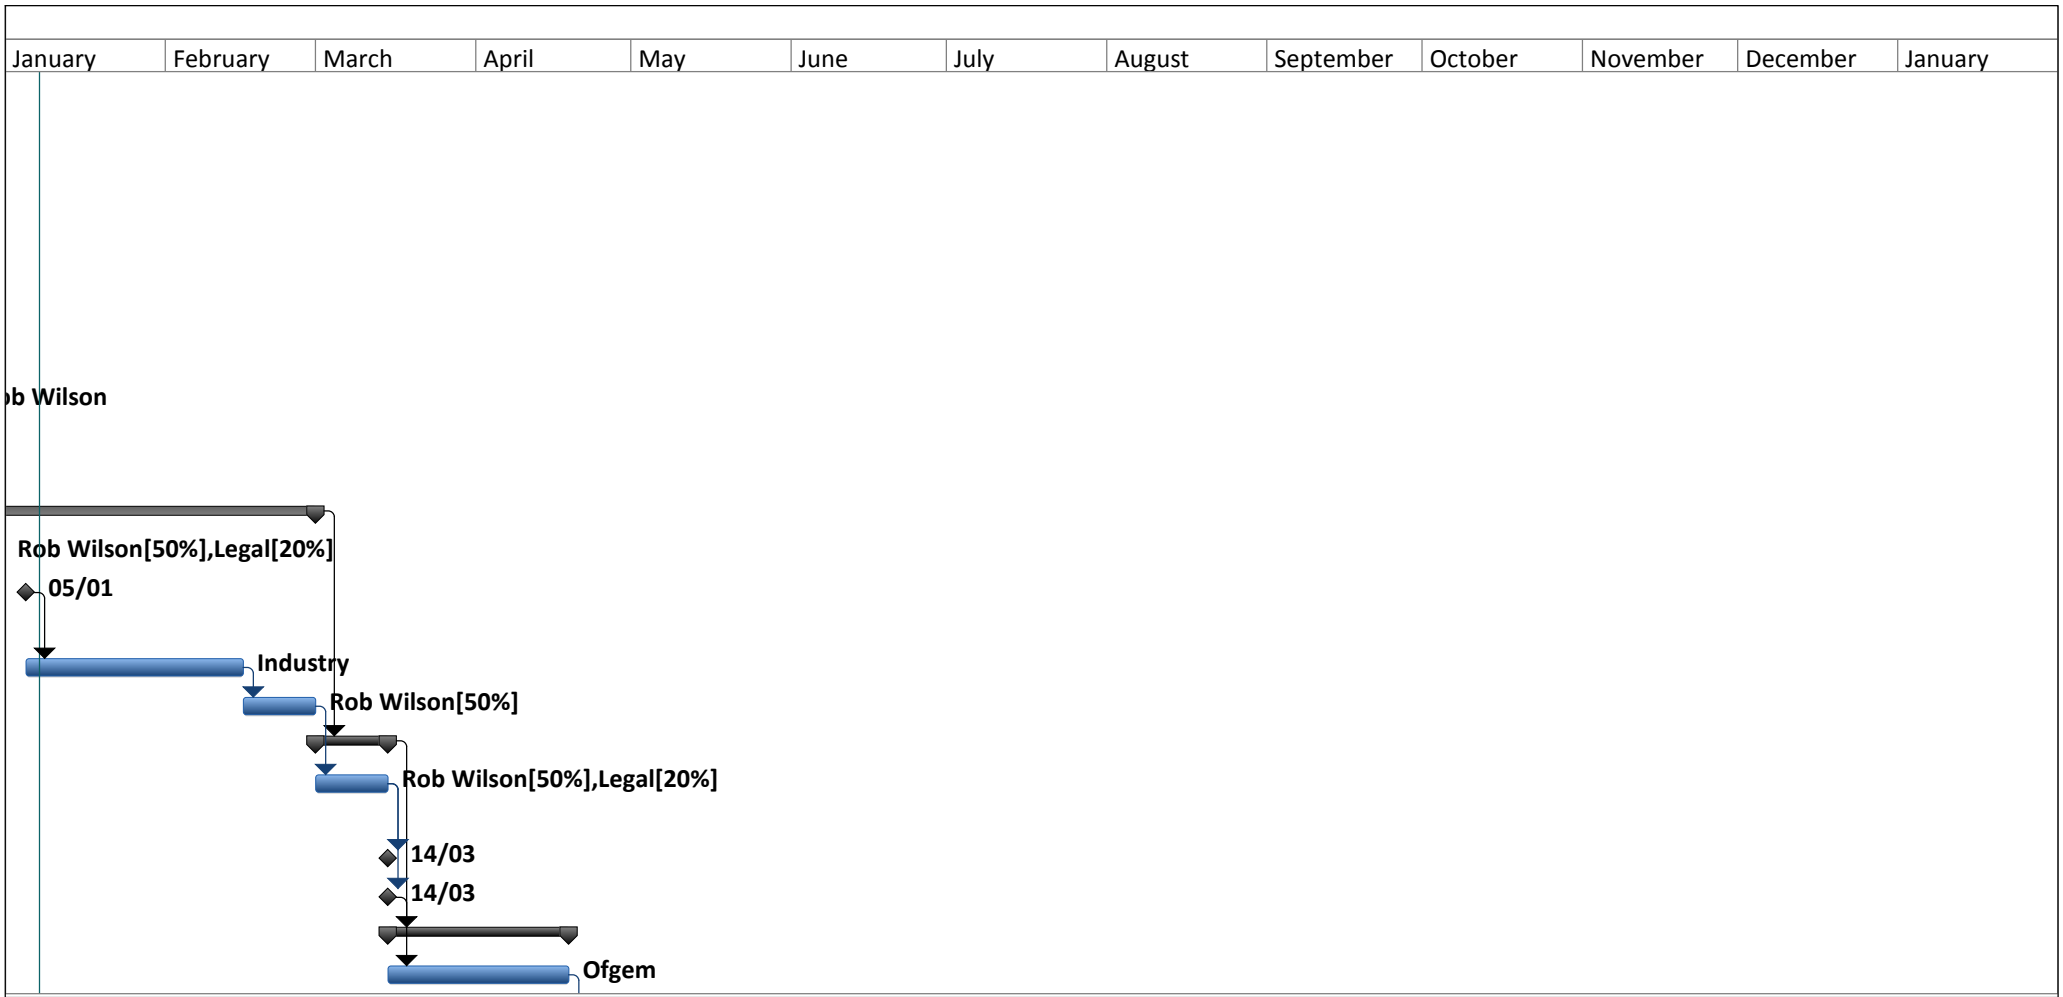


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			


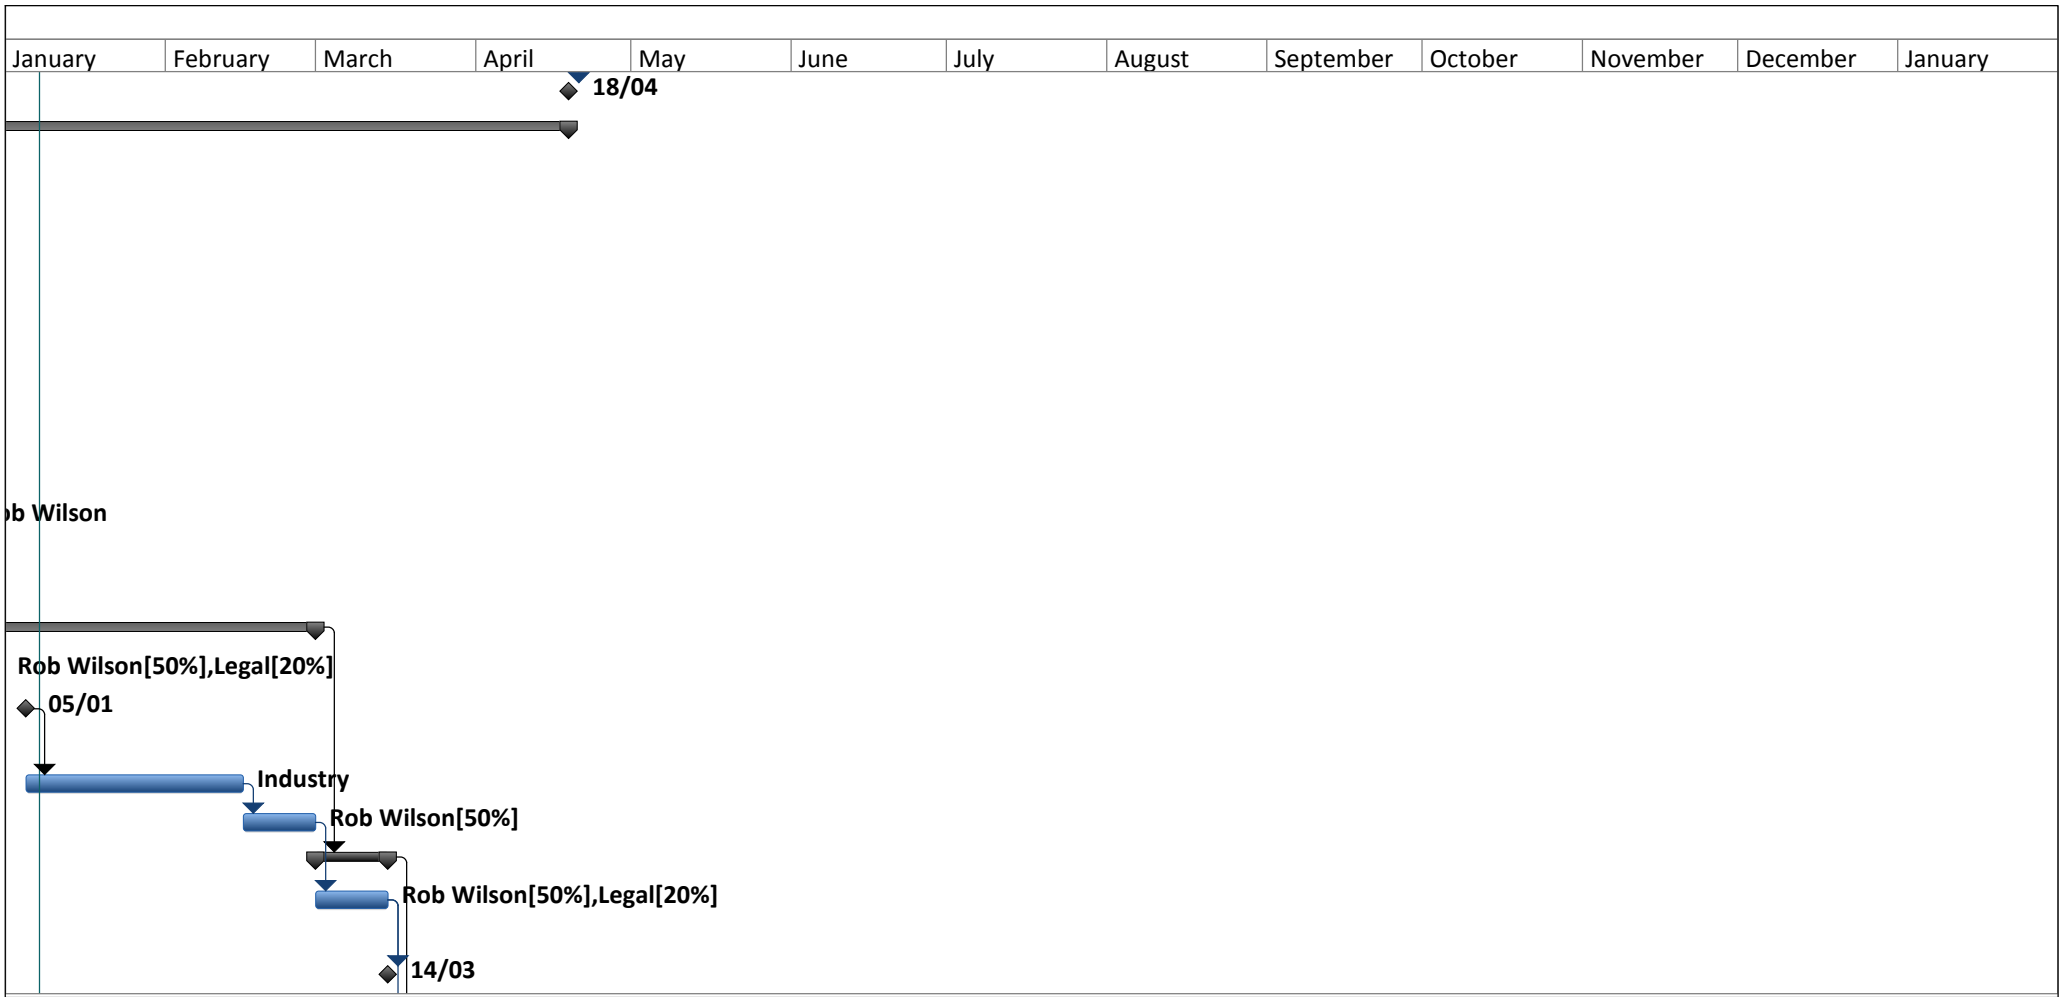


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

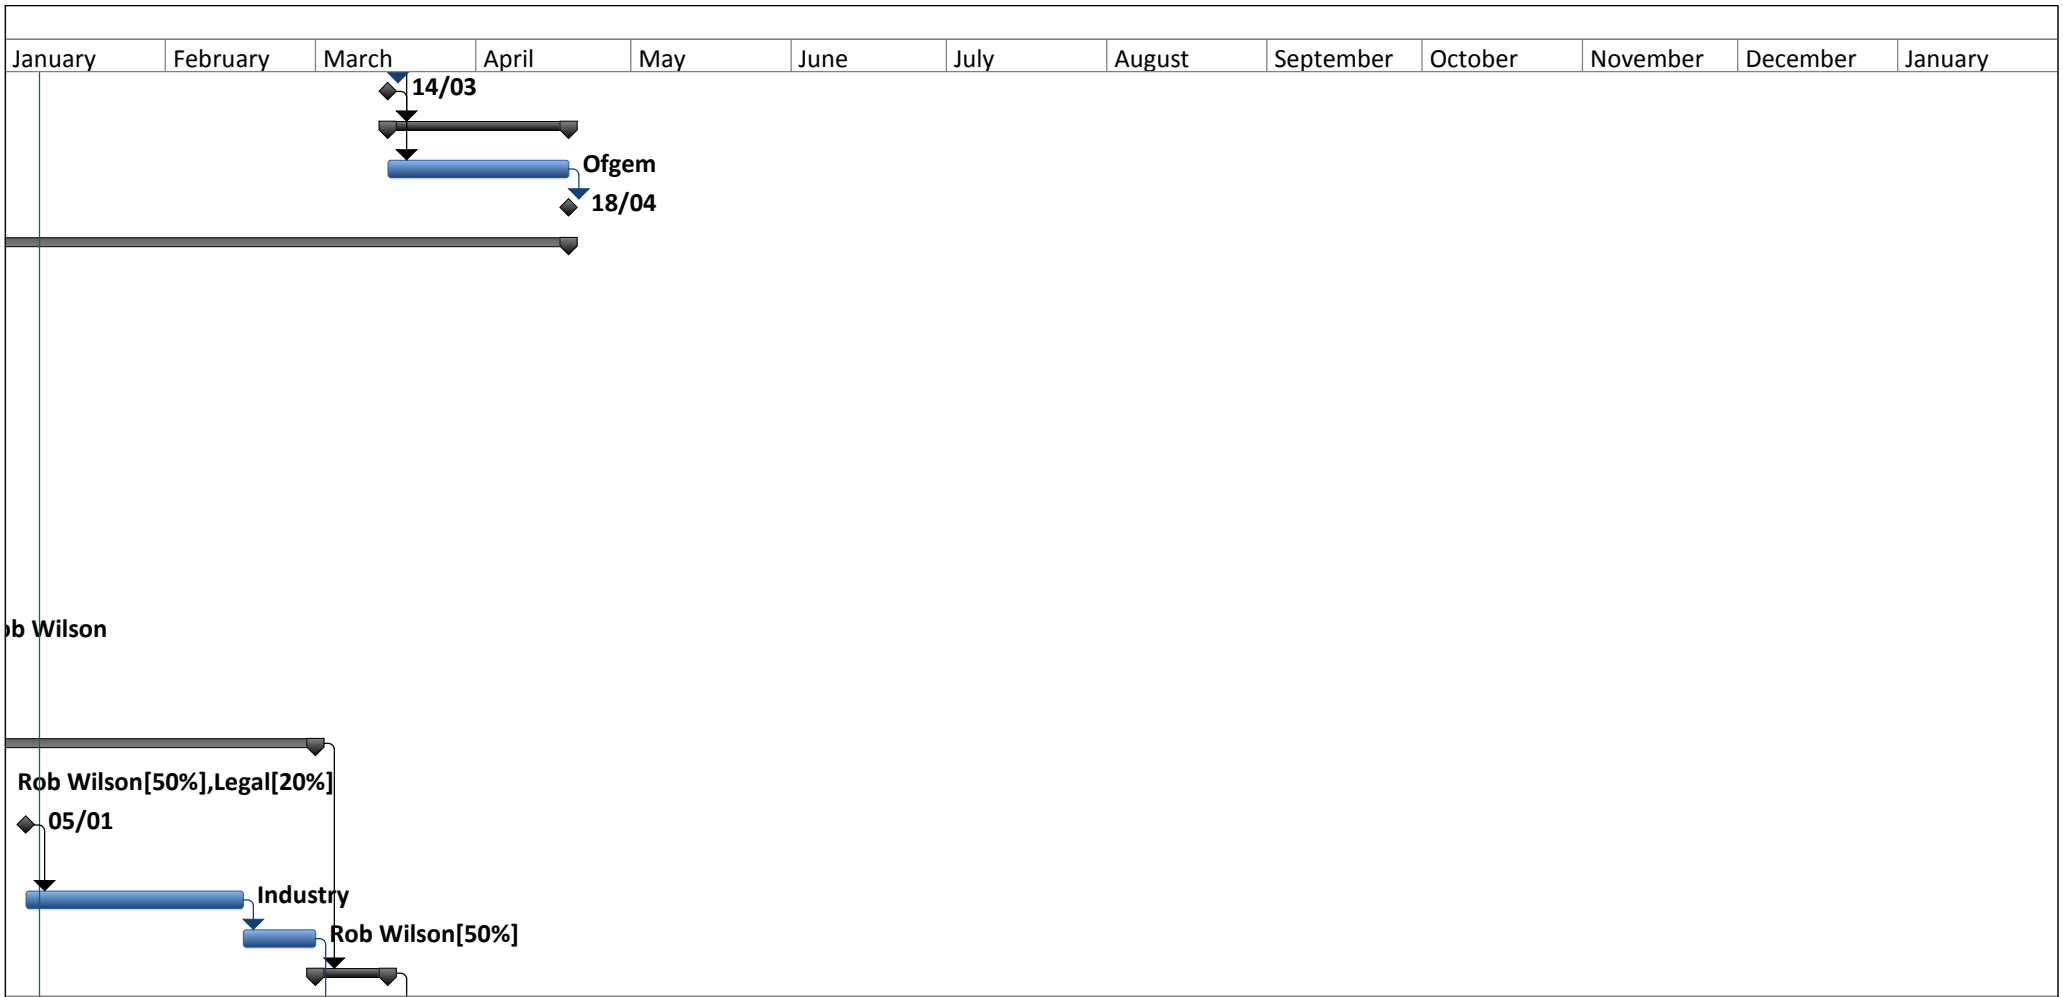


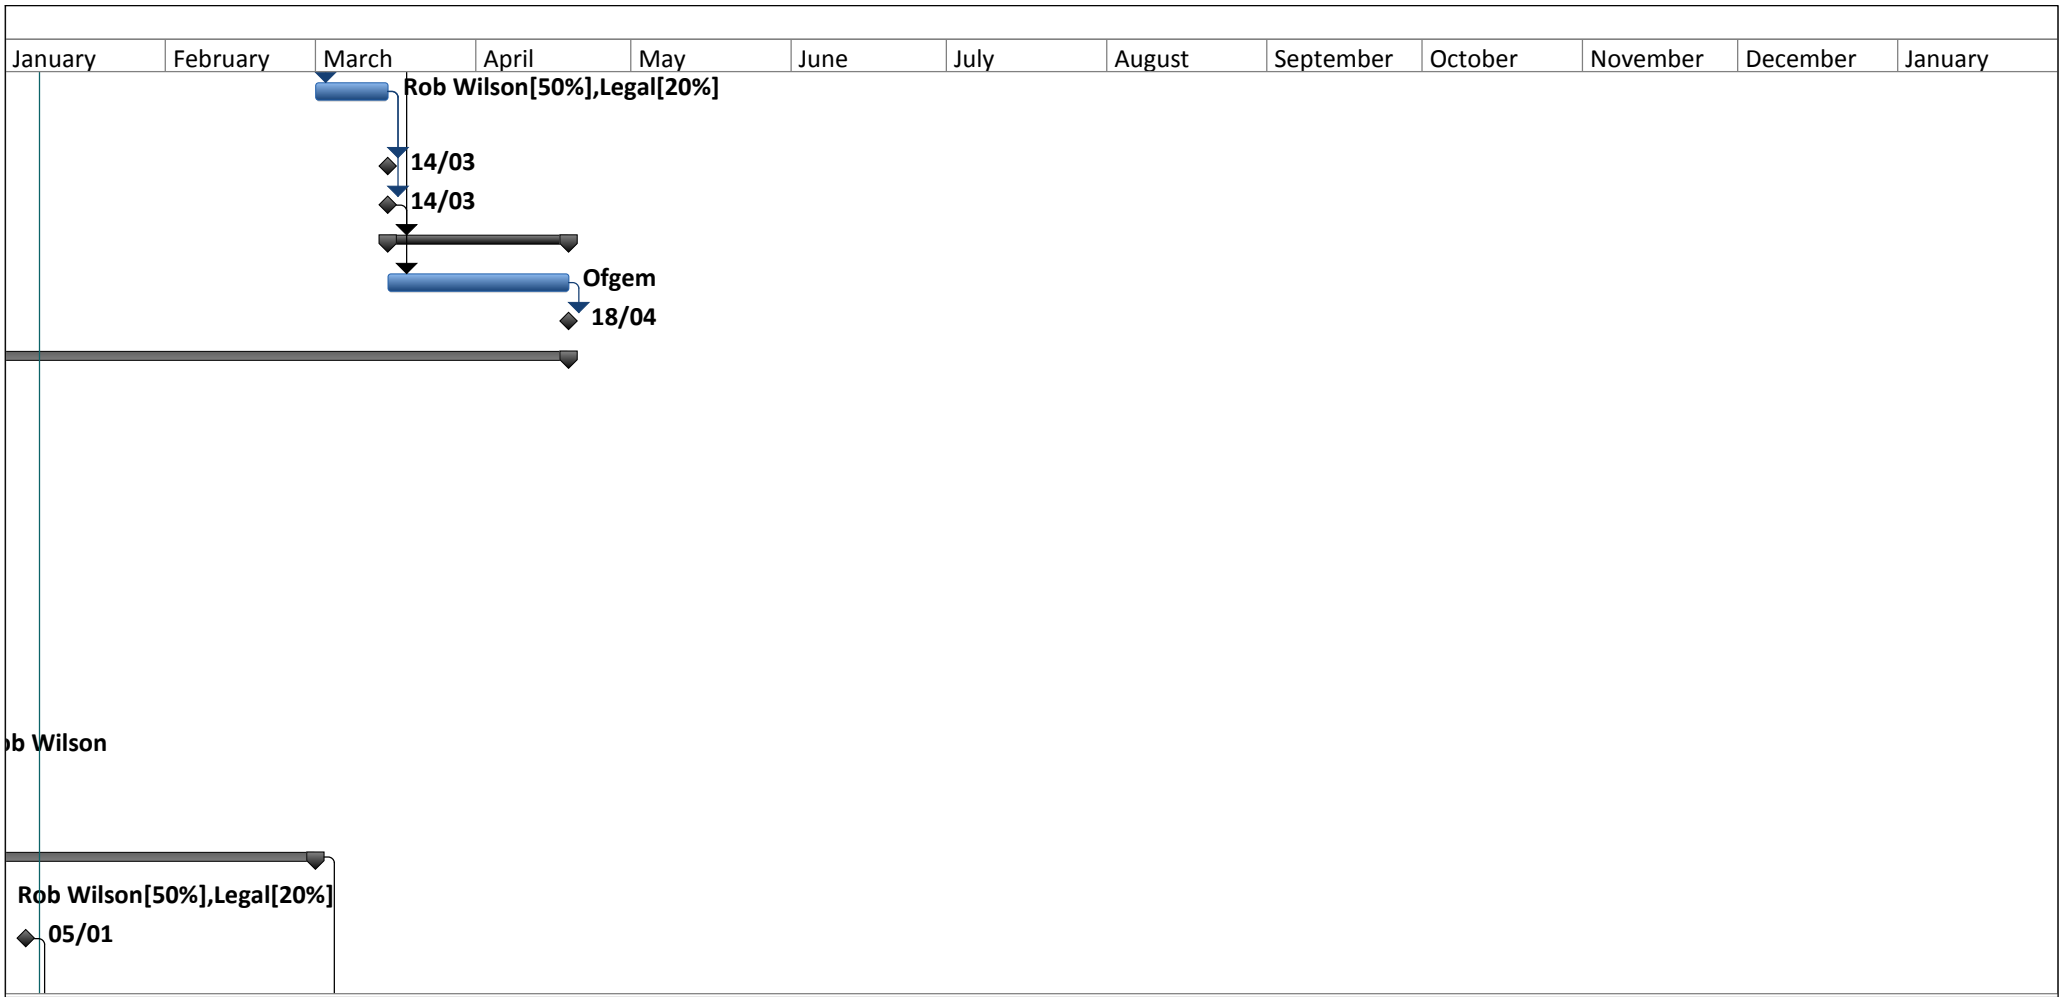


Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

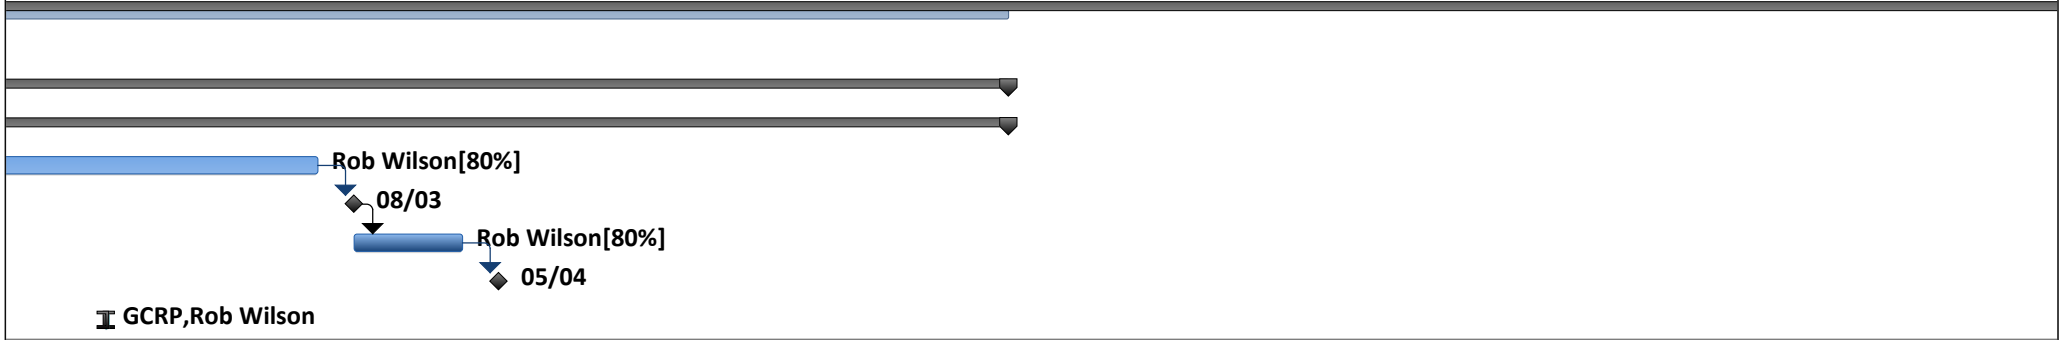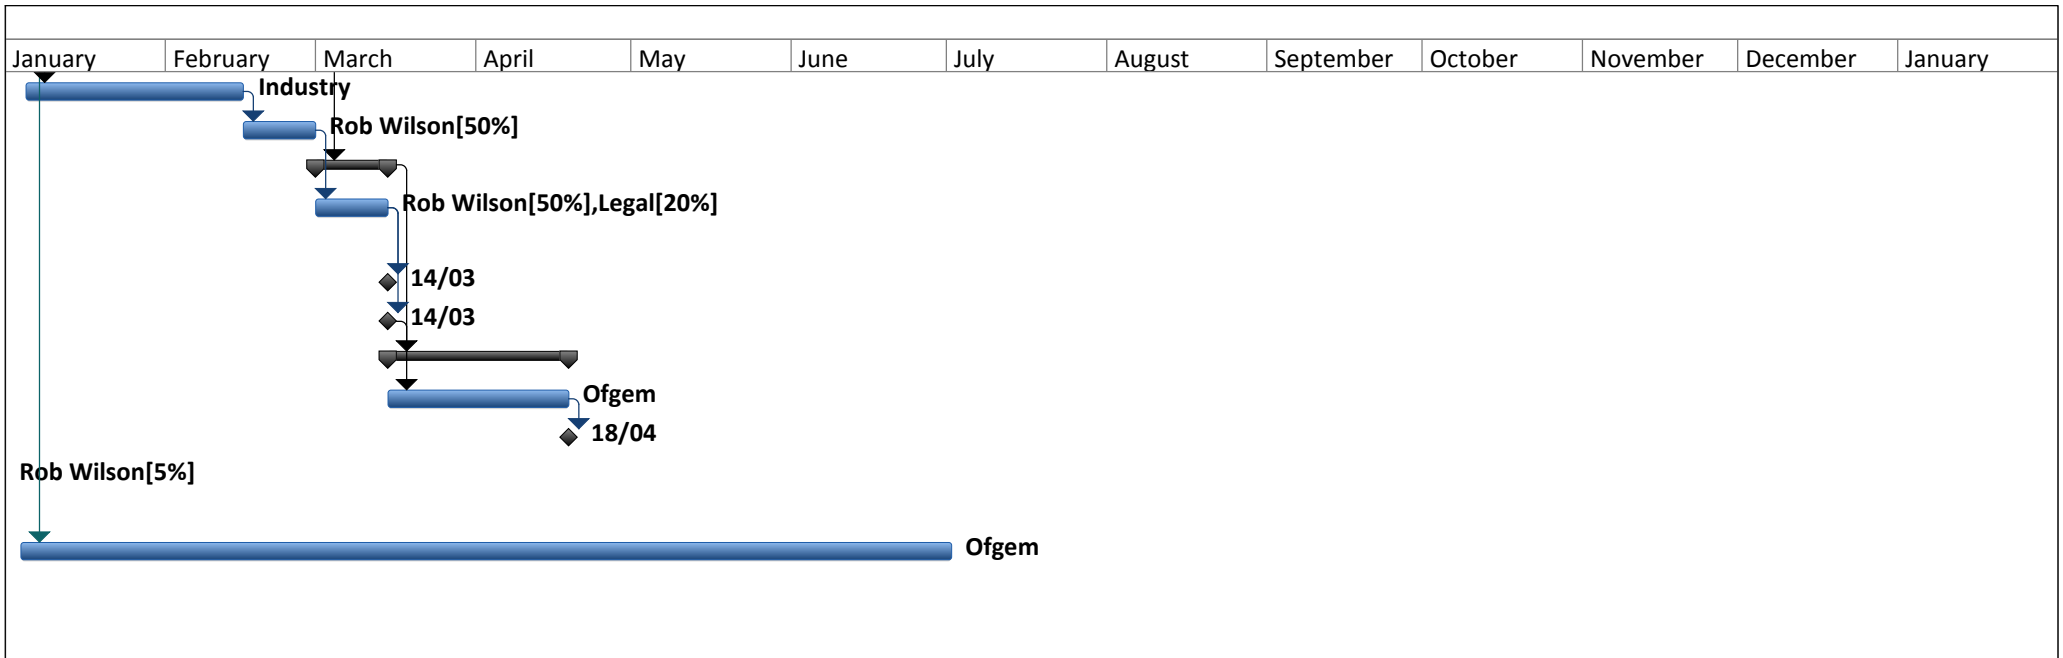

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

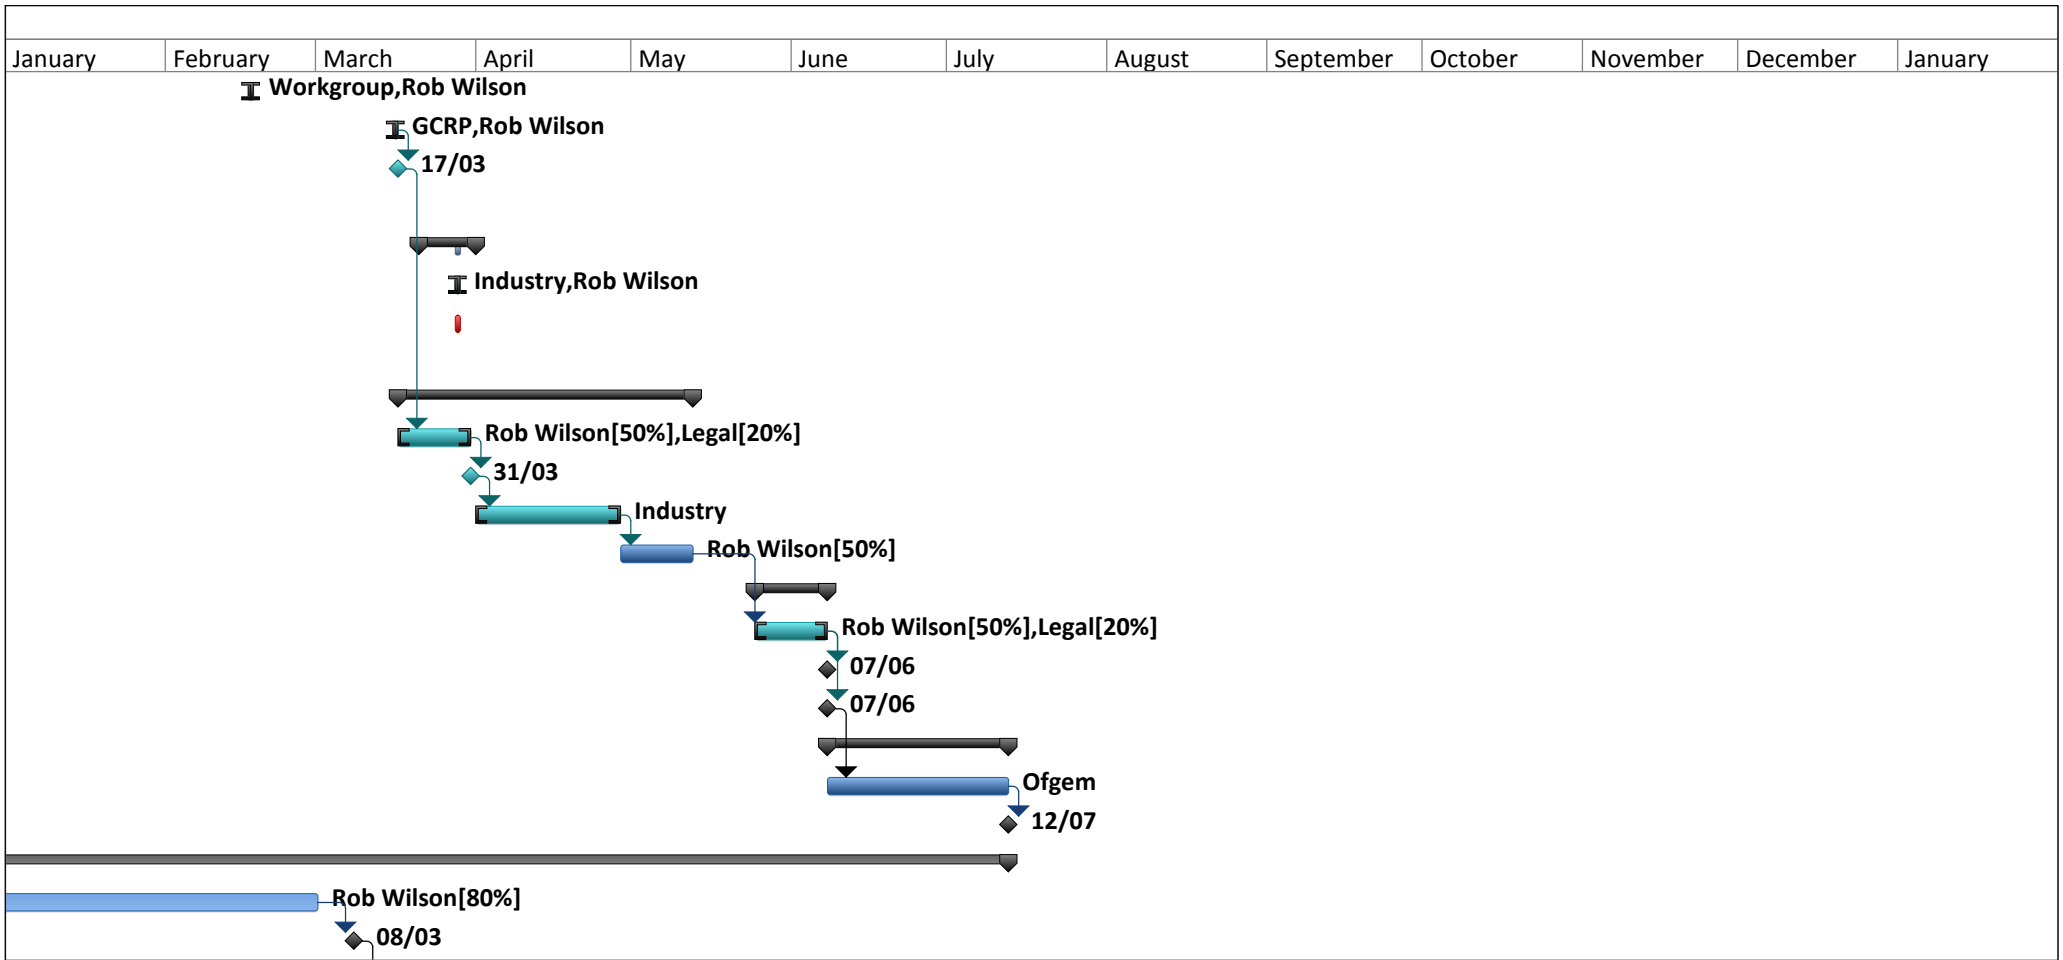


Project: RfG
Date: Mon 11/05/15

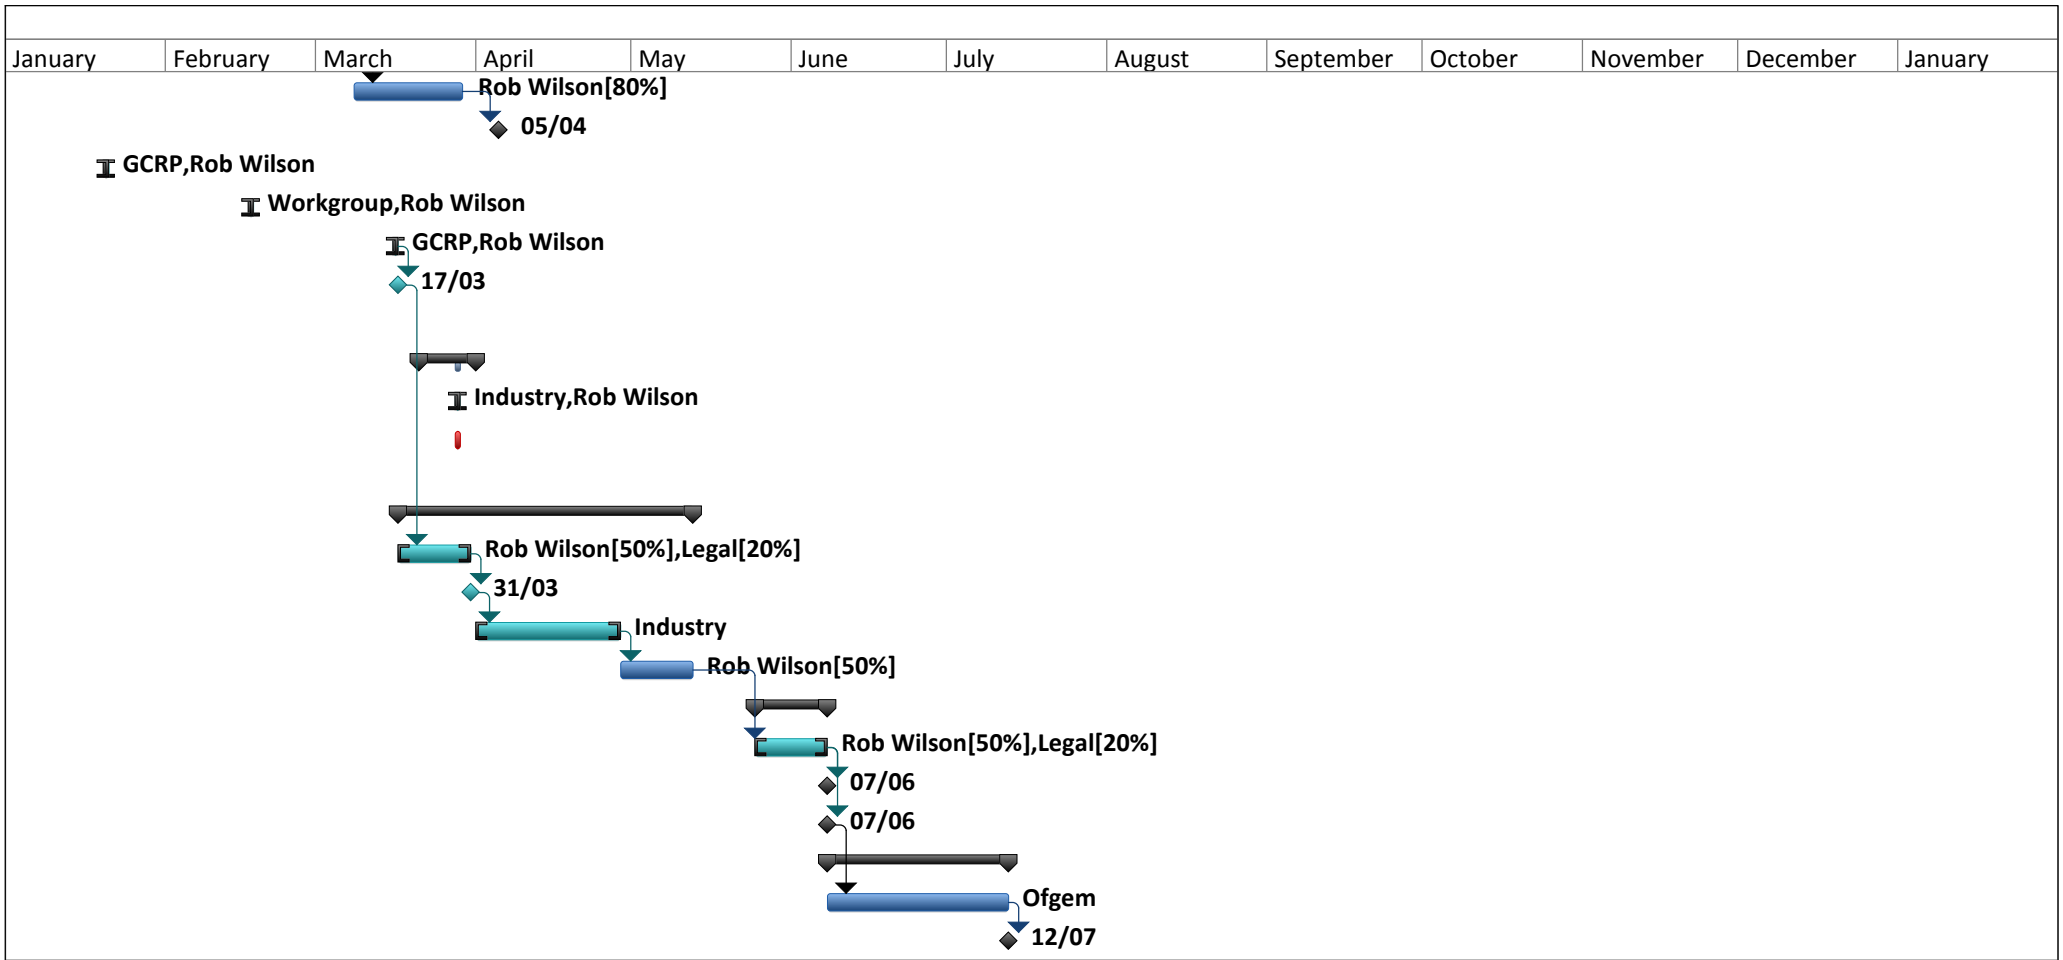


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

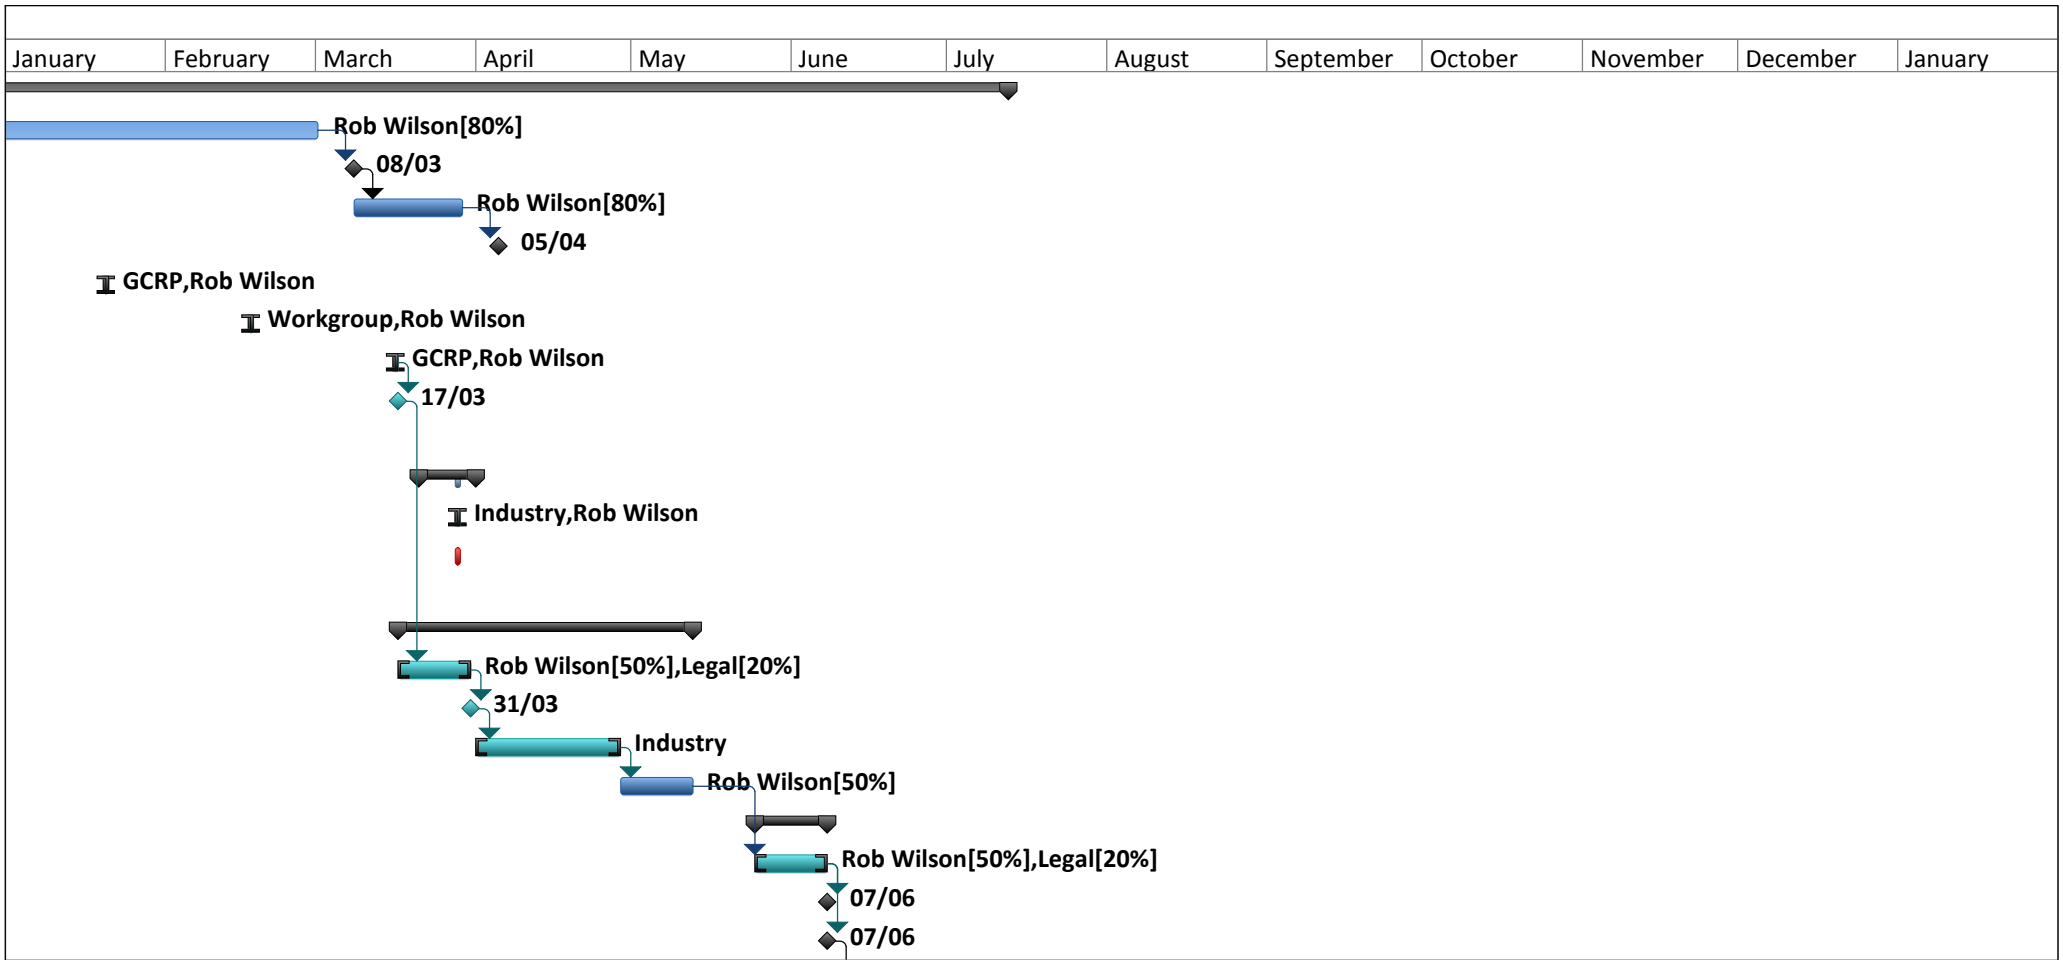


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

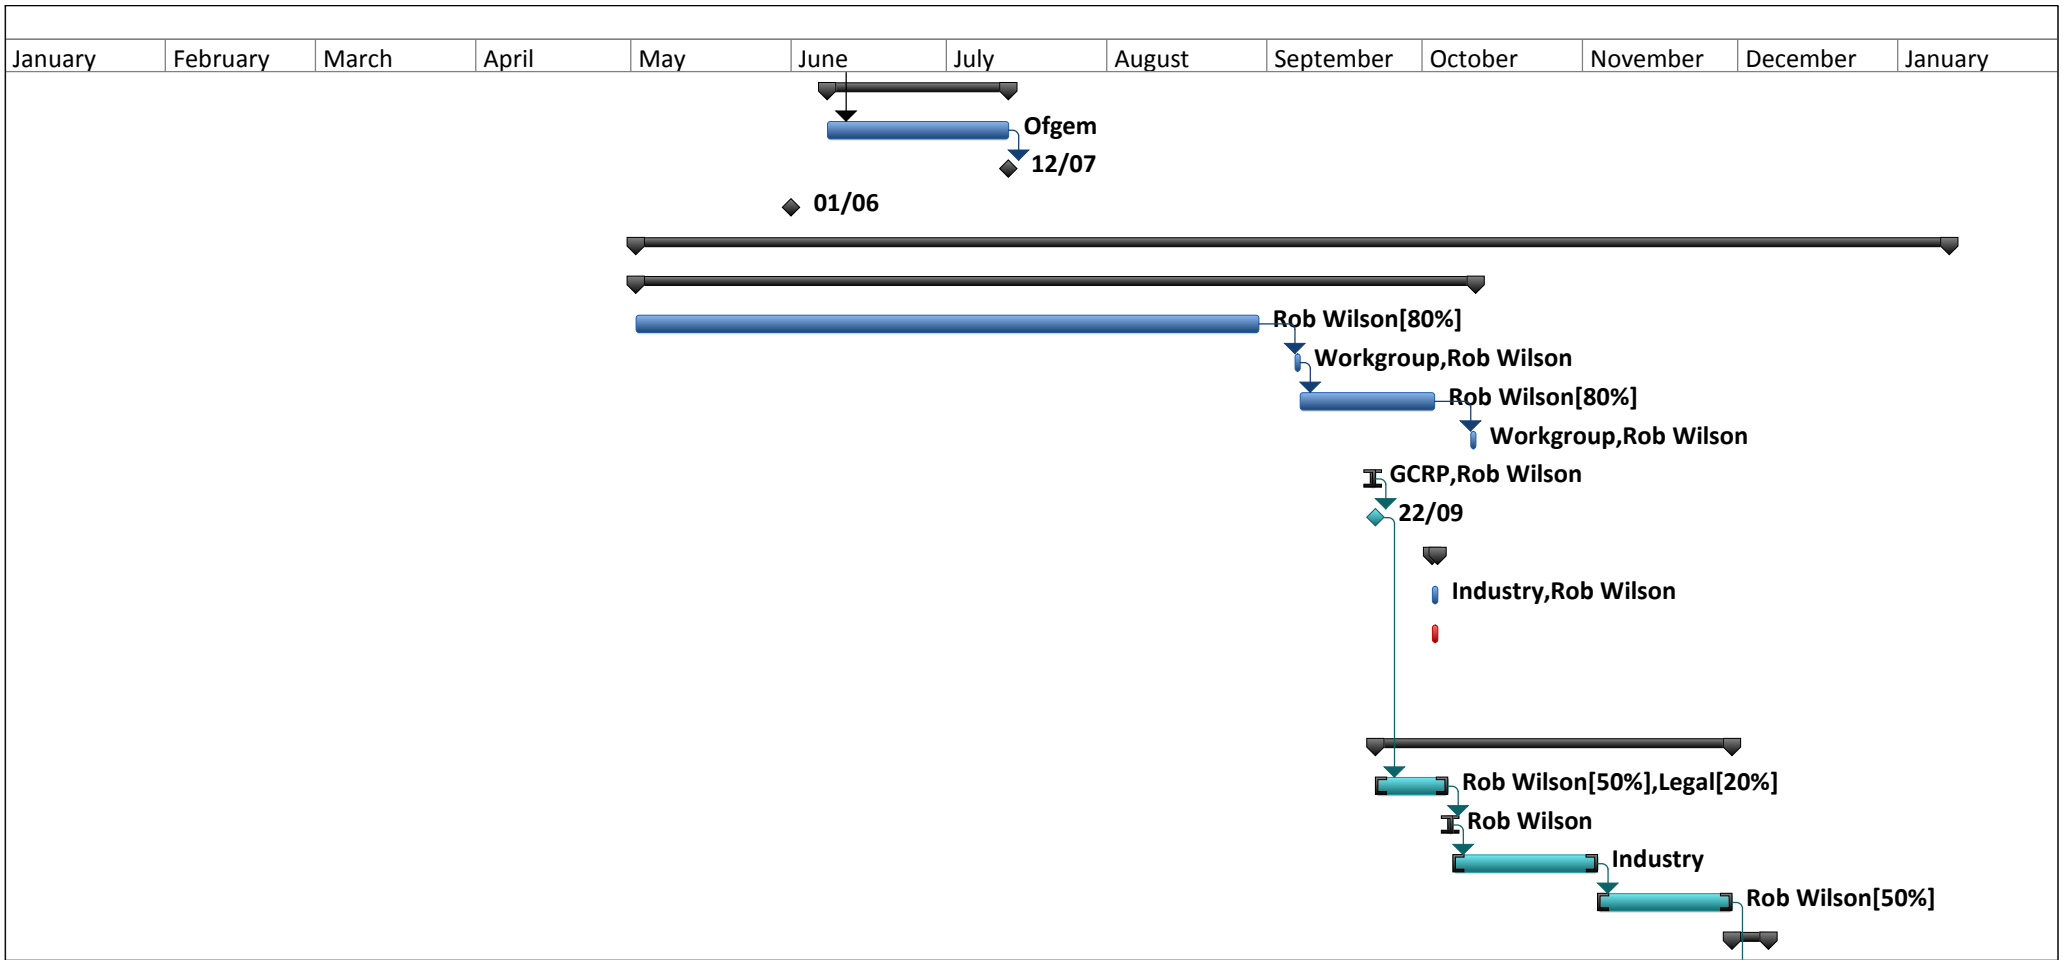


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

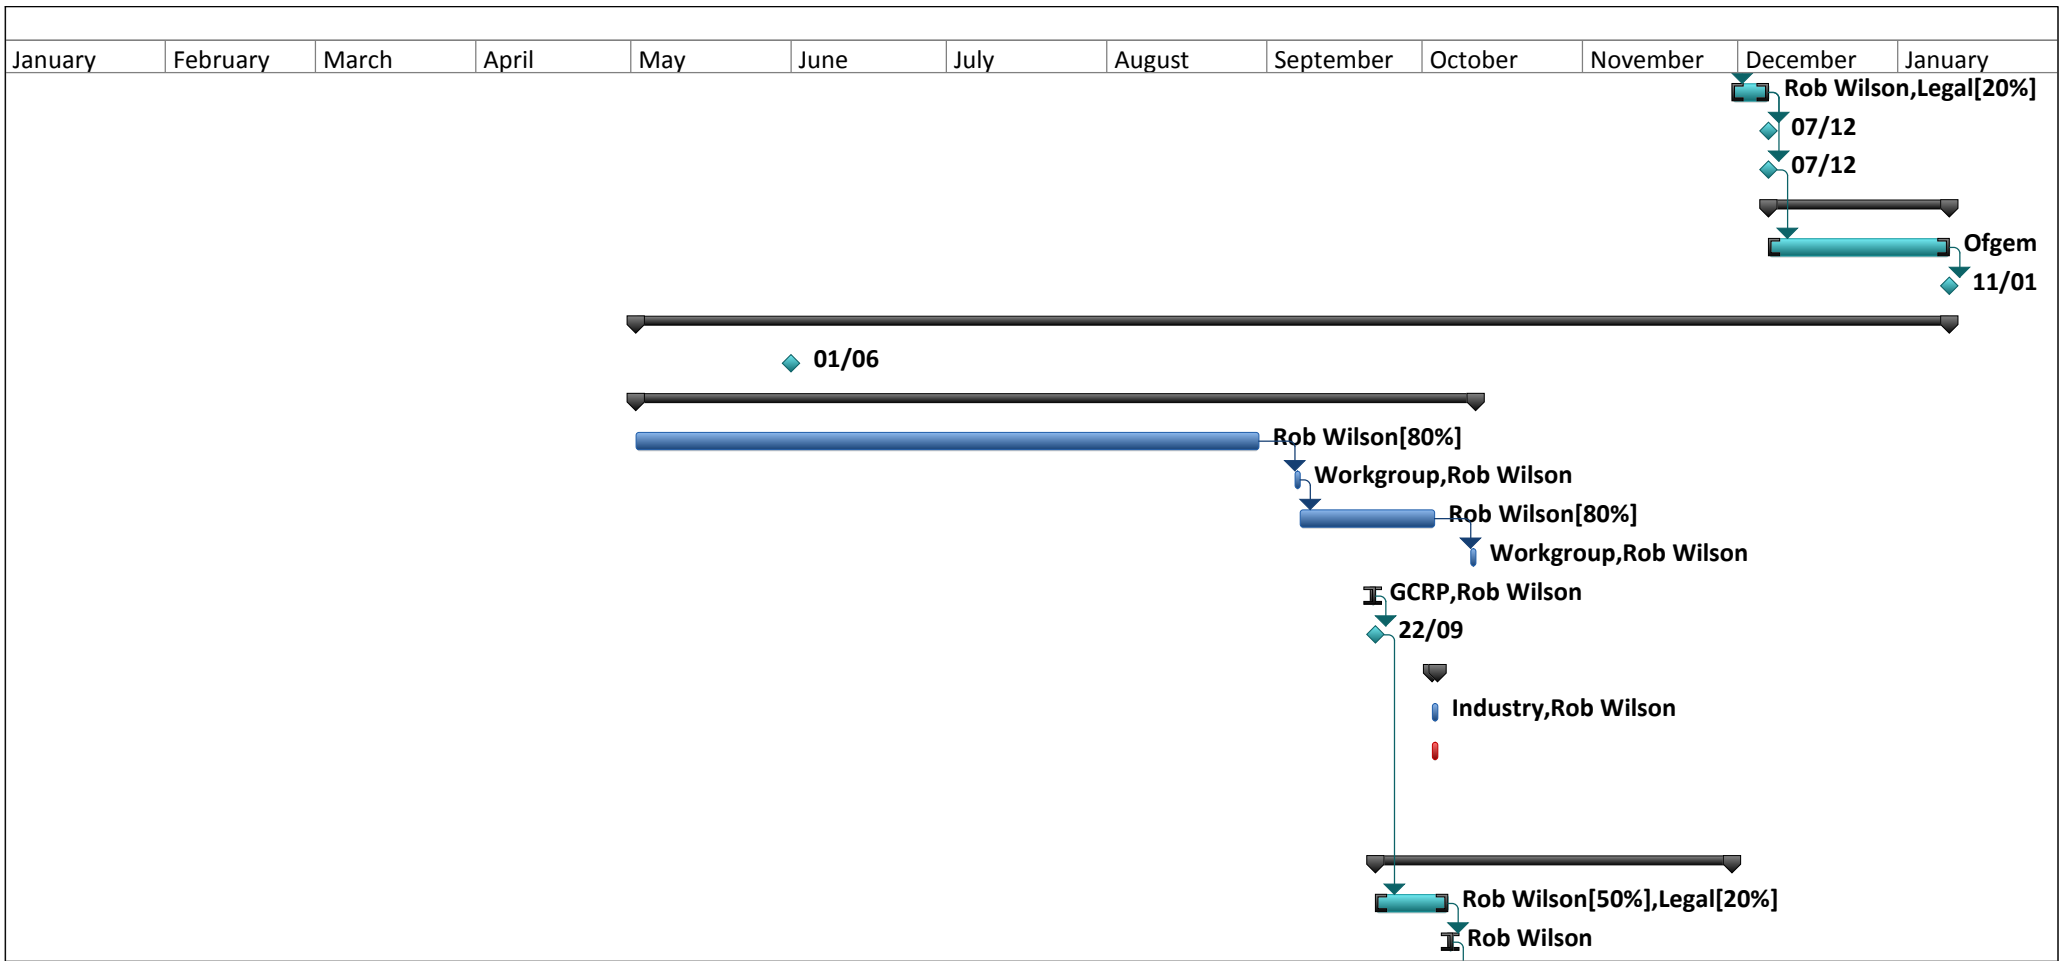


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

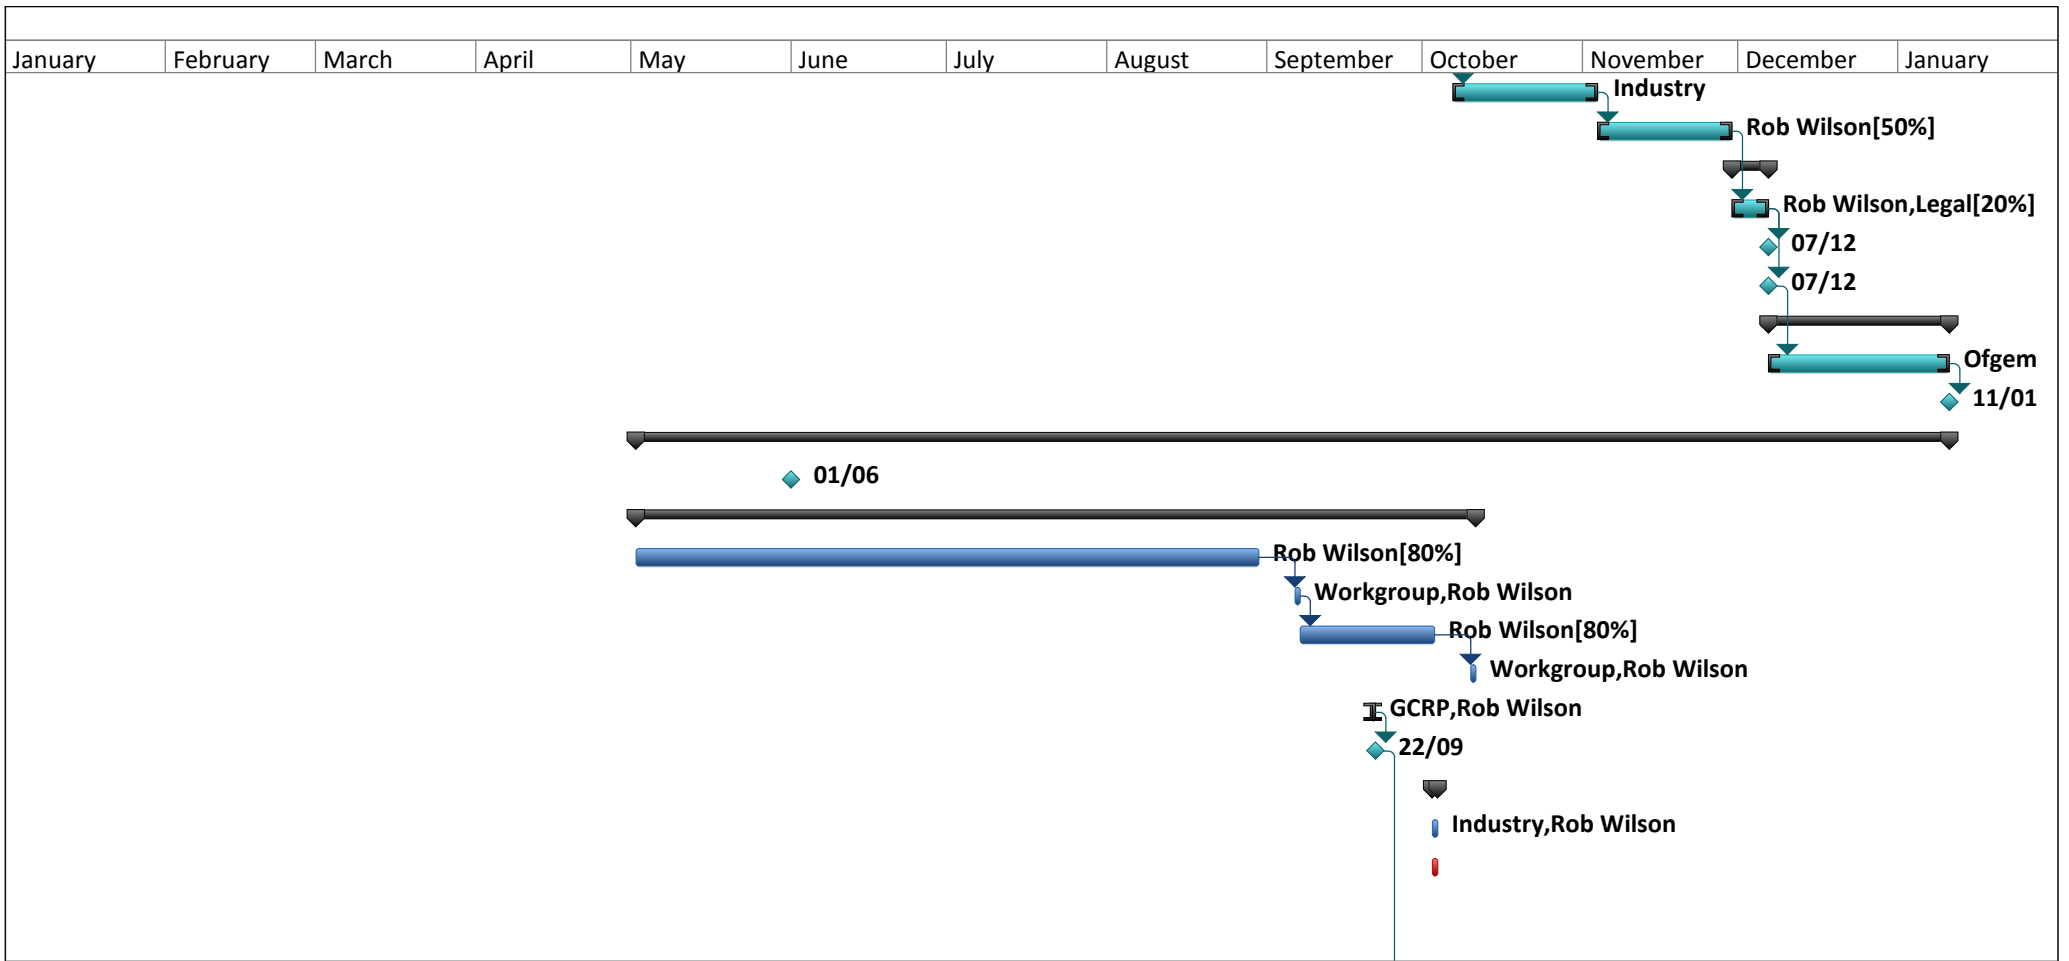



Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

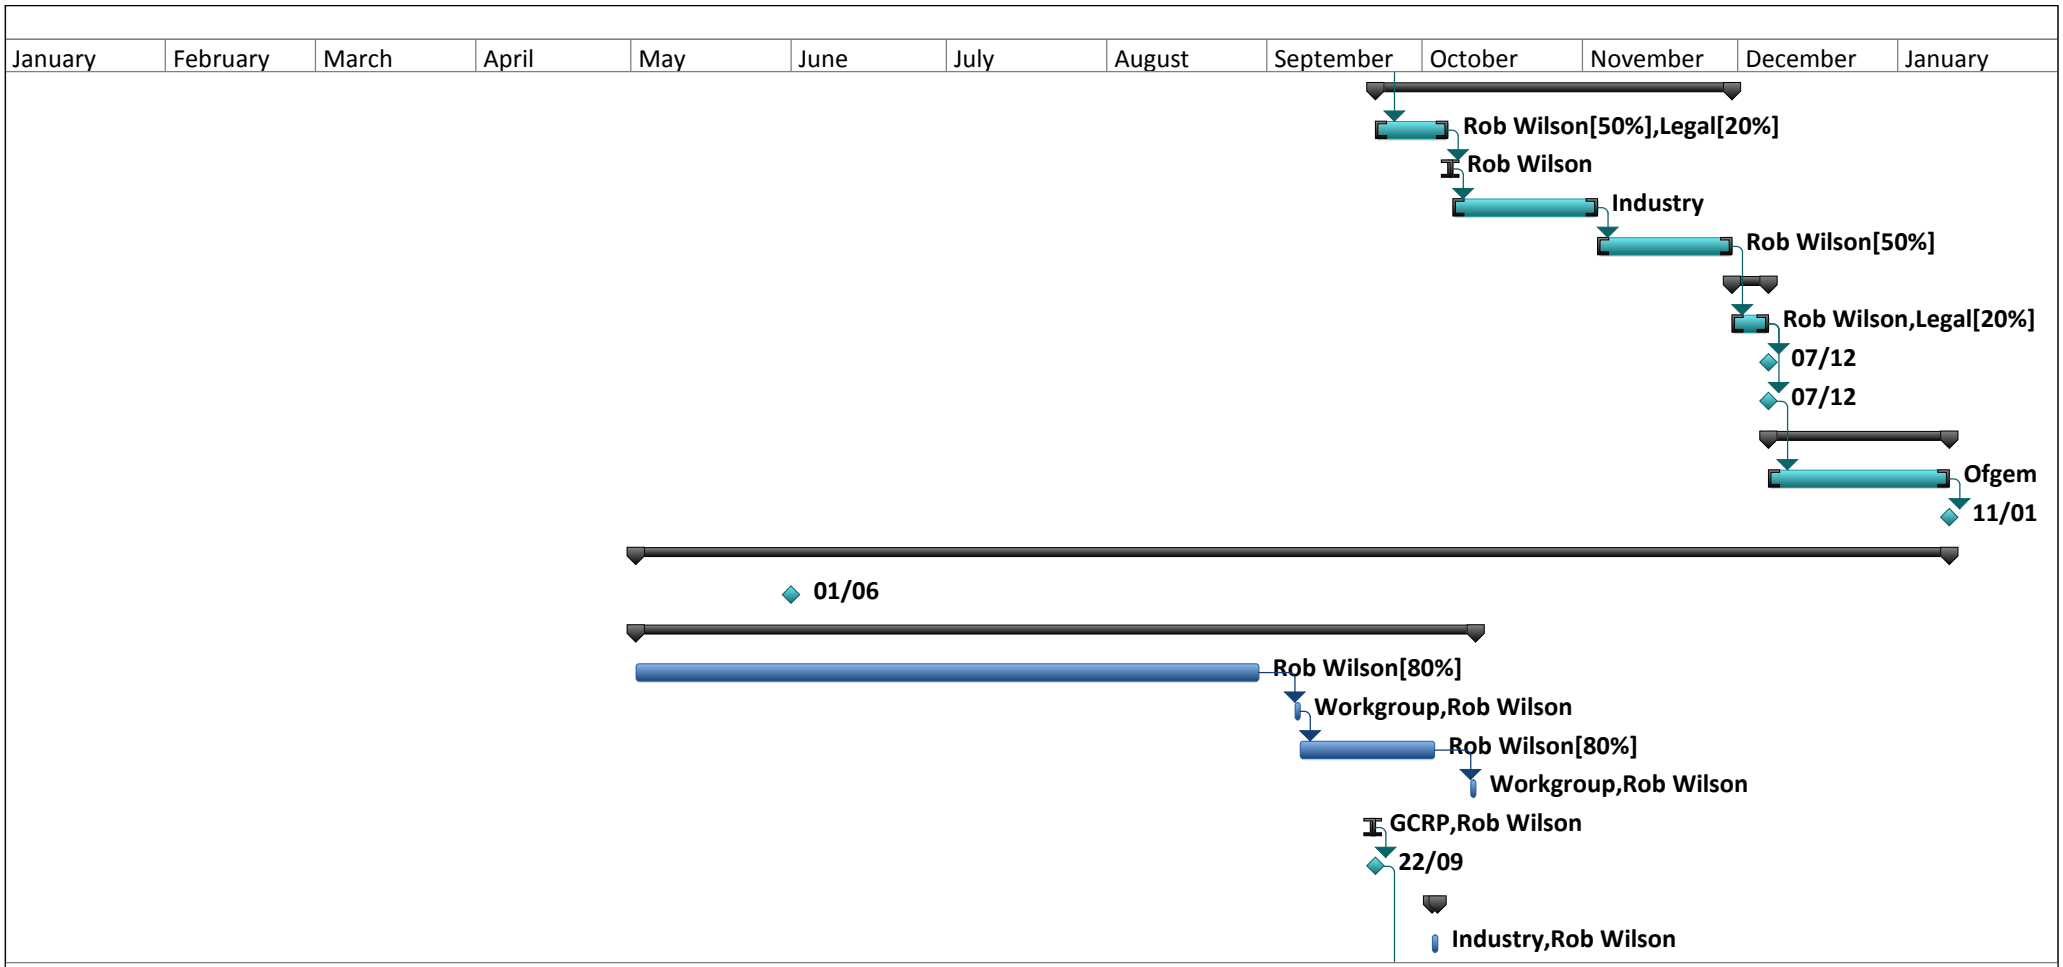


Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

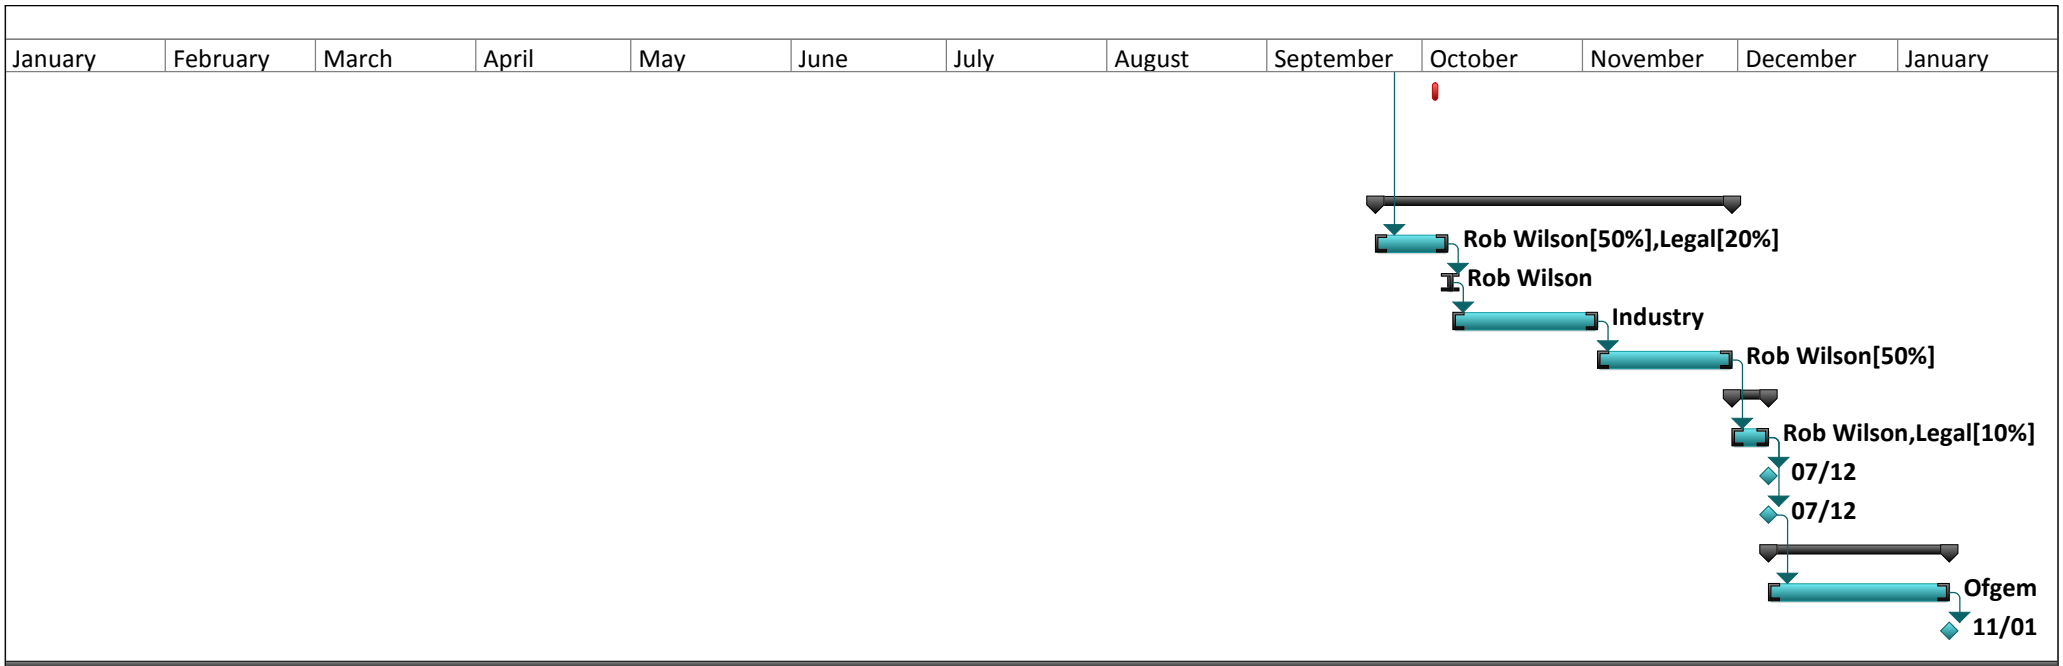

Project: RfG
Date: Mon 11/05/15


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

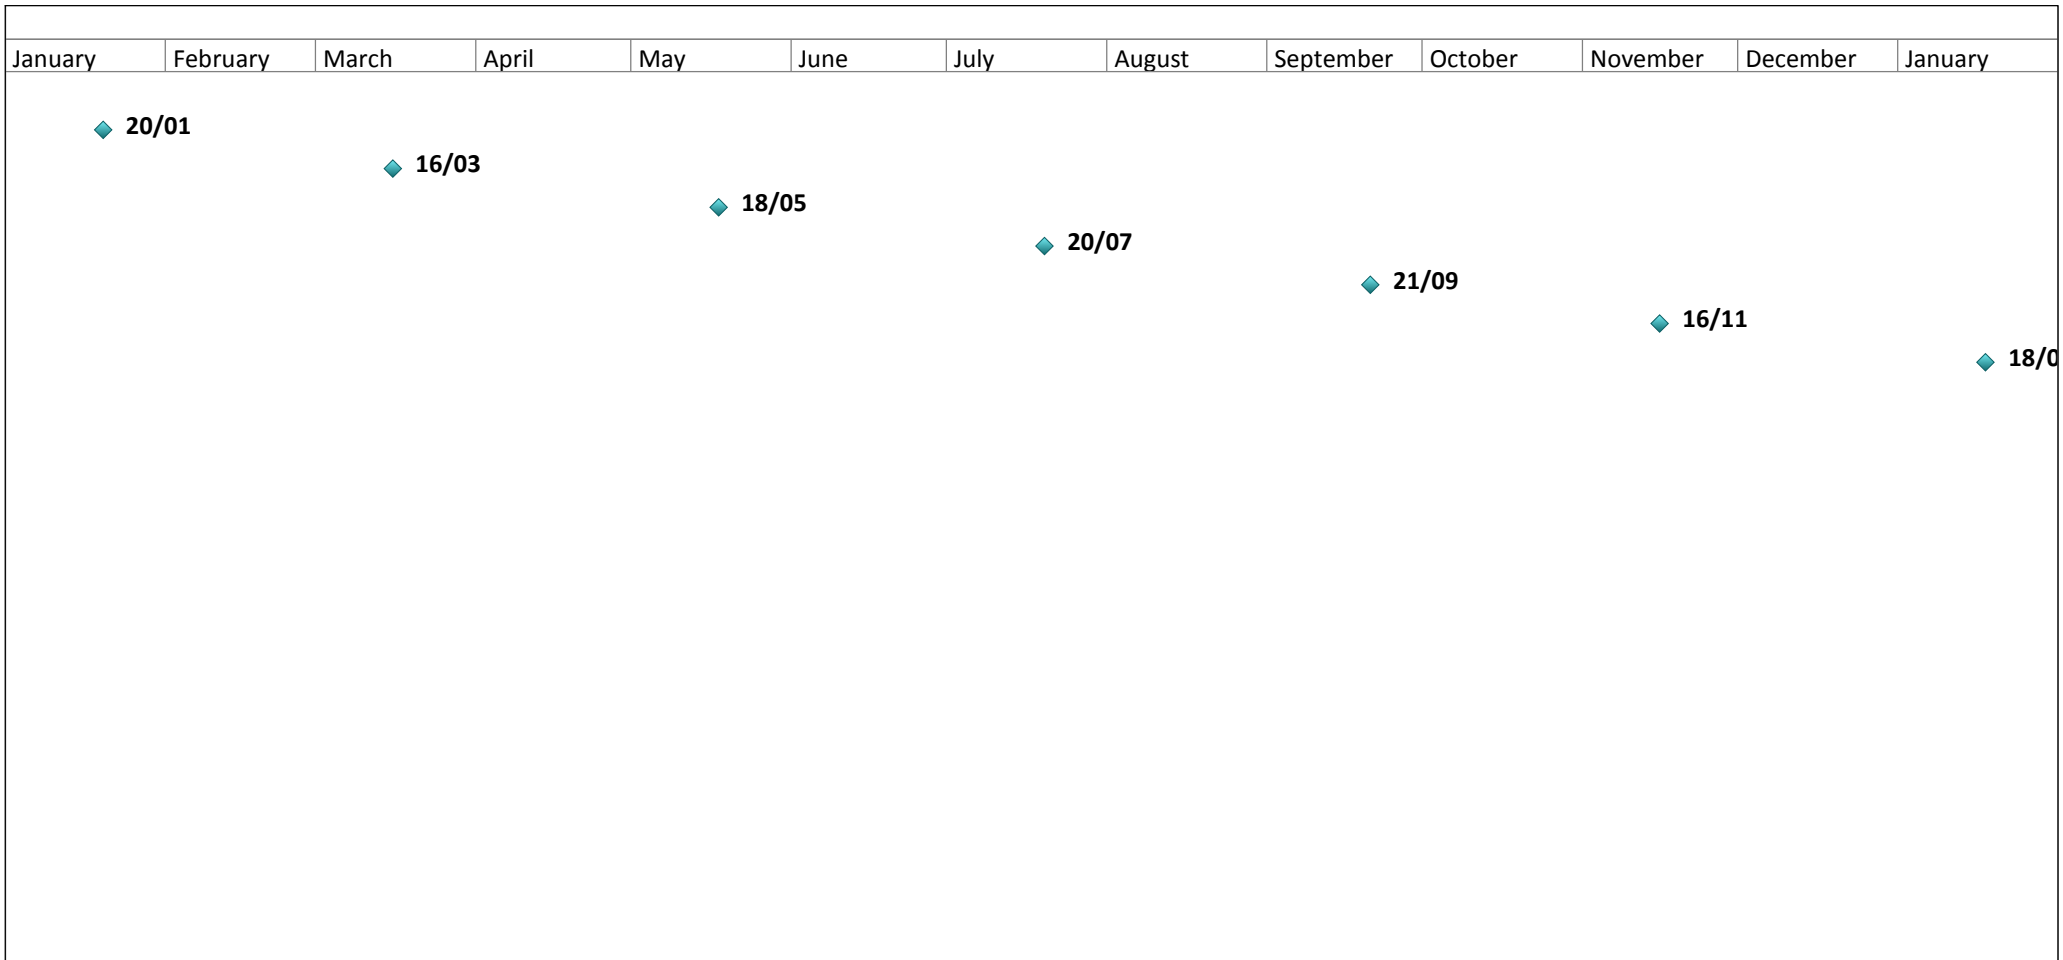

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





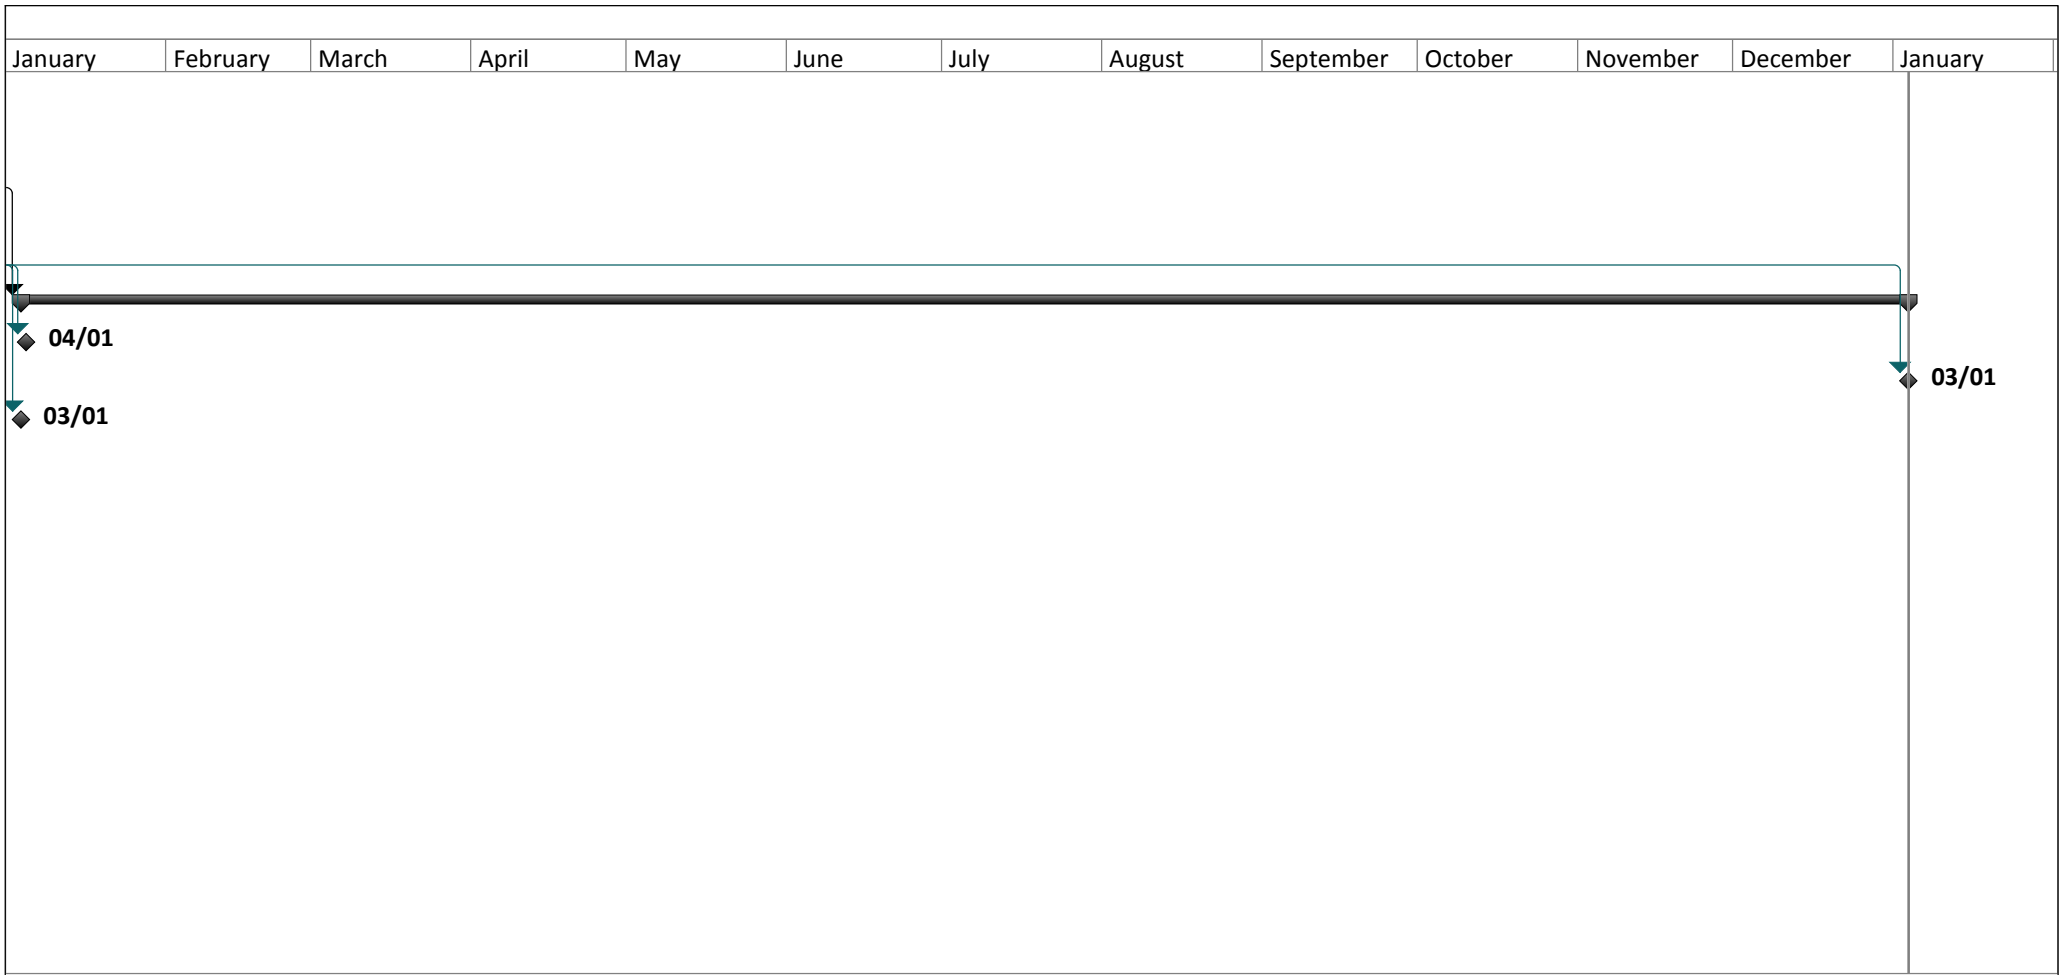

















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary				





















January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			























Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			























Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			























Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

January	February	March	April	May	June	July	August	September	October	November	December	January

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



50%]

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			



Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			























Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			























Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			























Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			











































Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

Project: RfG
Date: Mon 11/05/15





















Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			





















Project: RfG
Date: Mon 11/05/15





















Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			





















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















Project: RfG
Date: Mon 11/05/15





















Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			





















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			





















Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			




















Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			

Project: RfG
Date: Mon 11/05/15

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary			

Project: RfG Date: Mon 11/05/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary	
